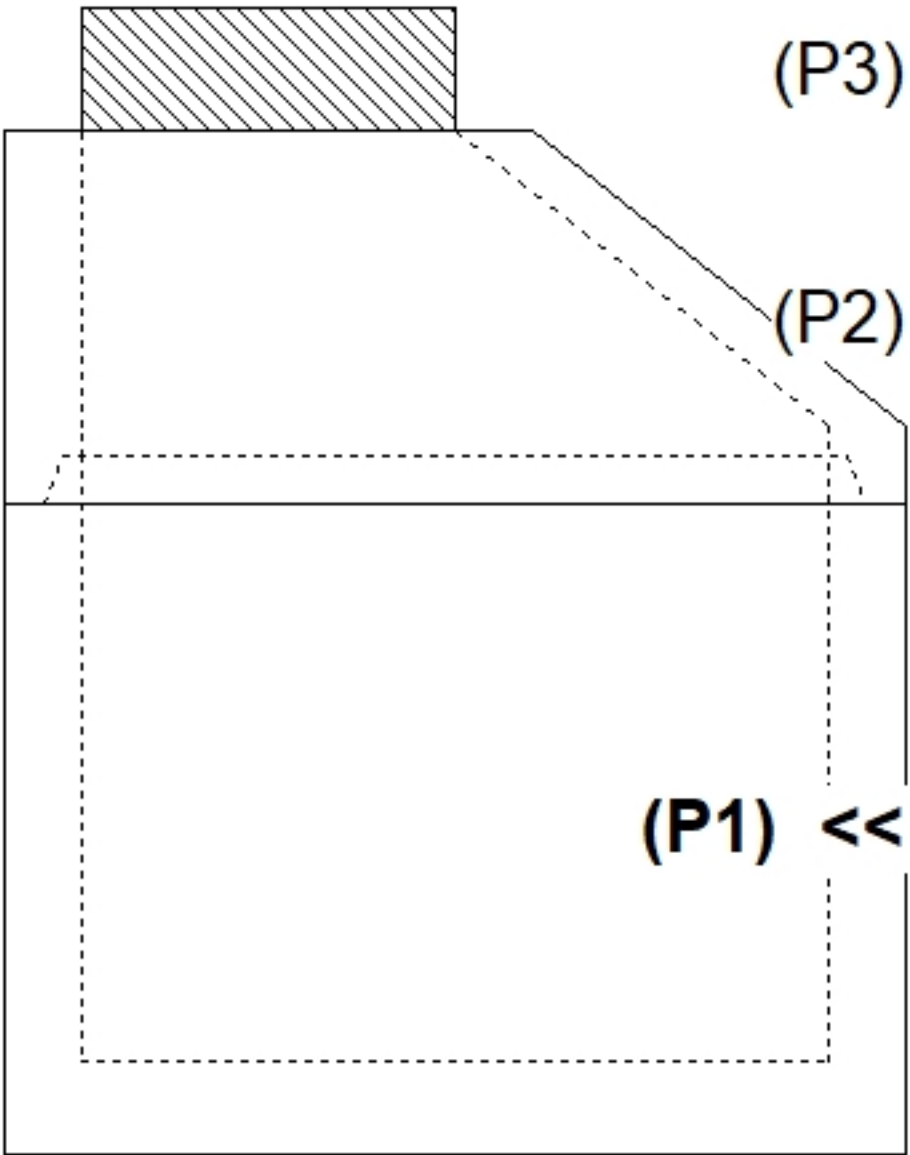
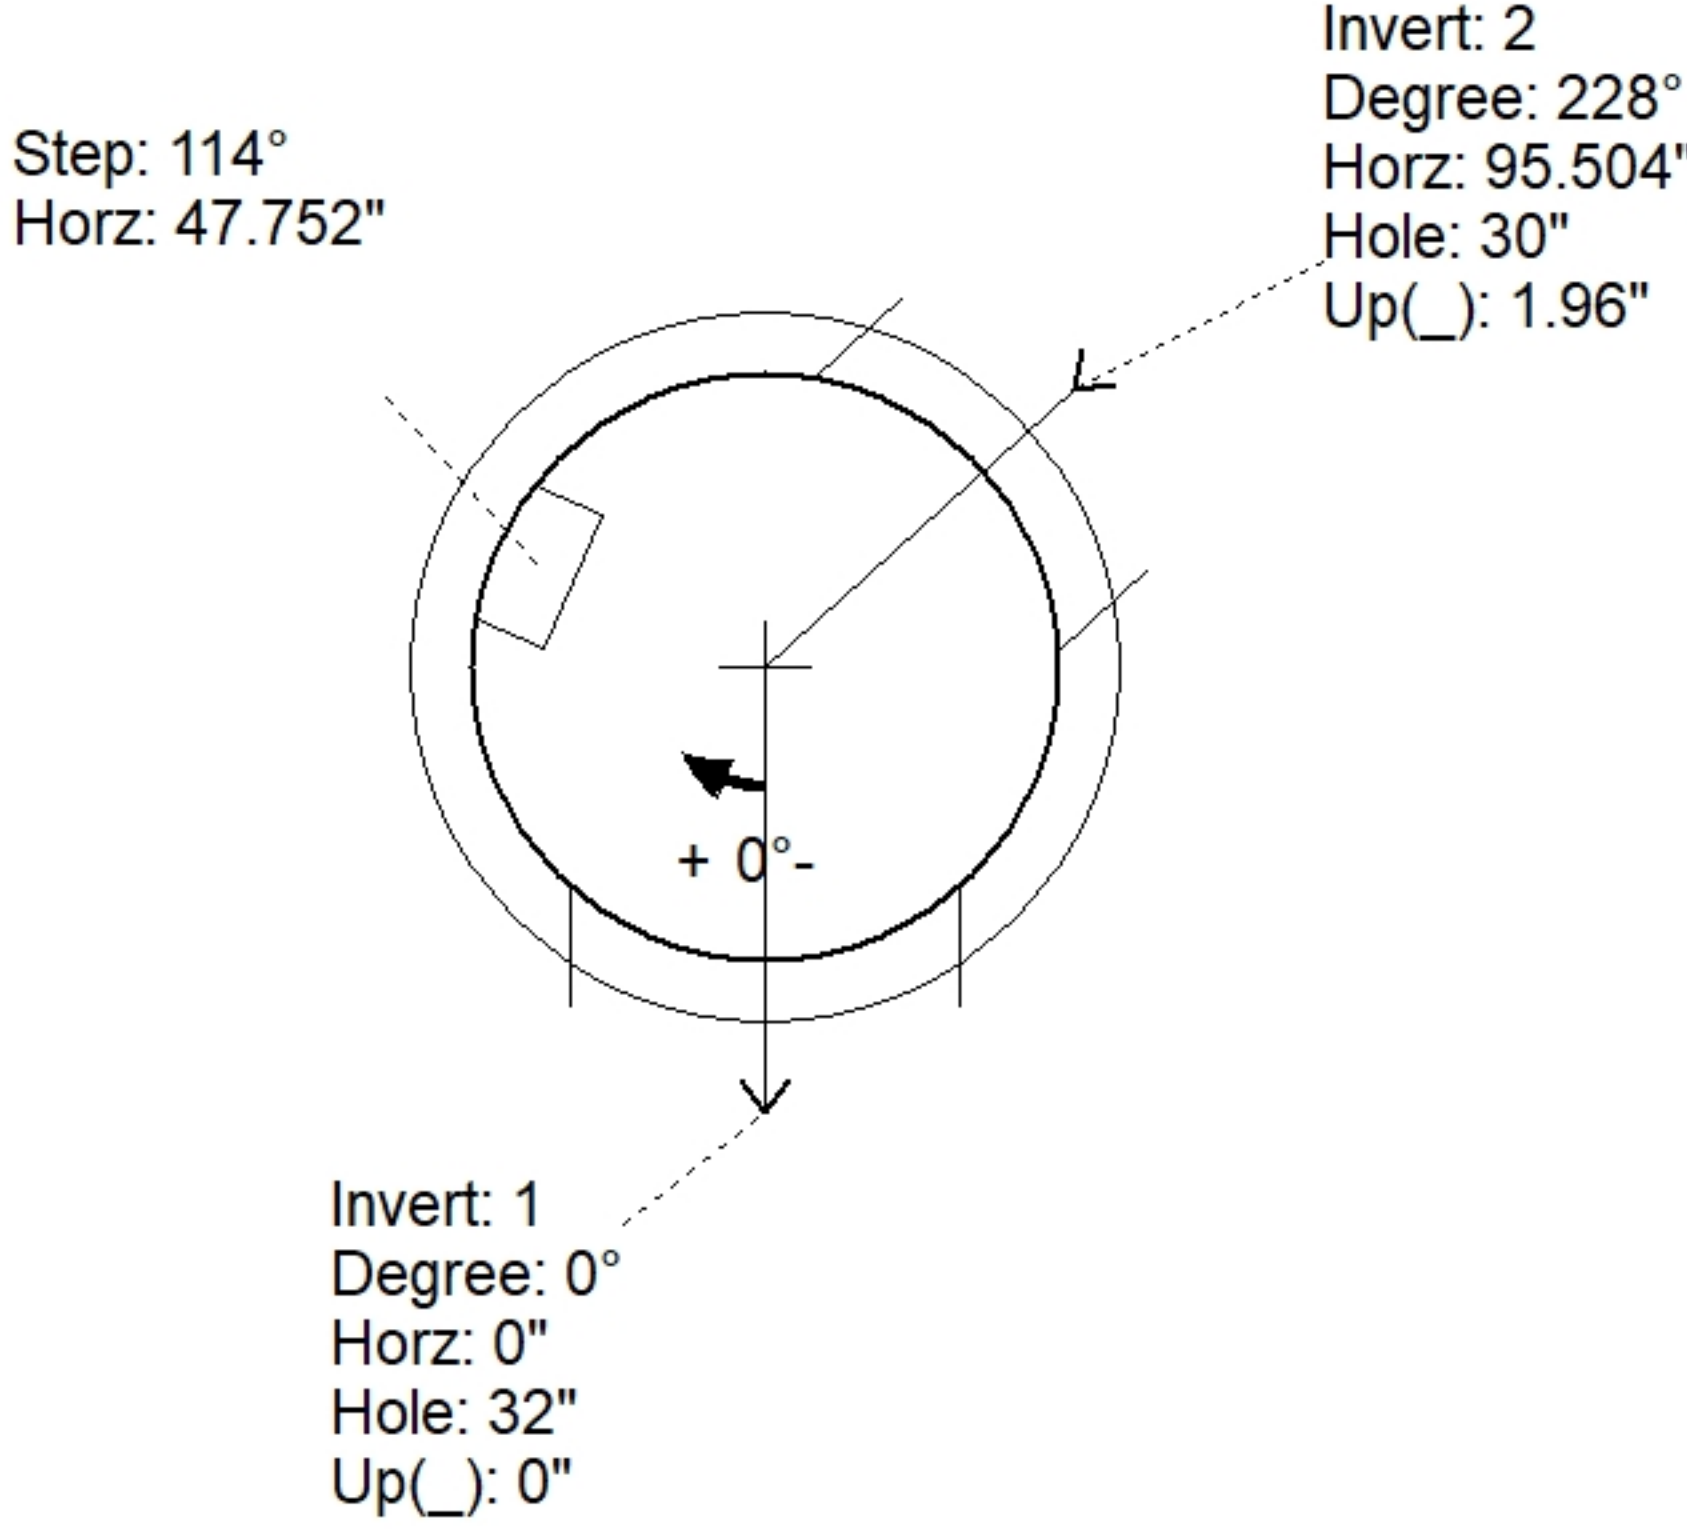
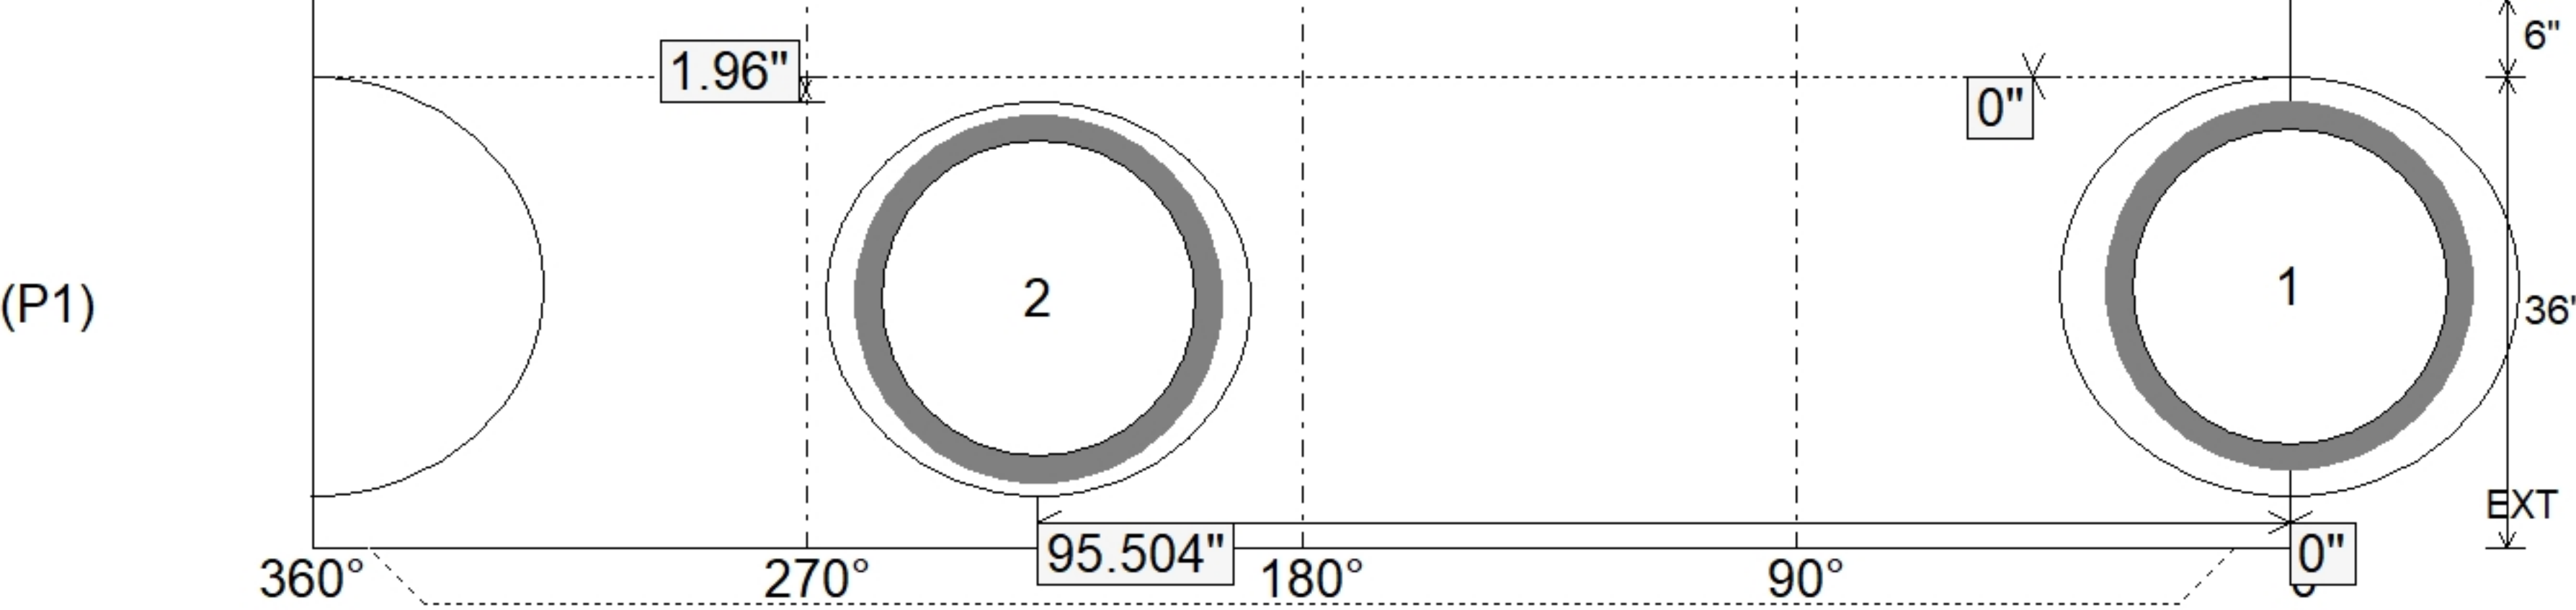
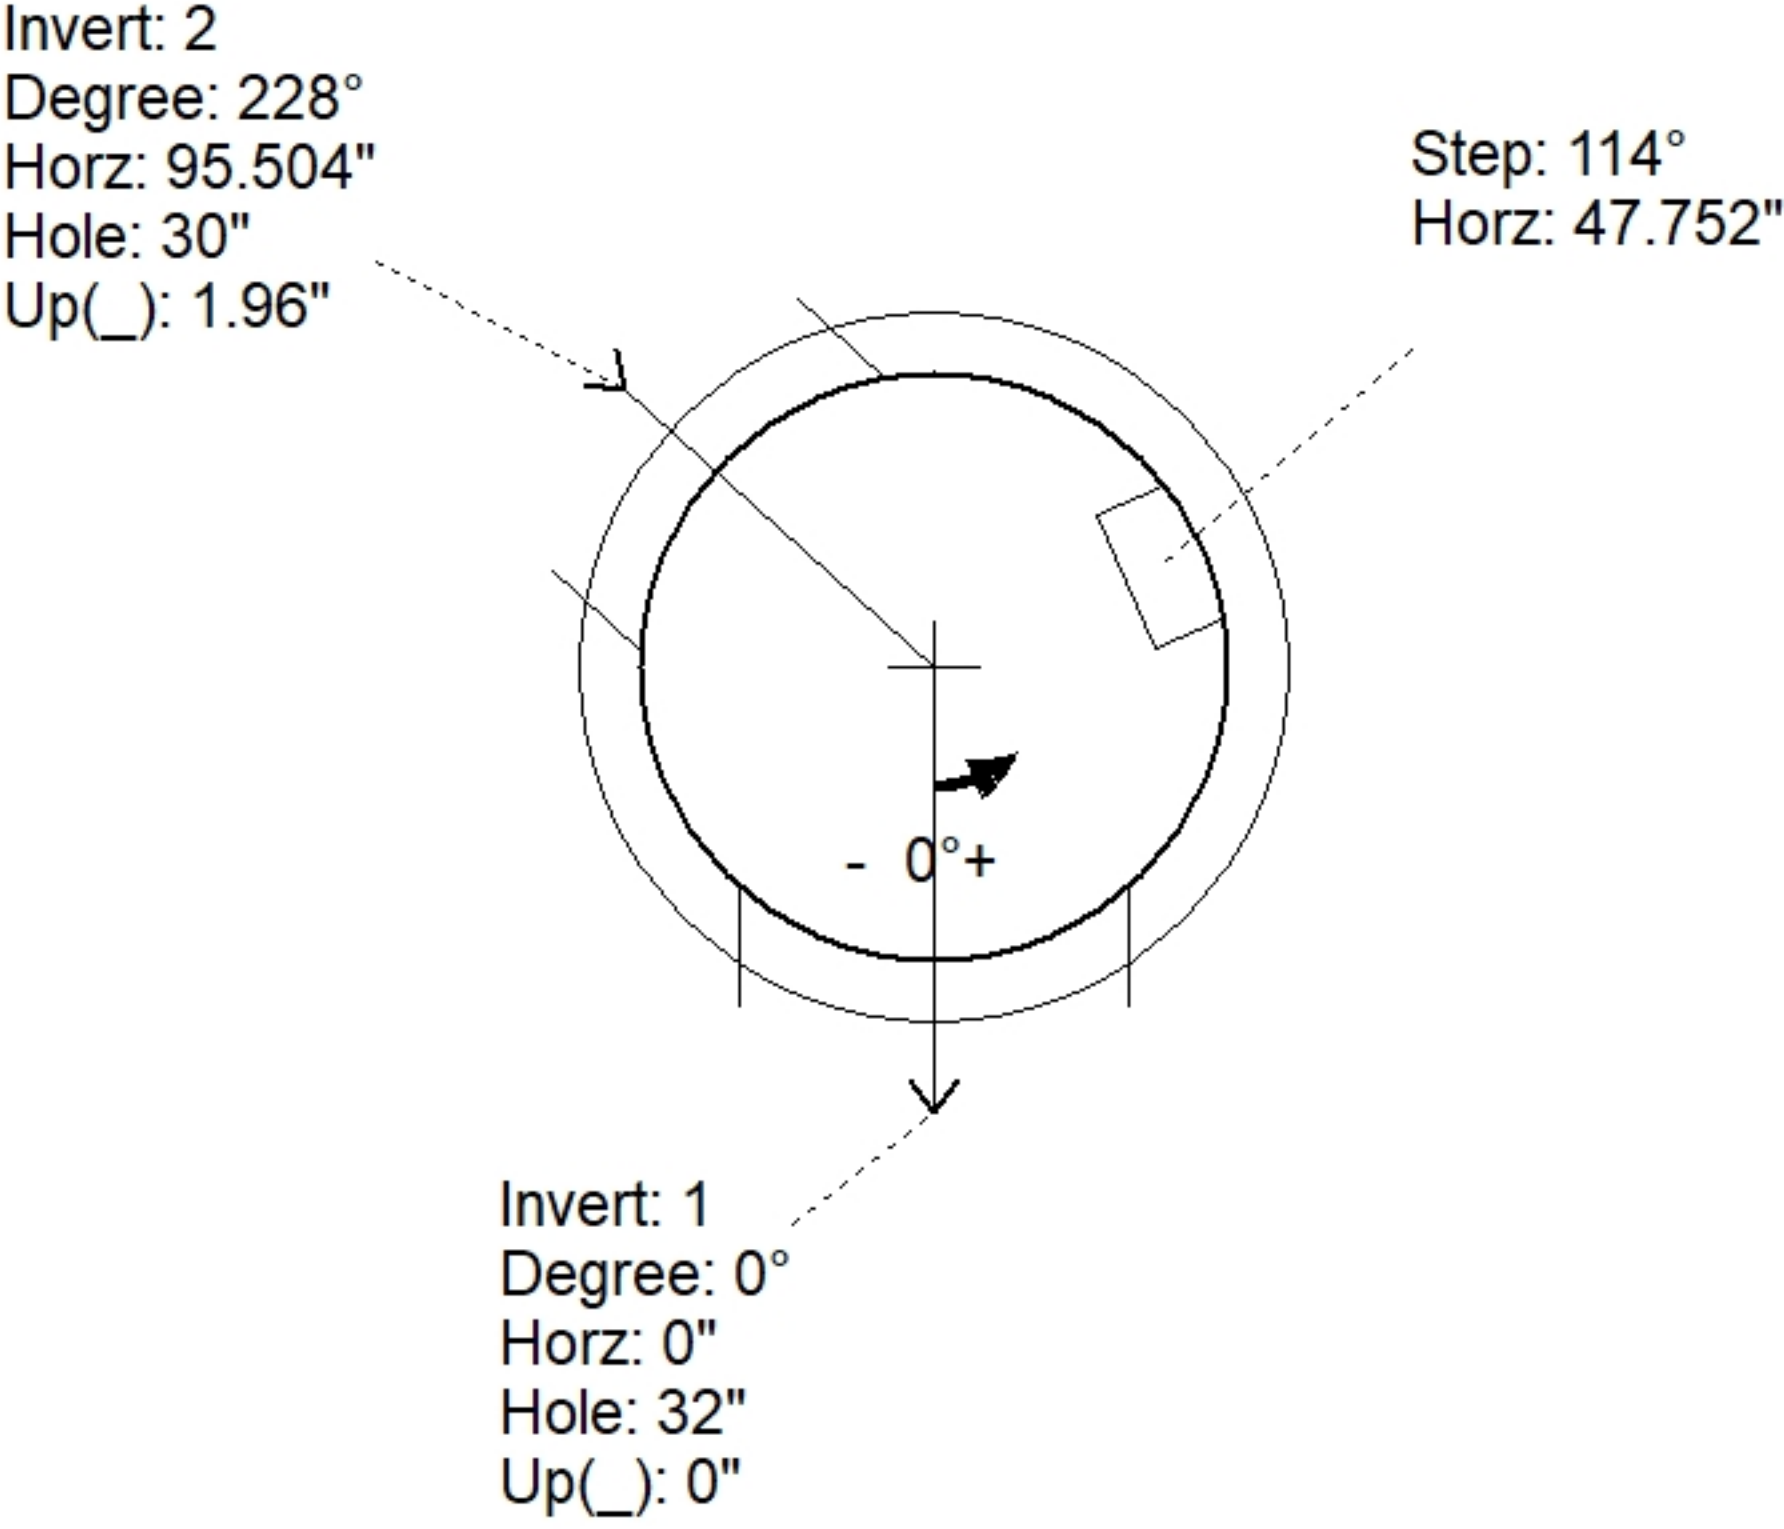


Job Name: 26-2648 Midtown Commons Apartments Job Location: Madisonville, KY Contractor: Steve Pleasant Excavating				Plant: Beaver Dam 7/20/2026 10:44:18 AM		Tech: S. Felletter PC:						
Structure ID: 4.6 MHA												
P1		MH048BA36		MH BASE T/n								
P3) 24" - CASTING HEIGHT - 8" P2) 48" - ECC CONE w/ 24" HOLE F/G - 24" P1) 48" - MH BASE T/n - 36" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) Hole - 32 1) Hole - 30 5) MH Step ML-10-TDS-NCR - 10"						0 lb 1550 lb 3166 lb 206 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 4922 lb		Structure Notes: 1. PER KYTC MH A / ASTM C478 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-510 F/C). REINFORCING PER ASTM A615 (GRADE 60.) - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.				
Rim: 433.89' Rim to Invert: 5.43' Slack: 1.16" Sump: 4" Step Position: 114°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	428.46'	0°	0"	24" ADS N-12	28"	Hole 32	32"	35.027"	0"	0"		
Invert 2	428.54'	228°	115.401"	24" ADS N-12	28"	Hole 30	30"	32.406"	1.96"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
						RIGHT-SIDE UP VIEW (int. dimensions)  INSIDE WALL DIMENSIONS  UPSIDE-DOWN VIEW (int. dimenions) 						
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 36" Height (Ext): 42"		Weight (Net): 3166 lb Volume (Net): 0.81cu.yd			
