

Job Name: 26-2648 Midtown Commons Apartments
Job Location: Madisonville, KY
Contractor: Steve Pleasant Excavating

Plant: Beaver Dam

Tech: S. Felletter

7/20/2026 10:46:18 AM

PC:



Structure ID: 4.7 DBI13G



P2 BX036048-08LD08-15X27

CB FLAT TOP 8"W w/15"x27" HOLE F/F

- P3) 15" x 27" - P.I.P. - BY OTHERS - 8"
P2) 36" x 48" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 35"
1) CASTING - HOE KY-230-G F/G (GRADE)
1) 36" x 48" - Conseal CS-102 1.00"
2) Hole - 32
2) Hole - 4

- 0 lb
1962 lb
5781 lb
237 lb
0 lb
0 lb
0 lb
Structure Notes:
1. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE KY-230-G F/G "GRADE").
6. STUB #5 BARS UP 4" AROUND OPENING IN TOP SLAB (SPA@12"C/C).

Structure Total: 7980 lb
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

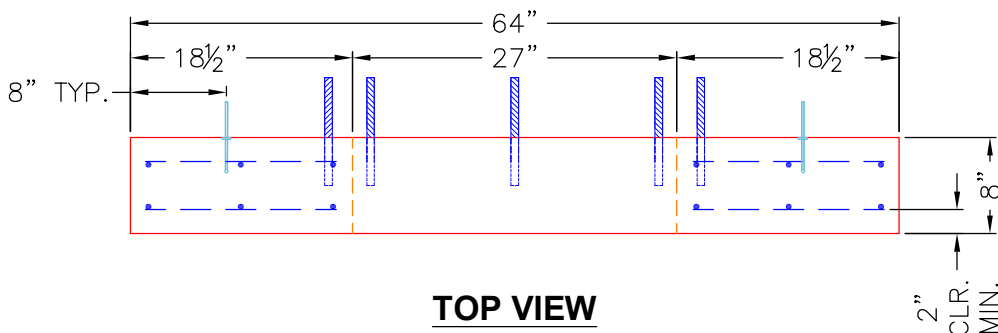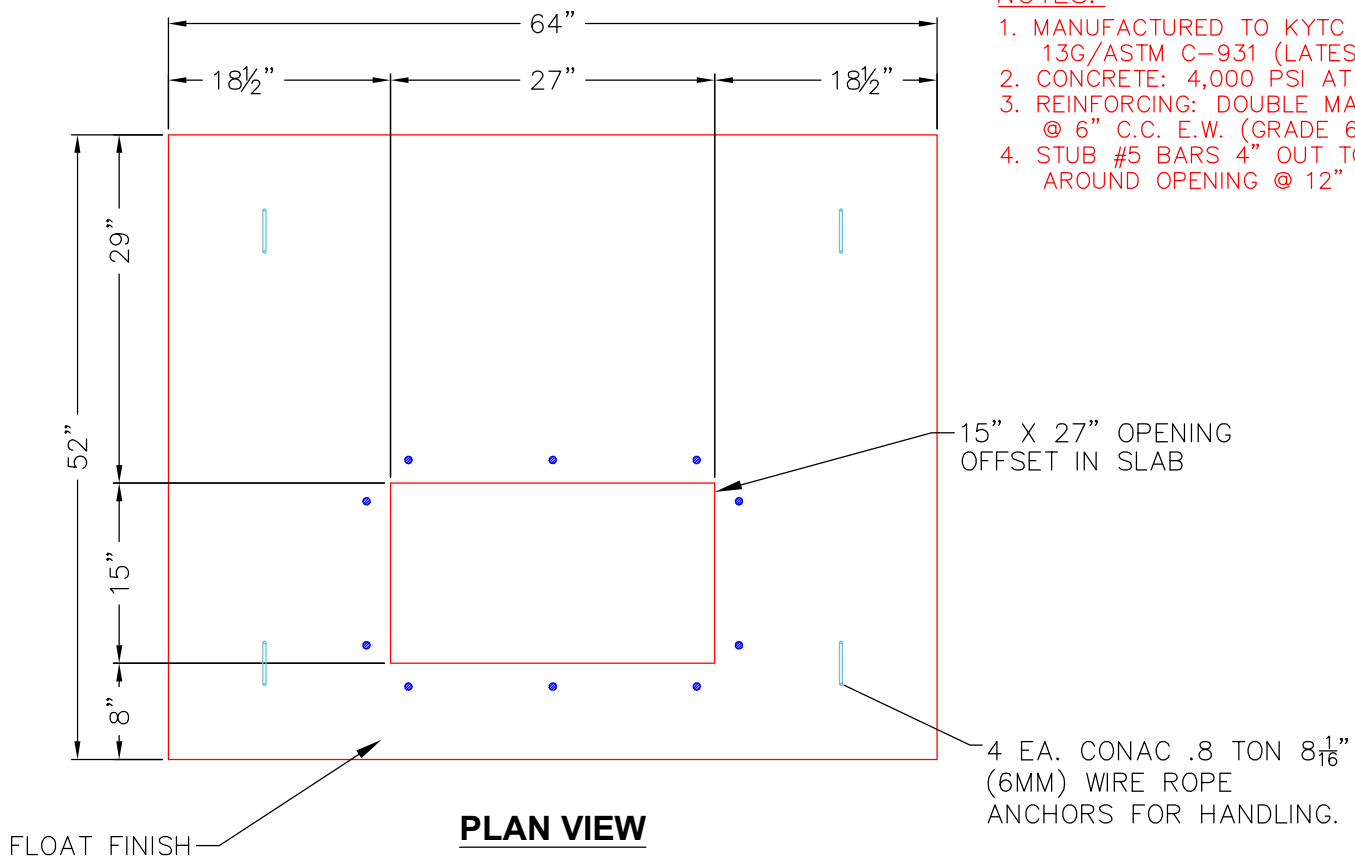

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1962 lb
Volume (Net): 0.5cu.yd
