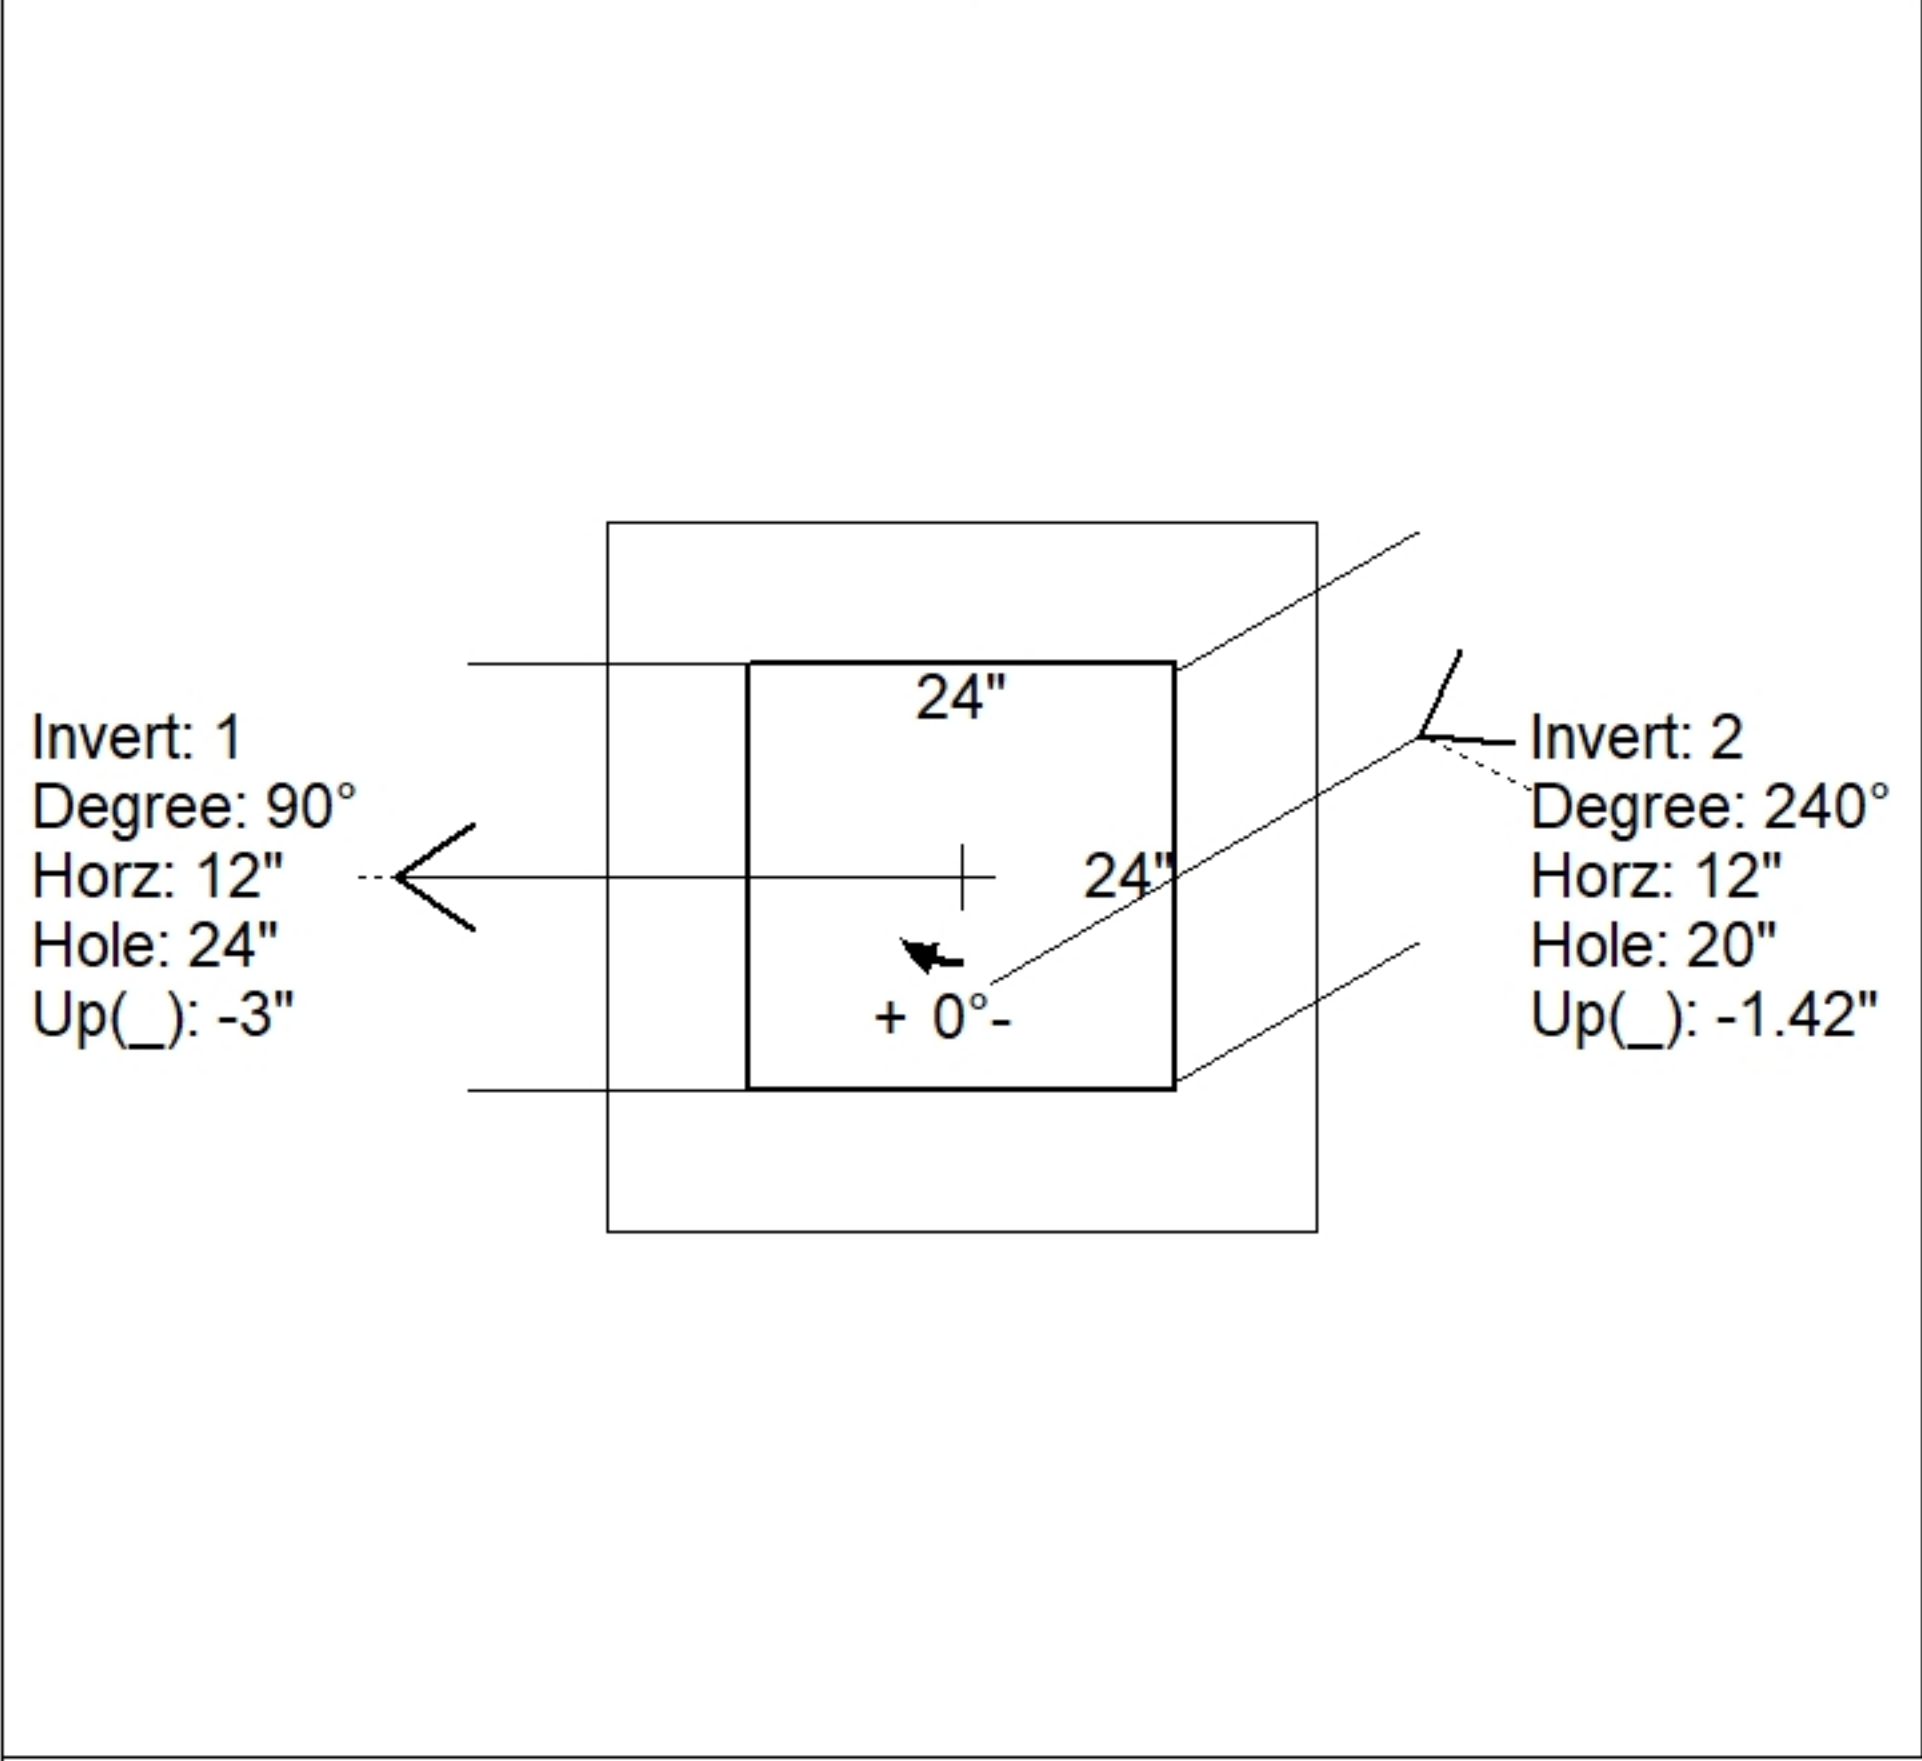
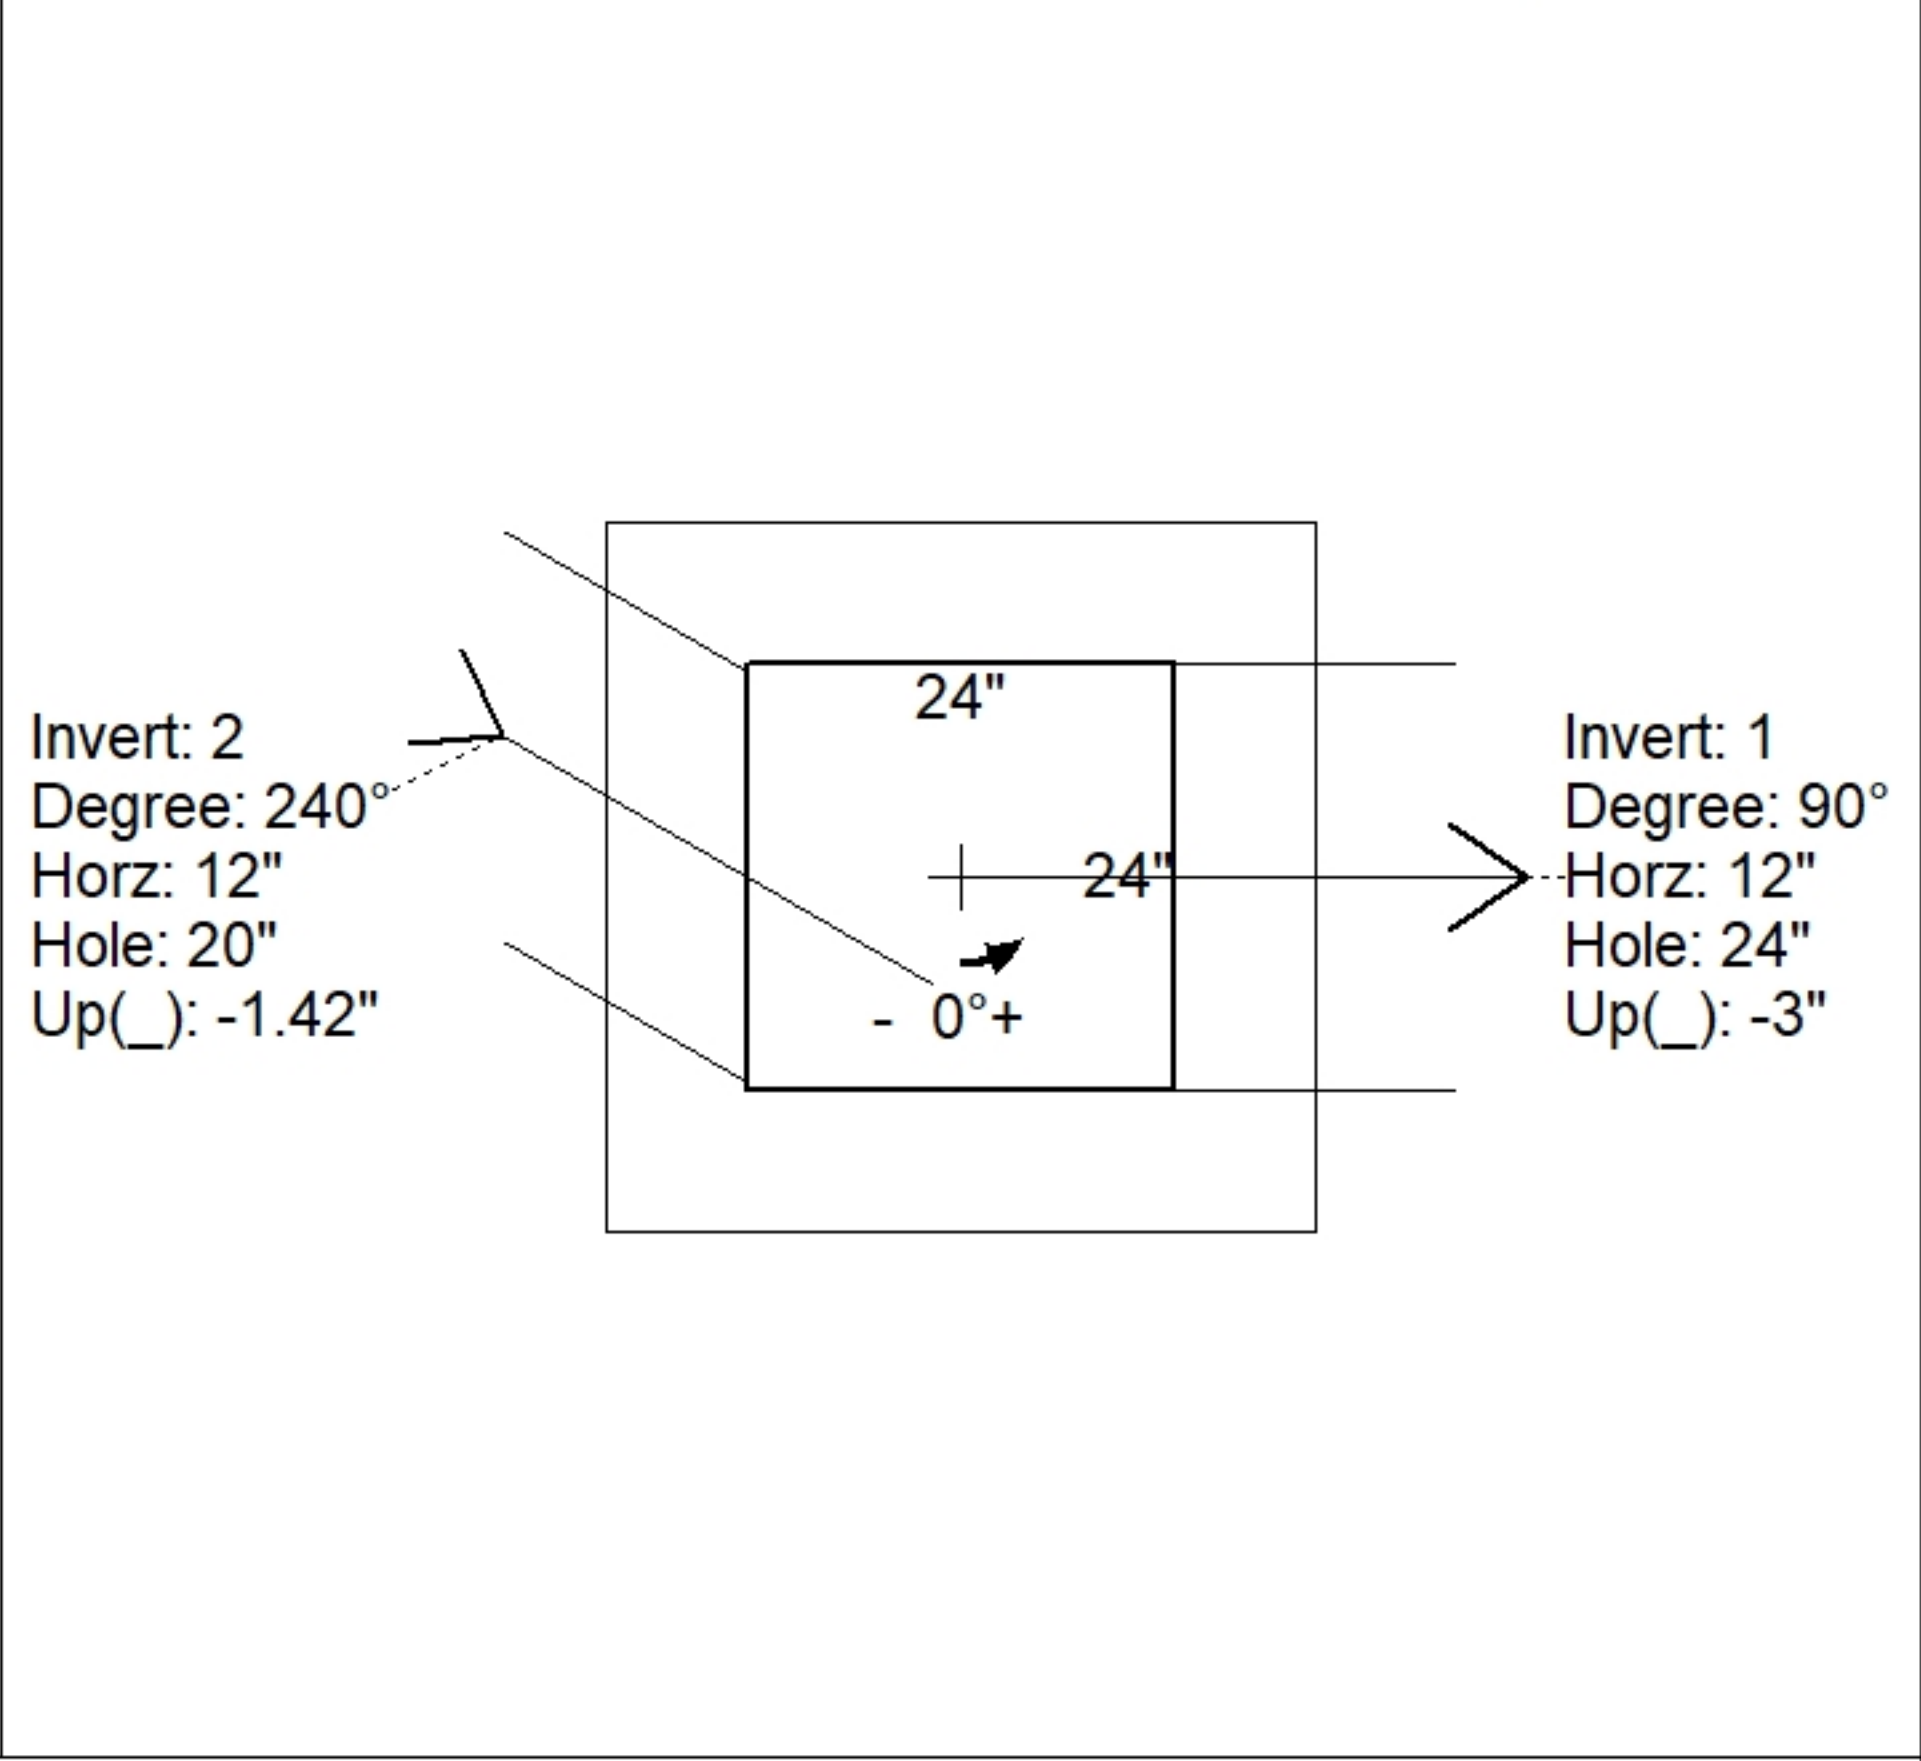
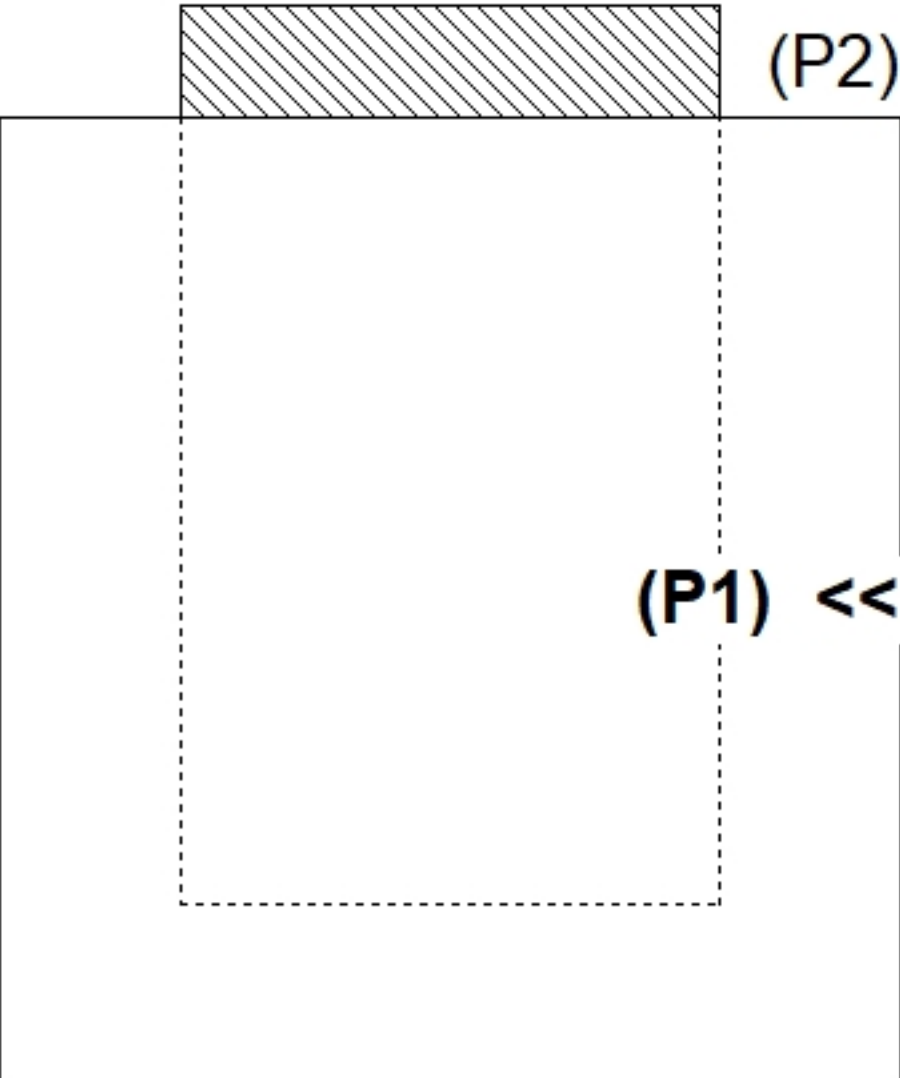
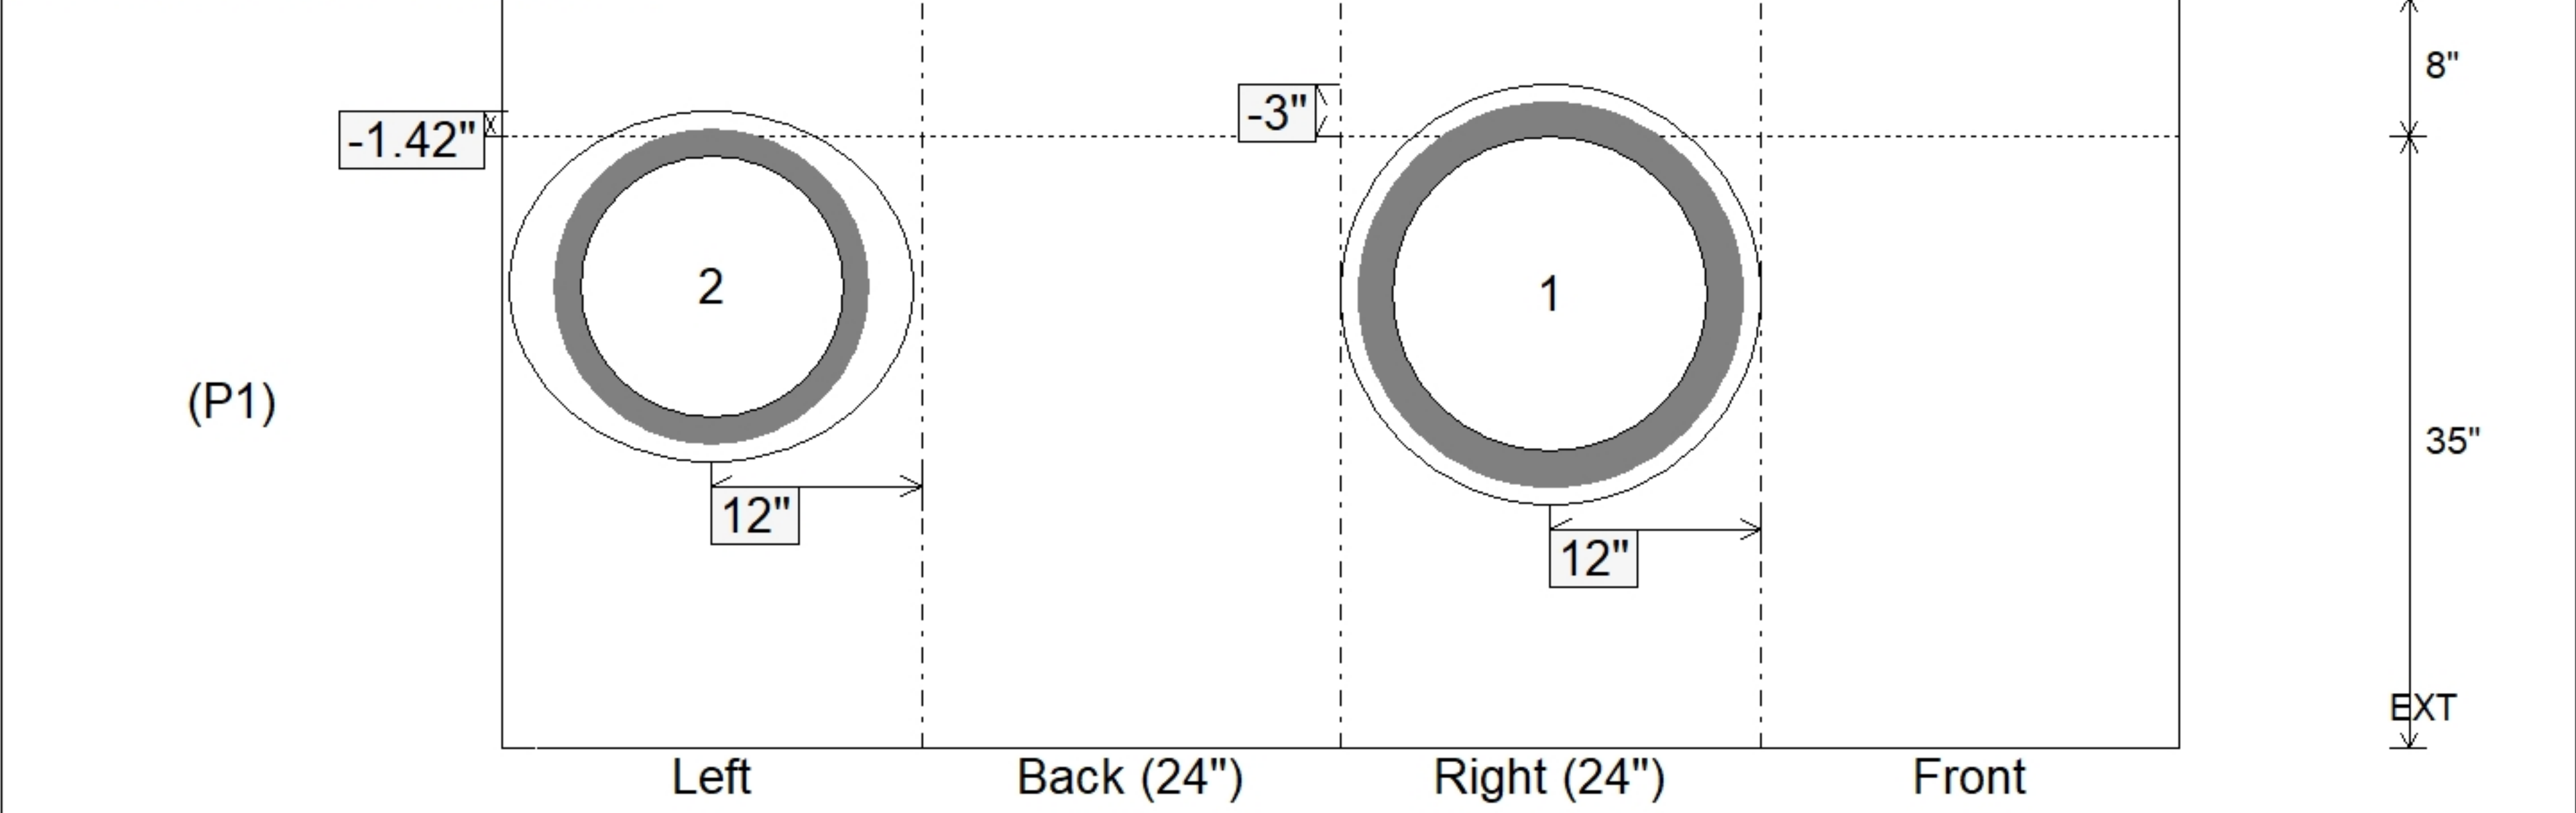


Job Name: 26-2648 Midtown Commons Apartments Job Location: Madisonville, KY Contractor: Steve Pleasant Excavating				Plant: Beaver Dam 7/20/2026 10:44:22 AM		Tech: S. Felletter PC:				
Structure ID: 6.2 CBIF										
P1		BX2424-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n						
P2) 24" x 24" - CASTING HEIGHT - 5" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 35" 1) CASTING - HOE KY-465 SET (CBI TY F) 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 24 1) Hole - 20						0 lb 3610 lb 465 lb 0 lb 0 lb 0 lb ----- Structure Total: 4075 lb		Structure Notes: 1. KYTC CBI TYPE F / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. NO STEPS. 5. CASTING BY ICAST (HOE KY-465 SET). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 430.02'		Rim to Invert: 3.41'		Slack: 0.92"		Sump: 0"		Step Position:		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	426.61'	90°	20"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"
Invert 2	426.7'	240°	15.381"	15" ADS N-12	18"	Hole 20	20"	23.094"	-1.42"	6"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)   INSIDE WALL DIMENSIONS 										
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 35" Height (Ext): 43"		Weight (Net): 3610 lb Volume (Net): 0.92cu.yd	
