


Contractor: Steve Pleasant Excavating

Plant: Beaver Dam





Slack: 0.64"

Structure Total: 7312 lb

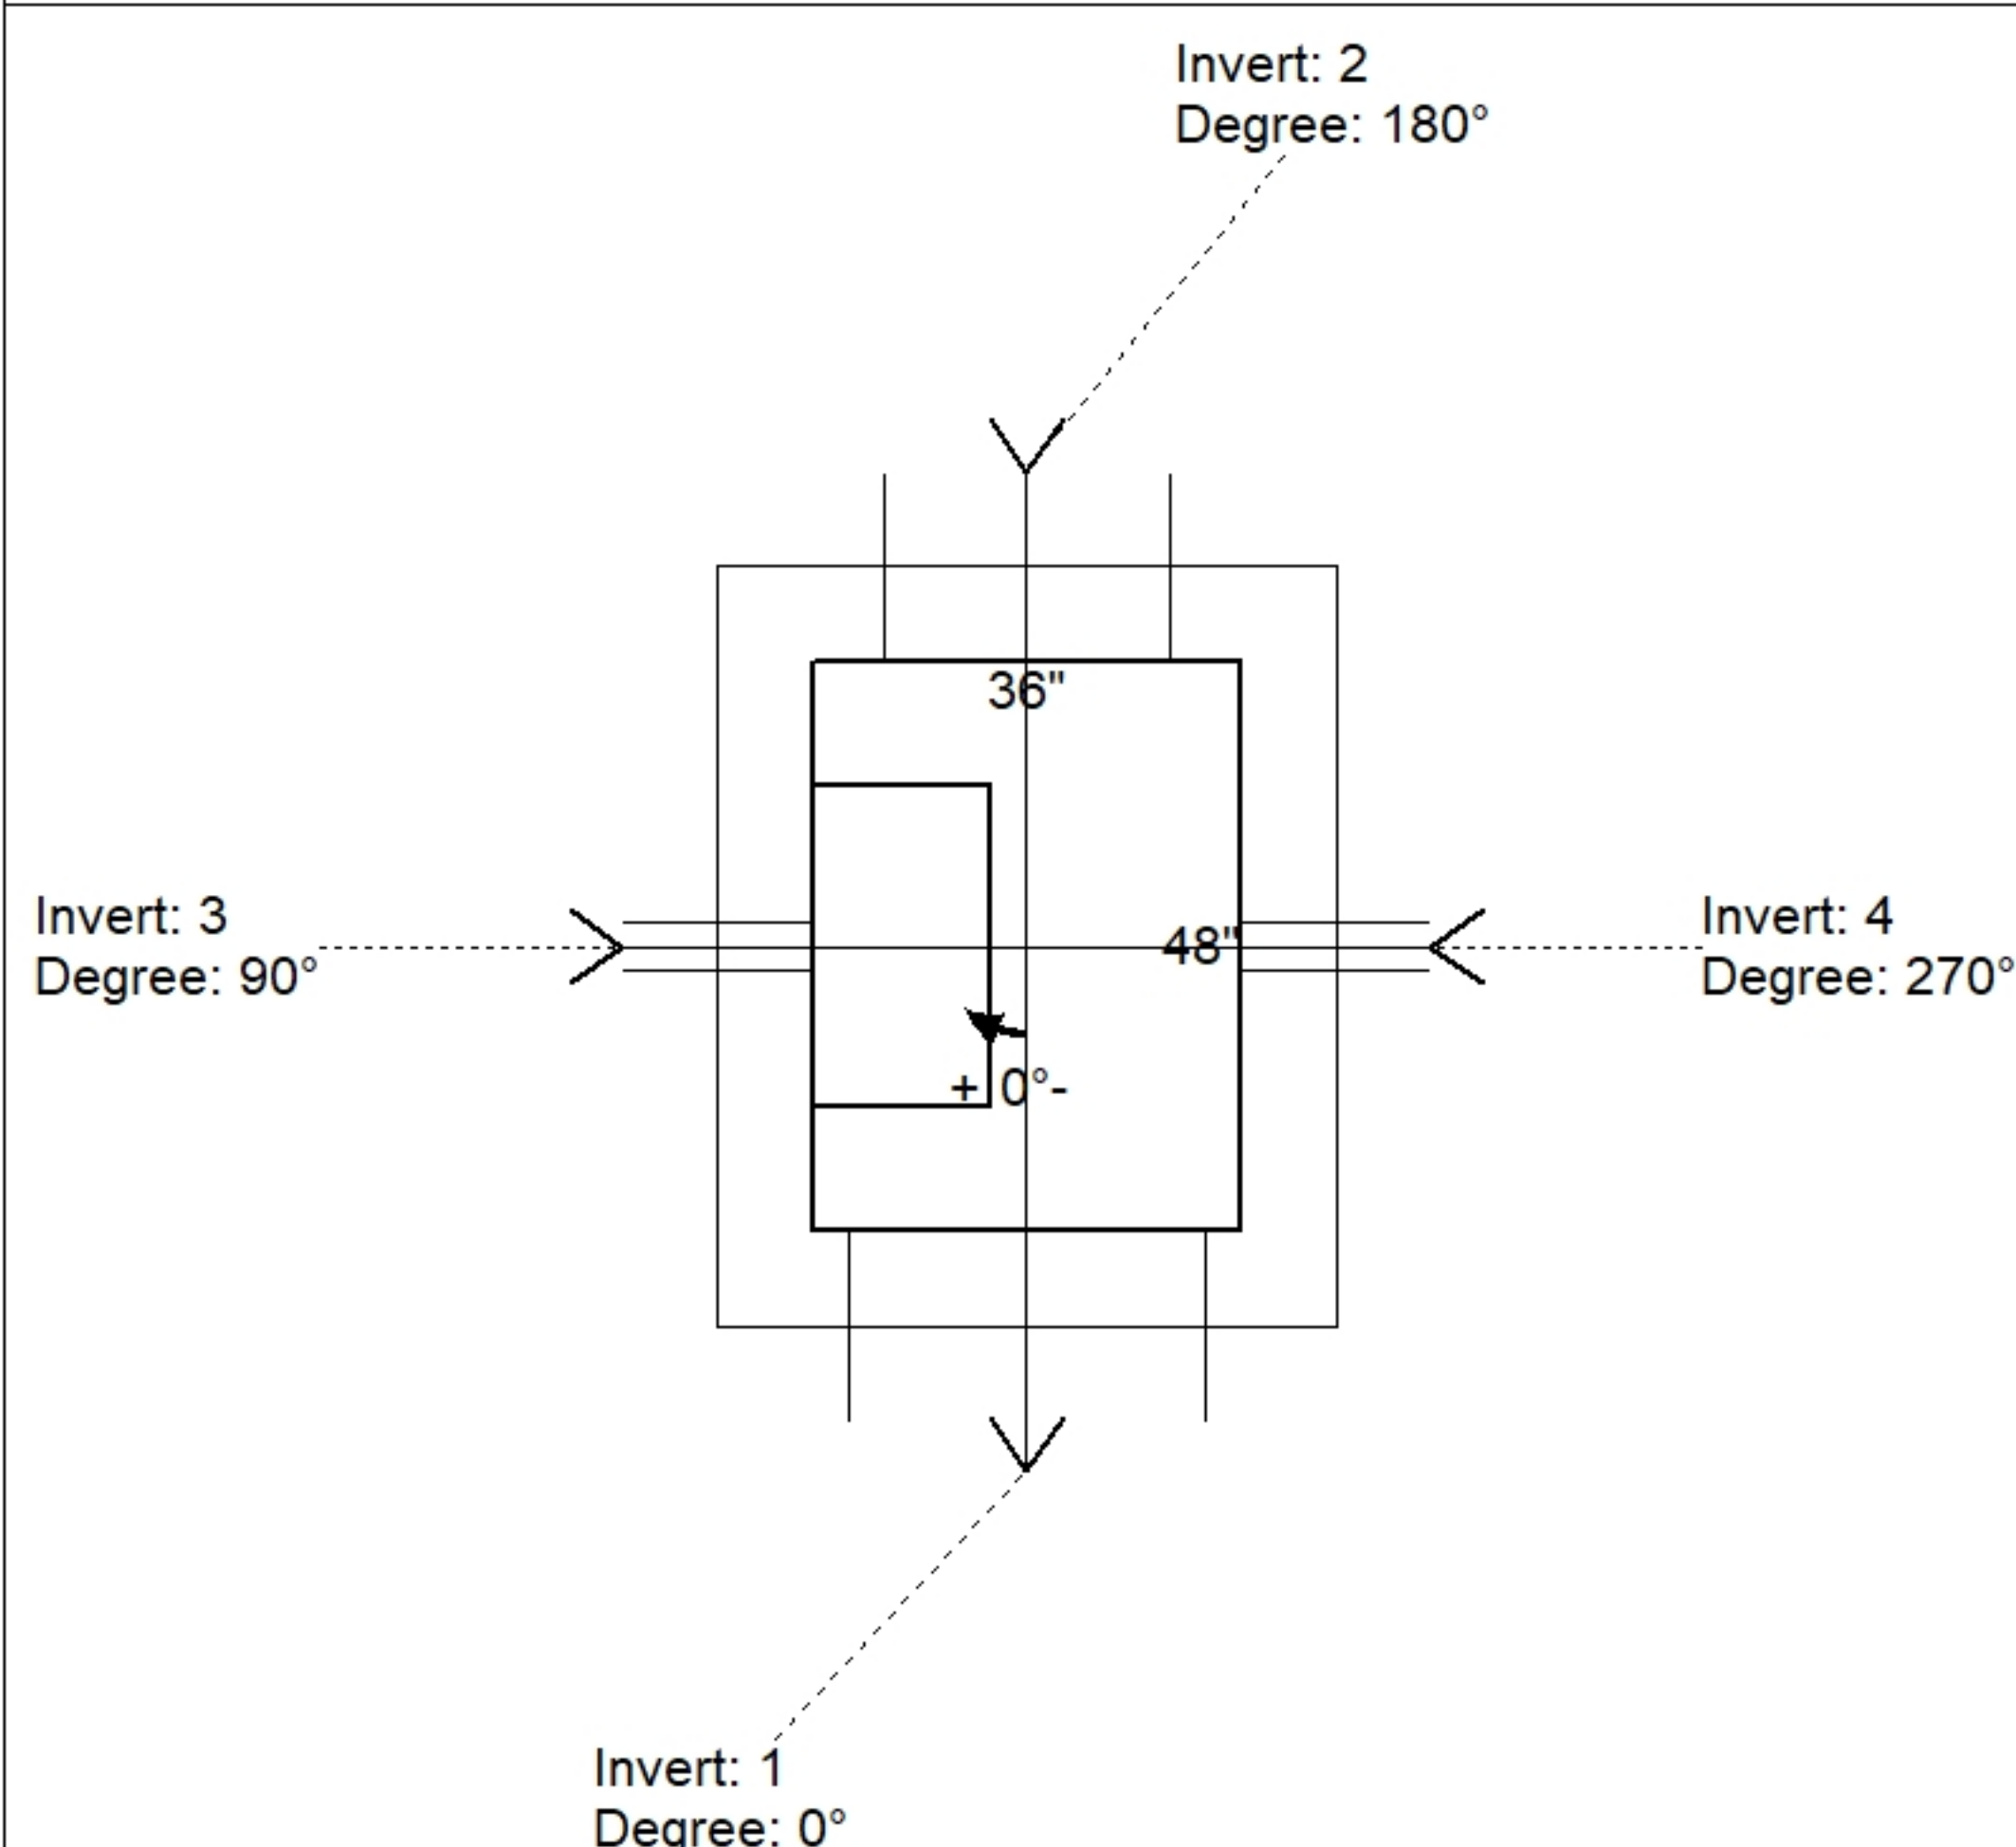

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (_)	Ref
Rim	429.77'							
Reducer								
Invert 1	426.05'	0°	24" ADS N-12	28"	30" x 30"	DOGHOUSE INVRTD 30"x30"	-3"	P1
Invert 2	426.13'	180°	18" ADS N-12	22"	24"	Hole 24	-2.04"	P1
Invert 3	427.716'	90°	4" WEEP HOLE	4"	4"	Hole 4	19.992"	P1
Invert 4	427.716'	270°	4" WEEP HOLE	4"	4"	Hole 4	19.992"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

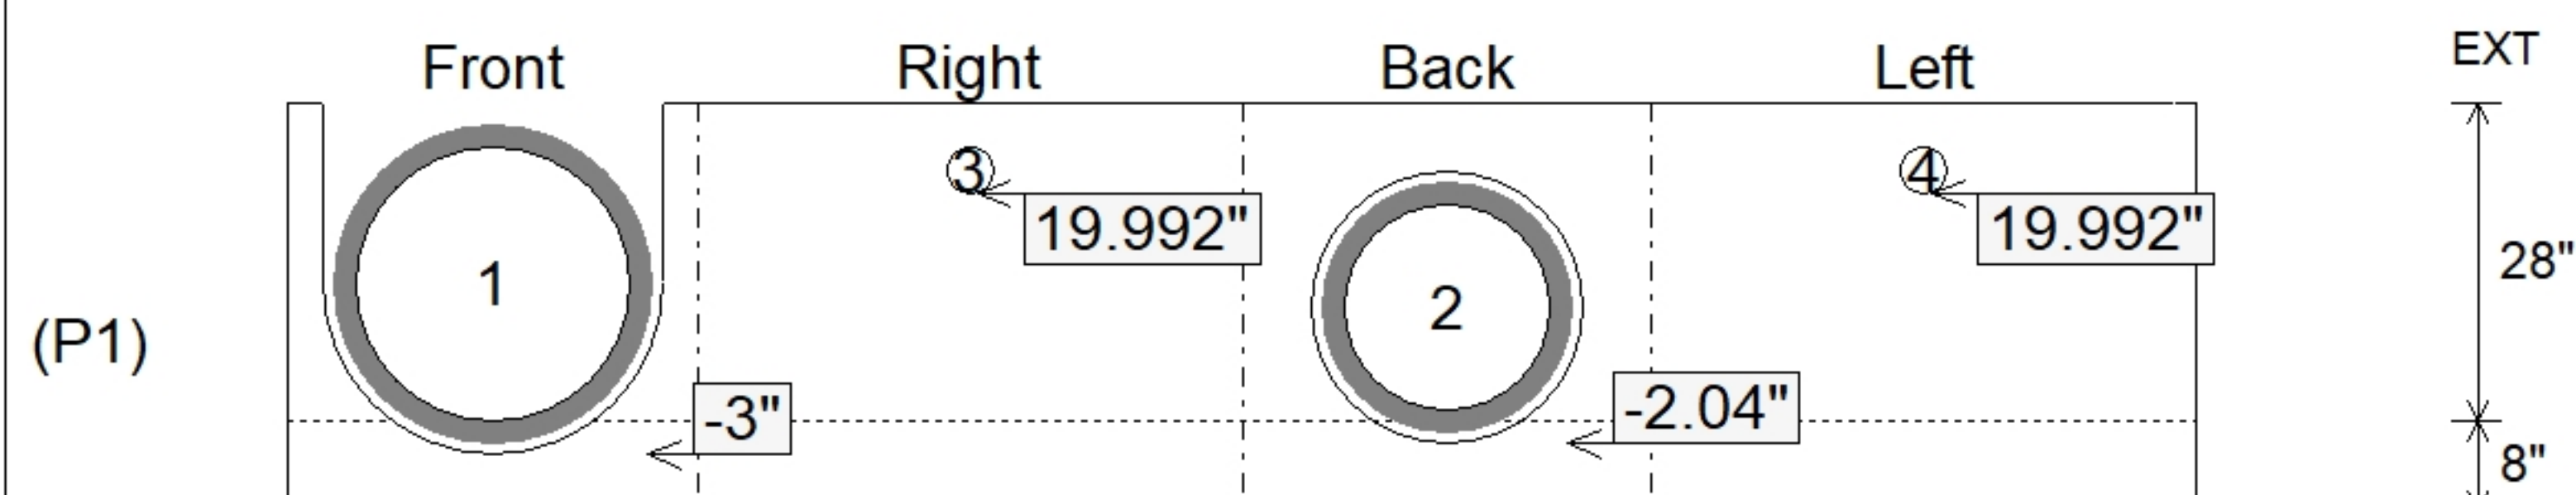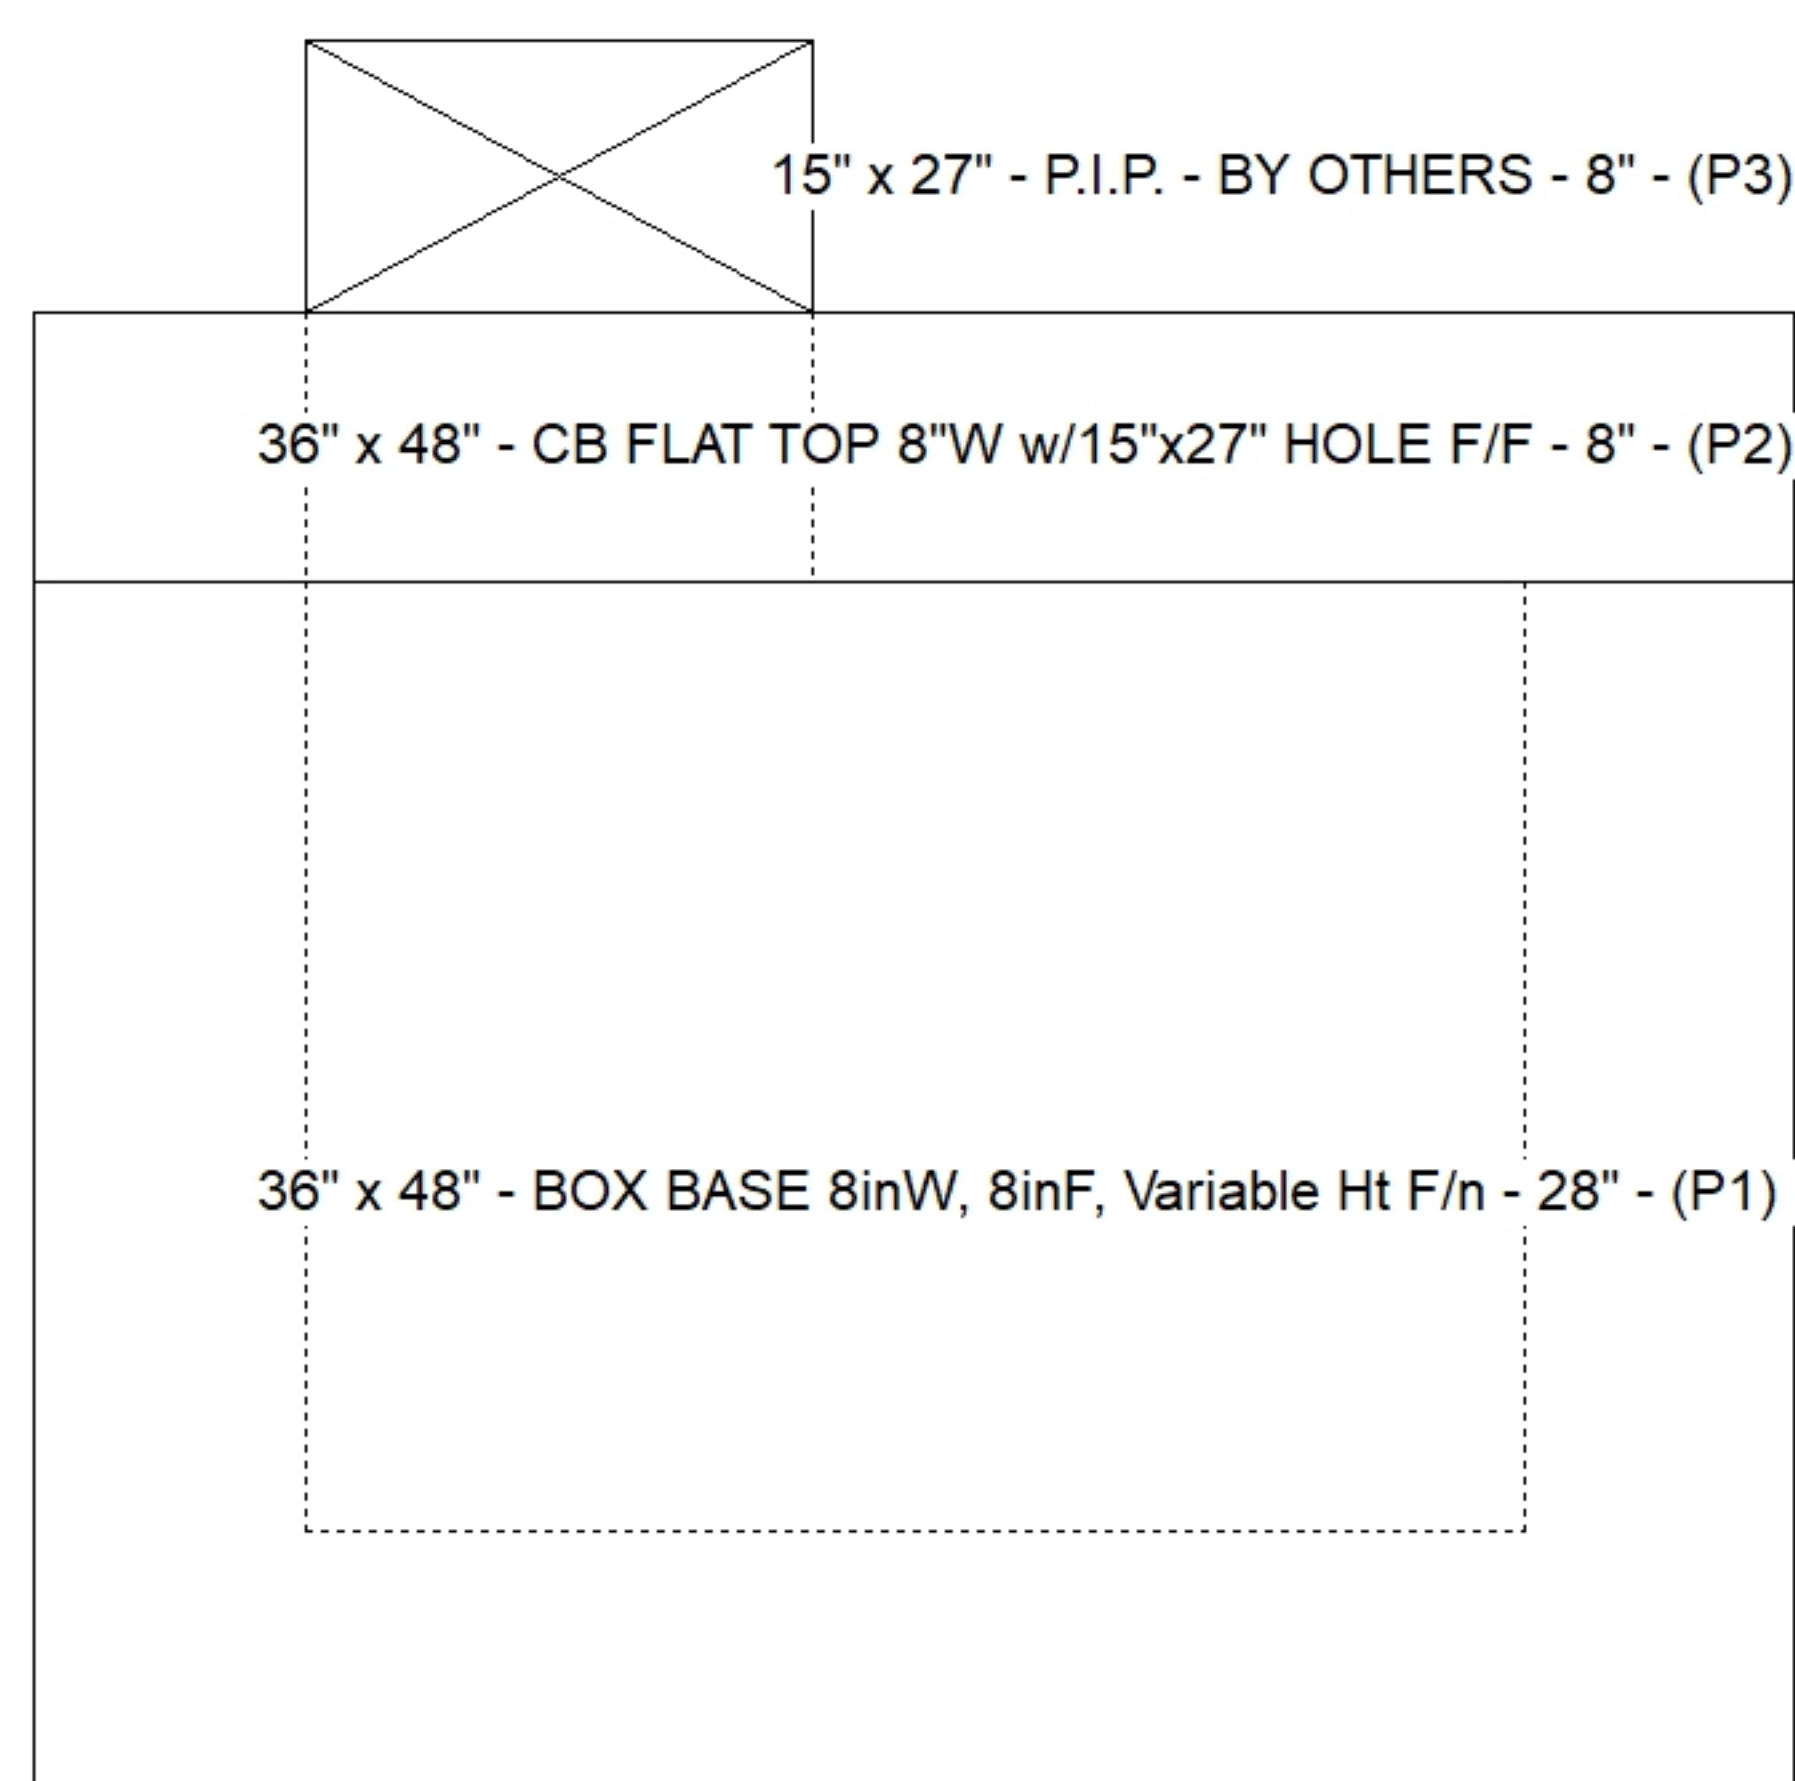

SUBMITTAL
APPROVED BY:
