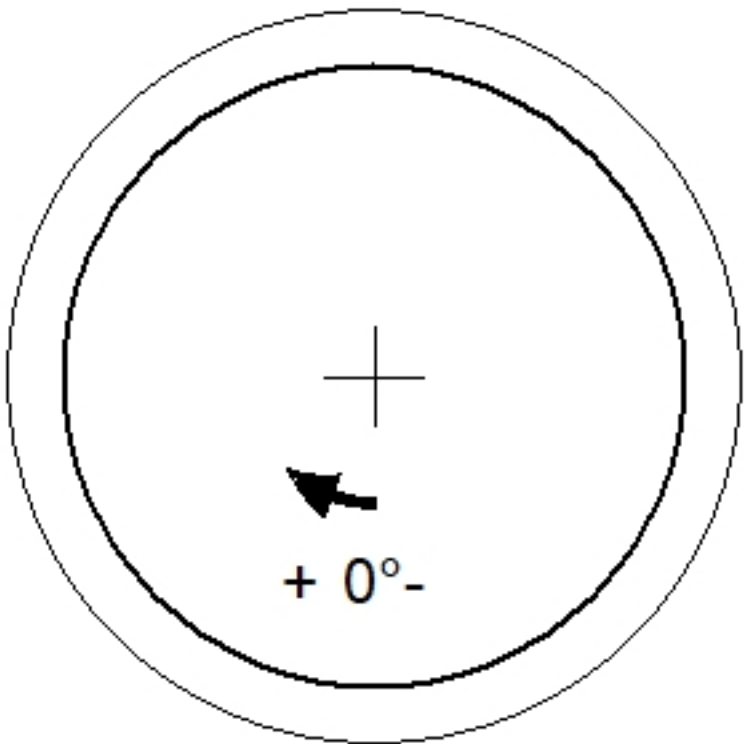
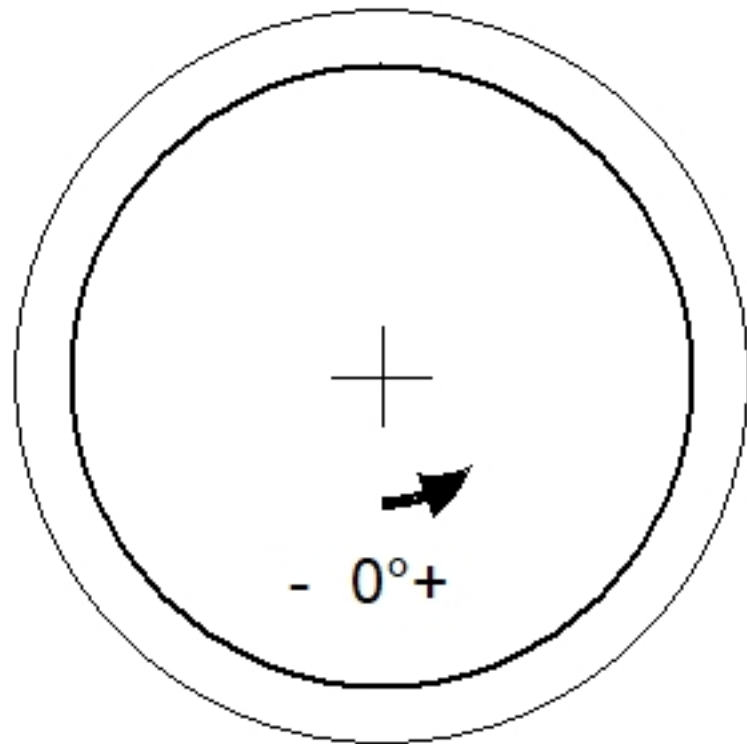
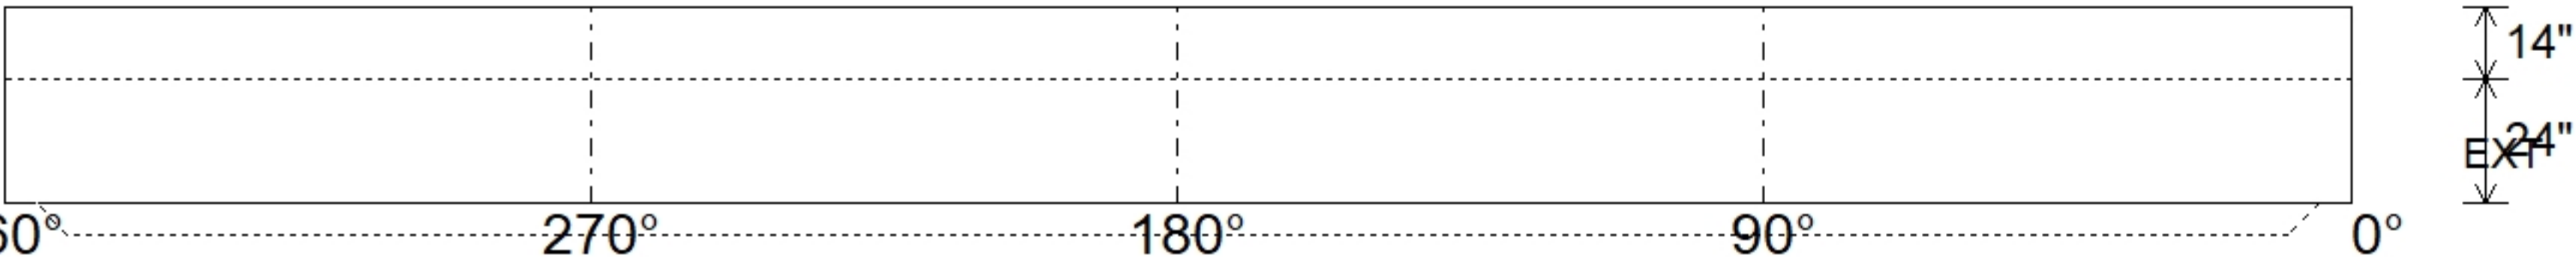


Job Name: 26-2692 868541 Georgetown Commons Phase 2					Plant: Beaver Dam		Tech: S. Felletter					
Job Location: Georgetown, KY					6/16/2026 3:18:13 PM		PC: C. Goff					
Contractor: Contech Engineering Solutions												
Structure ID: 10-CS-12												
P1		MH144BVF		MH MONOBASE 14F, Custom Ht T/n								
P6) 24" - CASTING HEIGHT - 4" P5) 144" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 18" P4) 144" - MH RISER T/G - 36" P3) 144" - MH RISER Custom Ht T/G - 64" P2) 144" - MH RISER T/G - 48" P1) 144" - MH MONOBASE 14F, Custom Ht T/n - 24" 1) CVSTENCILING 1) ASSEMBLY REQUIRED - BRACKETS ONLY 4) 144" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 32					0 lb 23623 lb 19370 lb 32619 lb 25826 lb 39578 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 141015 lb		Structure Notes: 4" CASTING BY OTHERS . LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE . ICAST TO INSTALL BRACKETS ONLY . CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE					
Rim: 871.5'					Rim to Invert: 7.76'		Slack: 7.036"		Sump: 107.916"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌋)	Offset		
Invert 1												
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
(P6) (P5) (P4) (P3) (P2) (P1) << RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions) 												
INSIDE WALL DIMENSIONS (P1) 												
Coating (Int):			Seam Up: Tongue		Wall Thickness: 13"		Height (Int): 24"		Weight (Net): 39578 lb			
Coating (Ext):			Seam Dn: n/a		Floor Height: 14"		Height (Ext): 38"		Volume (Net): 10.11cu.yd			
