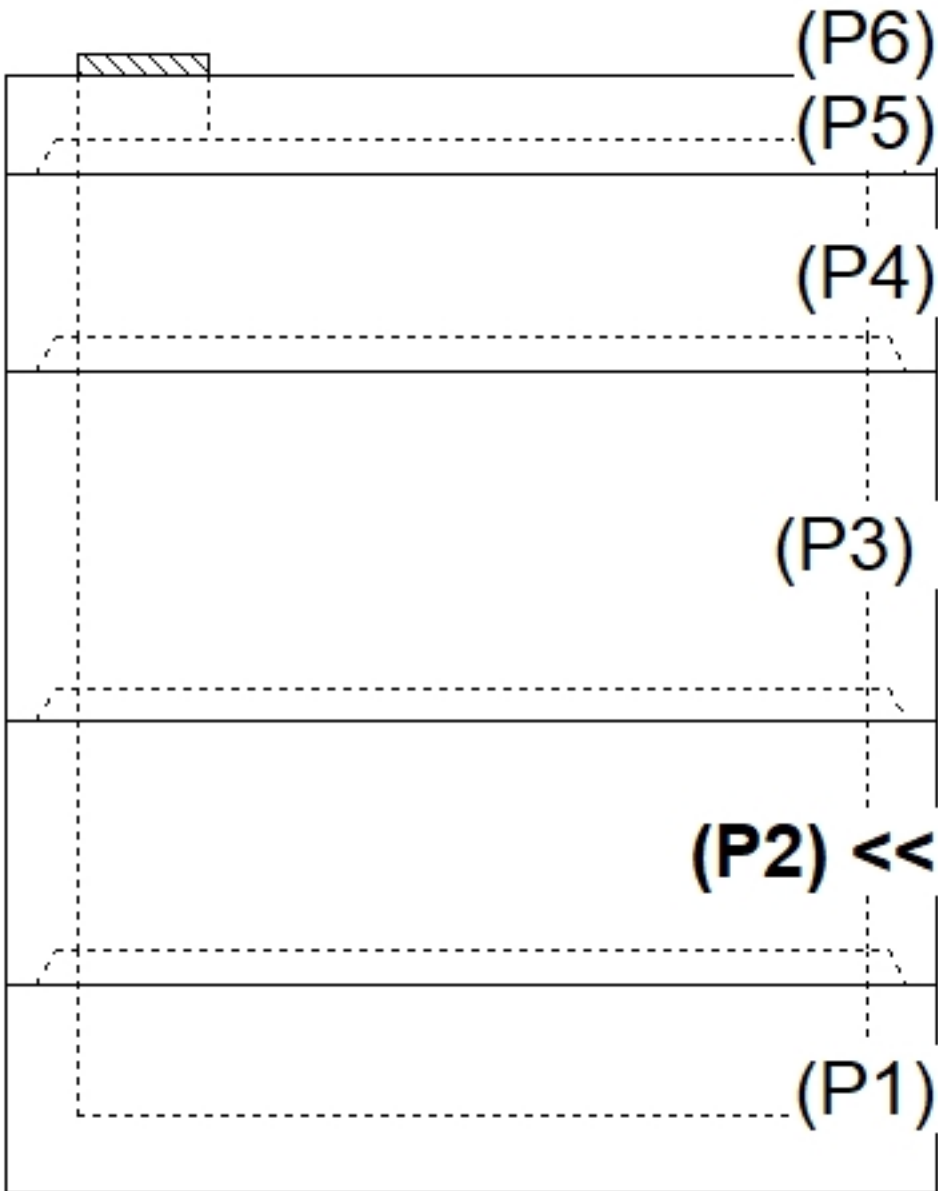
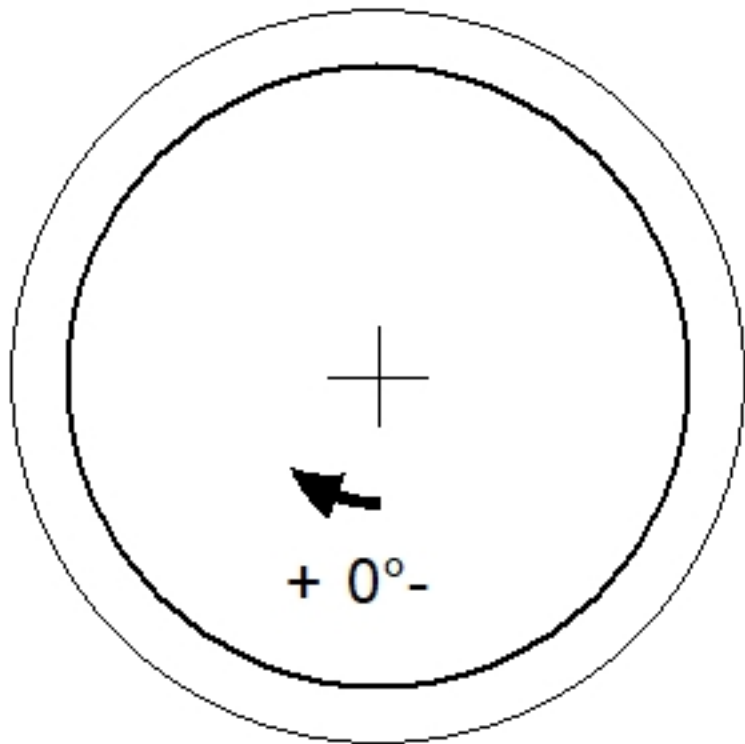
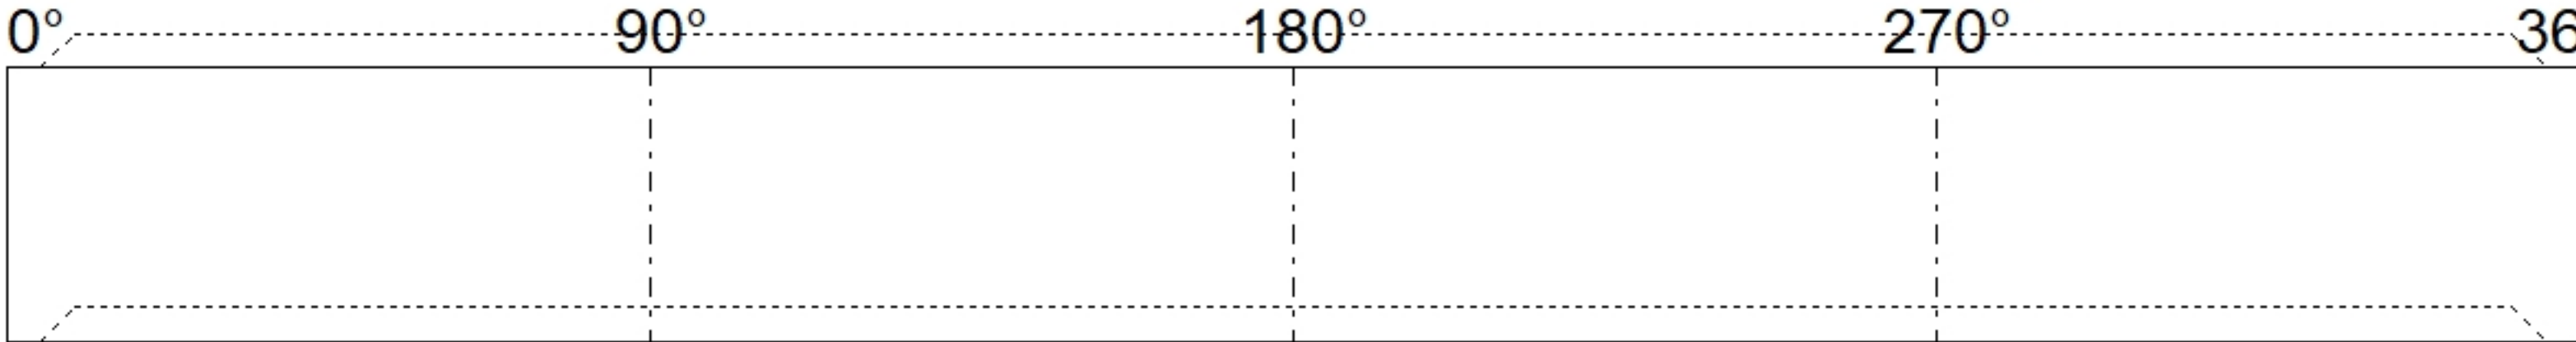


Job Name: 26-2692 868541 Georgetown Commons Phase 2 Job Location: Georgetown, KY Contractor: Contech Engineering Solutions					Plant: Beaver Dam 6/16/2026 3:18:36 PM		Tech: S. Felletter PC: C. Goff						
Structure ID: 10-CS-12													
P2			MH144RS48			MH RISER T/G							
P6) 24" - CASTING HEIGHT - 4" P5) 144" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 18" P4) 144" - MH RISER T/G - 36" P3) 144" - MH RISER Custom Ht T/G - 64" P2) 144" - MH RISER T/G - 48" P1) 144" - MH MONOBASE 14F, Custom Ht T/h - 24" 1) CVSTENCILING 1) ASSEMBLY REQUIRED - BRACKETS ONLY 4) 144" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 32						0 lb 23623 lb 19370 lb 32619 lb 25826 lb 39578 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 141015 lb		Structure Notes: 4" CASTING BY OTHERS . LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE . ICAST TO INSTALL BRACKETS ONLY . CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE					
Rim: 871.5' Rim to Invert: 7.76' Slack: 7.036" Sump: 107.916" Step Position:													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
(P2)										EXT 48"			
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 13" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 25826 lb Volume (Net): 6.6cu.yd			
