

Job Name: 26-2692 868541 Georgetown Commons Phase 2
Job Location: Georgetown, KY
Contractor: Contech Engineering Solutions

Plant: Beaver Dam

Tech: S. Felletter

6/15/2026 3:41:02 PM

PC: C. Goff



Structure ID: 10-CS-12

P3 MH144RSVF

MH RISER Custom Ht T/G

- P6) 24" - CASTING HEIGHT - 4"
P5) 144" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 18"
P4) 144" - MH RISER T/G - 36"
P3) 144" - MH RISER Custom Ht T/G - 64"
P2) 144" - MH RISER T/G - 48"
P1) 144" - MH MONOBASE 14F, Custom Ht T/n - 24"
1) CVSTENCILING
1) ASSEMBLY REQUIRED - BRACKETS ONLY
4) 144" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 32



0 lb
23623 lb
19370 lb
32619 lb
25826 lb
39578 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 141015 lb

Structure Notes:
4" CASTING BY OTHERS
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICAST TO INSTALL BRACKETS ONLY
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE


Rim: 871.5' Rim to Invert: 7.76' Slack: 7.036" Sump: 107.916" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	863.74'	270°	400.553"	24" HDPE	27.8"	Hole 32	32"	32.269"	25.916"	0"
Invert 2	863.74'	218°	299.079"	24" HDPE	27.8"	Hole 32	32"	34.394"	25.916"	-24"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

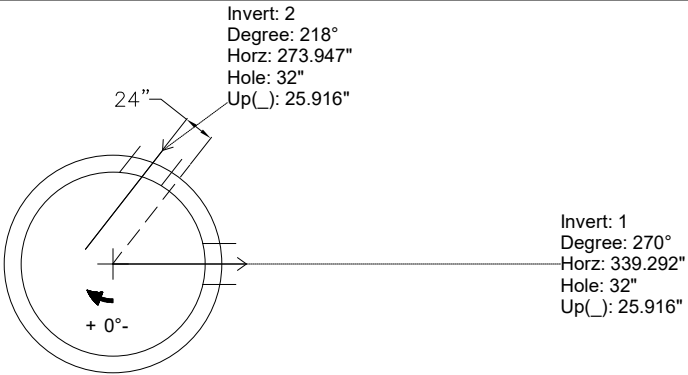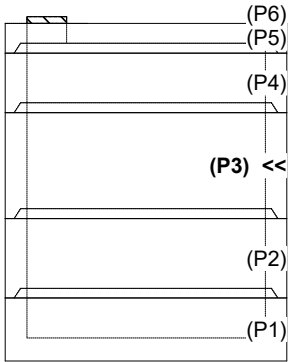

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 13" Floor Height: 0"	Height (Int): 64" Height (Ext): 64"	Weight (Net): 32619 lb Volume (Net): 8.33cu.yd
----------------------------------	------------------------------------	---	--	---
