
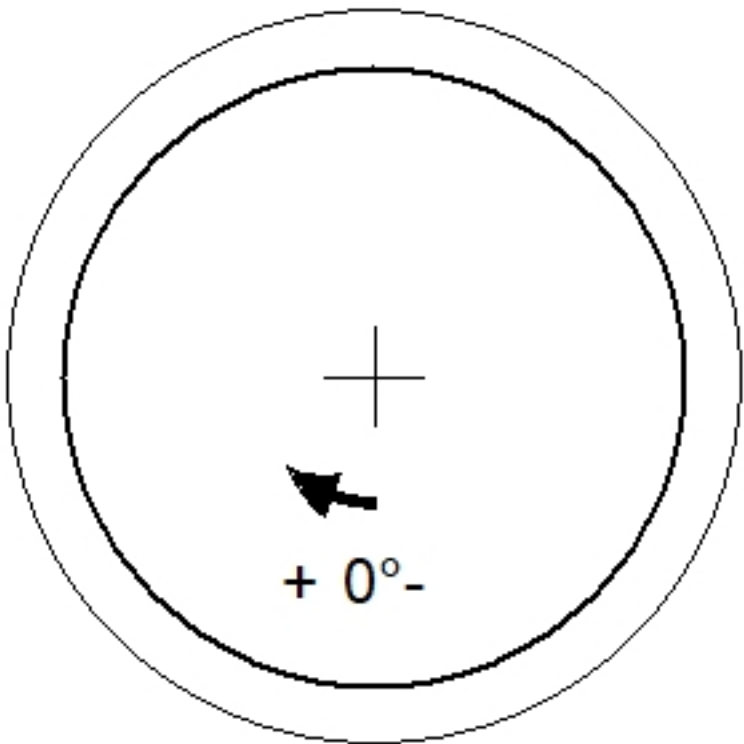
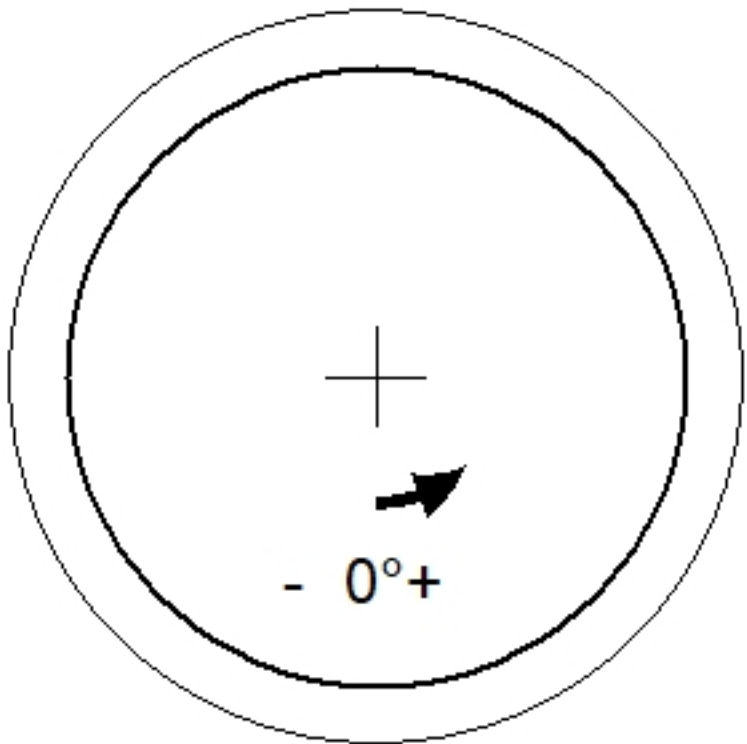
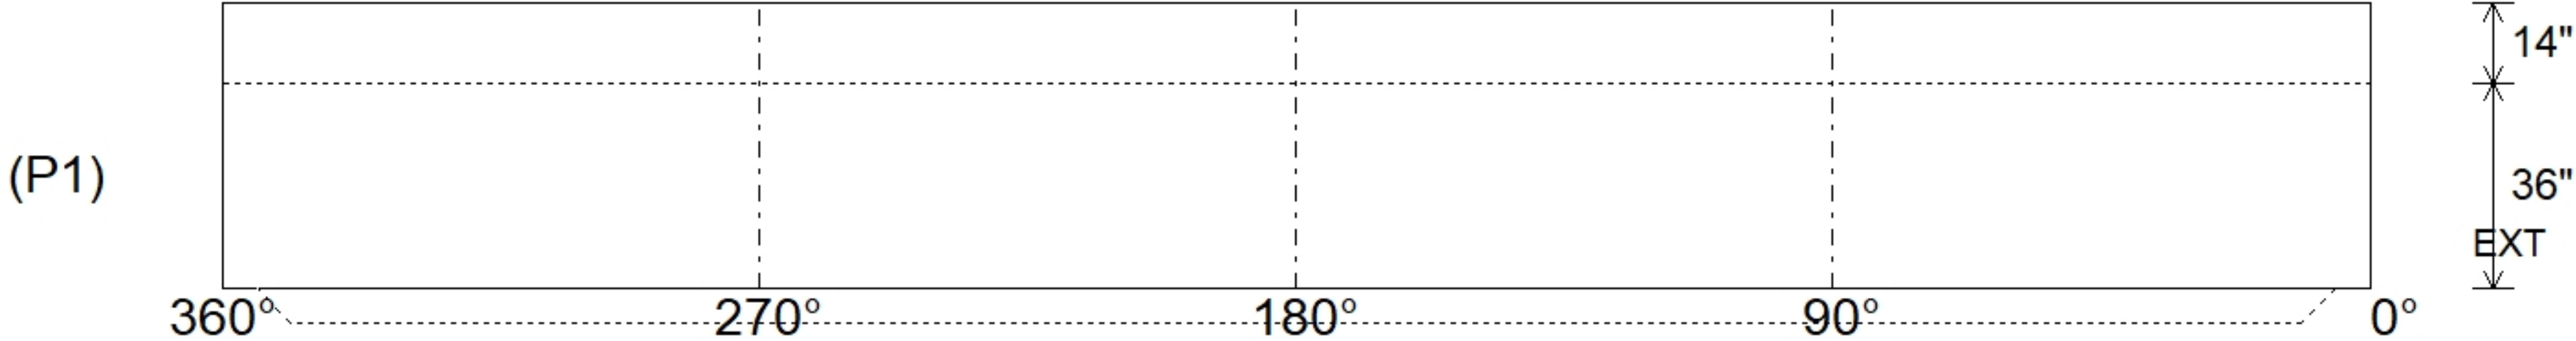


Job Name: 26-2692 868541 Georgetown Commons Phase 2					Plant: Beaver Dam		Tech: S. Felletter							
Job Location: Georgetown, KY					6/16/2026 3:18:12 PM		PC: C. Goff							
Contractor: Contech Engineering Solutions														
Structure ID: 15-CS-10														
P1		MH120BVF		MH MONOBASE 14F, Custom Ht T/n										
P5) 24" - CASTING HEIGHT - 4" P4) 120" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 18" P3) 120" - MH RISER T/G - 84" P2) 120" - MH RISER T/G - 36" P1) 120" - MH MONOBASE 14F, Custom Ht T/n - 36" 1) CVSTENCILING 1) ASSEMBLY REQUIRED - BRACKETS ONLY 3) 120" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 32					0 lb 16223 lb 30345 lb 13675 lb 32280 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 92523 lb		Structure Notes: 4" CASTING BY OTHERS . LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE . ICAST TO INSTALL BRACKETS ONLY . CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE							
Rim: 872.5' Rim to Invert: 7.25' Slack: 1.076" Sump: 92.076" Step Position:														
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌋)	Offset				
Invert 1														
Invert 2														
Invert 3														
Invert 4														
Invert 5														
Invert 6														
Invert 7														
Invert 8														
					RIGHT-SIDE UP VIEW (int. dimensions)					UPSIDE-DOWN VIEW (int. dimenions)				
														
					INSIDE WALL DIMENSIONS									
														
Coating (Int):			Seam Up: Tongue		Wall Thickness: 11"		Height (Int): 36"		Weight (Net): 32280 lb					
Coating (Ext):			Seam Dn: n/a		Floor Height: 14"		Height (Ext): 50"		Volume (Net): 8.24cu.yd					
