

Job Name: 26-2692 868541 Georgetown Commons Phase 2
Job Location: Georgetown, KY
Contractor: Contech Engineering Solutions

Plant: Beaver Dam
6/15/2026 3:41:01 PM

Tech: S. Felletter
PC: C. Goff



Structure ID: 15-CS-10

P3 MH120RS84

MH RISER T/G

- P5) 24" - CASTING HEIGHT - 4"
P4) 120" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 18"
P3) 120" - MH RISER T/G - 84"
P2) 120" - MH RISER T/G - 36"
P1) 120" - MH MONOBASE 14F, Custom Ht T/n - 36"
1) CVSTENCILING
1) ASSEMBLY REQUIRED - BRACKETS ONLY
3) 120" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 32



0 lb
16223 lb
30345 lb
13675 lb
32280 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 92523 lb

Structure Notes:
4" CASTING BY OTHERS
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICAST TO INSTALL BRACKETS ONLY
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE


Rim: 872.5' Rim to Invert: 7.25' Slack: 1.076" Sump: 92.076" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	865.25'	270°	334.58"	24" HDPE	27.8"	Hole 32	32"	32.392"	10.076"	0"
Invert 2	865.25'	317°	417.304"	24" HDPE	27.8"	Hole 32	32"	35.76"	10.076"	24"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

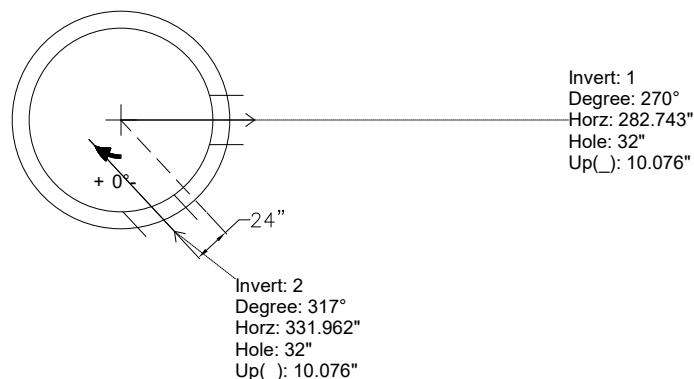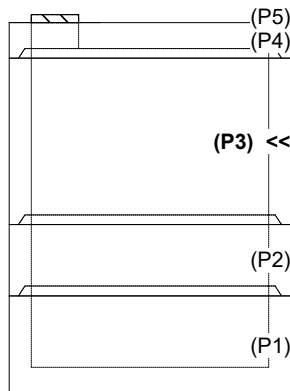

INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 11"
Floor Height: 0"

Height (Int): 84"
Height (Ext): 84"

Weight (Net): 30345 lb
Volume (Net): 7.75cu.yd
