



Job Name: 26-2712 - Appalachian Center for Preventive Medicine Job Location: Prestonsburg, KY Contractor: Rising Sun Development Company					Plant: 100 10/8/2026 11:21:30 AM		Tech: Jared - F PC: T. Ryan				
Structure ID: DBI 2 ST-DBI											
P1 BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht F/n									
P2) 24" x 36" - CASTING HEIGHT - 4" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 39" 1) CASTING - HOE 518 F/G 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 16						0 lb 5106 lb 354 lb 0 lb 0 lb ----- 0 lb Structure Total: 5460 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 518 F/G). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 645.73' Rim to Invert: 3.66' Slack: 0.92" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	642.07'	0°	20"	12" HDPE	14.5"	Hole 16	16"	16"	-1.25"	0"	
Invert 2	642.07'	180°	20"	12" HDPE	14.5"	Hole 16	16"	16"	-1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

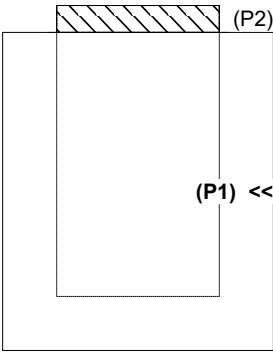

(P1) <<


(P2)

RIGHT-SIDE UP VIEW (int. dimensions)

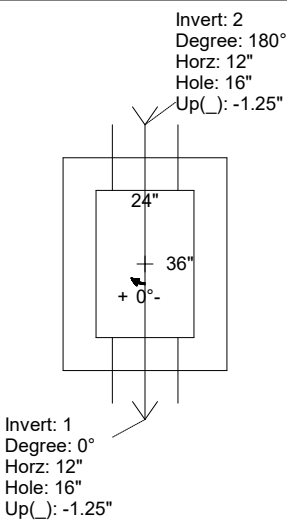

Upside-Down View (int. dimensions)

INSIDE WALL DIMENSIONS

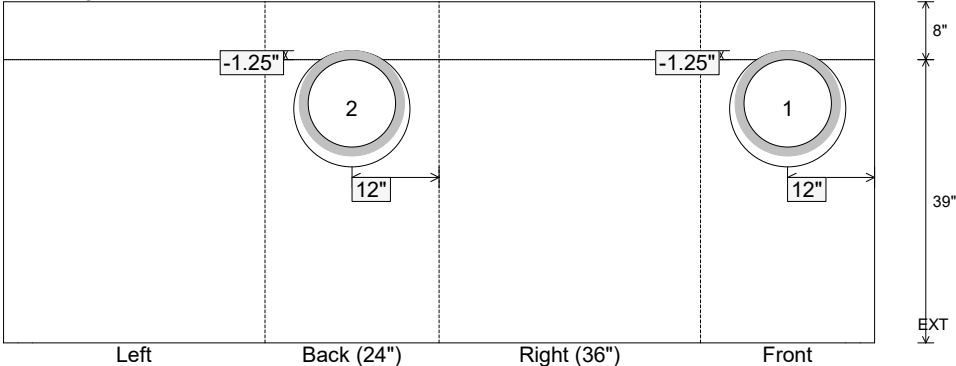

Left Back (24") Right (36") Front

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 39" Height (Ext): 47"	Weight (Net): 5106 lb Volume (Net): 1.3cu.yd
----------------------------------	-------------------------------	--	--	---
