



Job Name: 26-2748 ST Development Greystone Subdivision Job Location: Madisonville, KY Contractor: Steve Pleasant Excavating				Plant: 100 7/7/2026 7:54:37 AM		Tech: Jared - A PC: Erica Bradley				
Structure ID: 5A ST-CI										
P1 BX2424-08BA36				BOX BASE 8inW, 8inF F/n						
P2) 24" x 24" - CASTING HEIGHT - 3.50" P1) 24" x 24" - BOX BASE 8inW, 8inF F/n - 36" 1) CASTING - HOE 410 F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 20						0 lb 3957 lb 228 lb 0 lb 0 lb ----- 4185 lb Structure Total:		Structure Notes: 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. STORM INVERT BY OTHERS 5. HOE-410 FRAME & GRATE SUPPLIED BY ICAST		
Rim: 430.03' Rim to Invert: 3.25' Slack: 0.75" Sump: 1.25" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	426.78'	270°	20"	15" HDPE	17.6"	Hole 20	20"	20"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

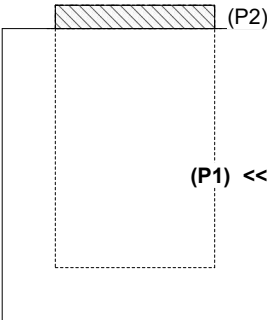


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

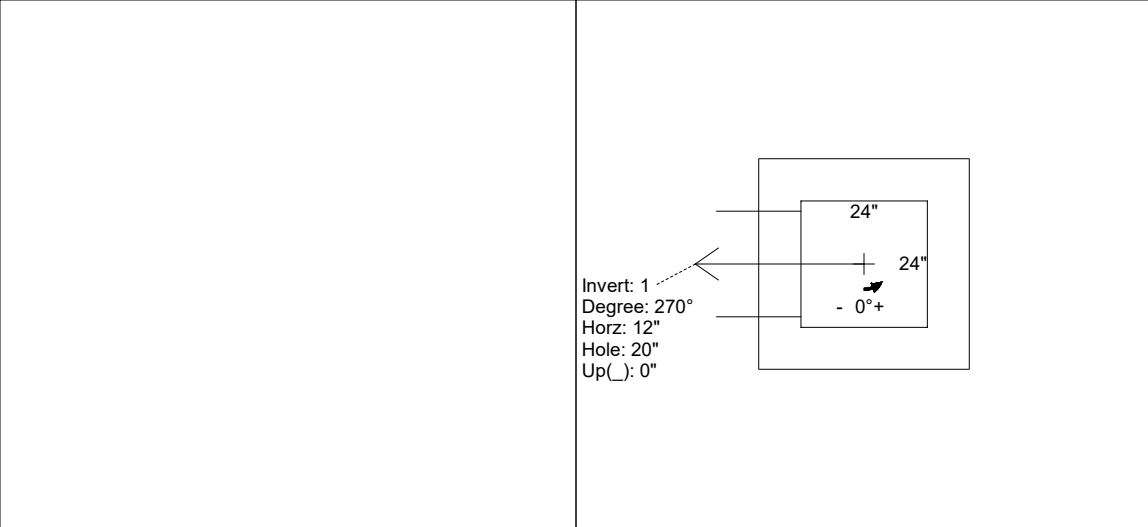

INSIDE WALL DIMENSIONS

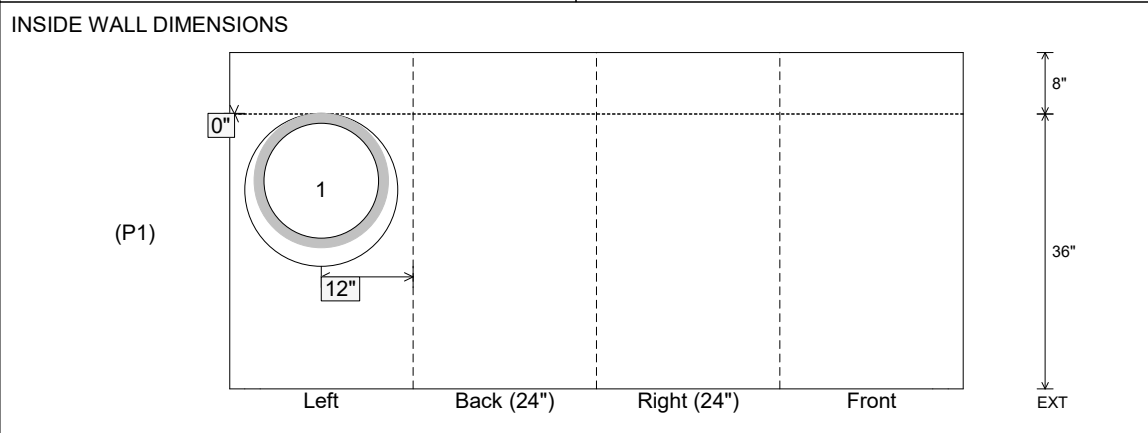

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 3957 lb Volume (Net): 1.01cu.yd
----------------------------------	-------------------------------	--	--	--
