



Job Name: 26-2756 - Lofts at Cadiz Job Location: Cadiz, KY 42241 Contractor: BTM Excavating, LLC					Plant: 100		Tech: Jared - F			
					9/17/2026 10:47:21 PM		PC: T. Lewis			
Structure ID: CBI-2 ST-CI-QL20										
P1 MH060BAVF			MH BASE Custom Ht F/n							
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 60" - MH FLAT TOP SPEC. HT. (6") w/24"x36" Hole F/F - 6" P1) 60" - MH BASE Custom Ht F/n - 43" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 60" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) DOGHOUSE INVRTD - 44"x43" 3) MH Step ML-10-TDS-NCR - 10"					0 lb 1615 lb 5353 lb 442 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 7410 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.			
Rim: 475.97' Rim to Invert: 4.36' Slack: 0.07" Sump: 2.75" Step Position: 240										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	471.61'	0°	0"	36" HP STORM	41.5"	DOGHOUSE INVRTD 44"x43"	44" x 43"	49.393"	0"	0"
Invert 2	471.61'	155°	97.375"	36" HP STORM	41.5"	DOGHOUSE INVRTD 44"x43"	44" x 43"	49.393"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

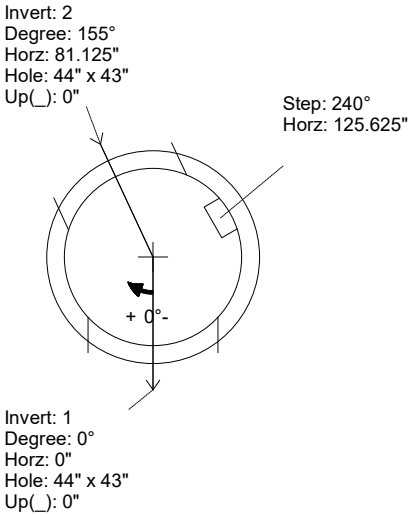

UPSIDE-DOWN VIEW (int. dimensions)

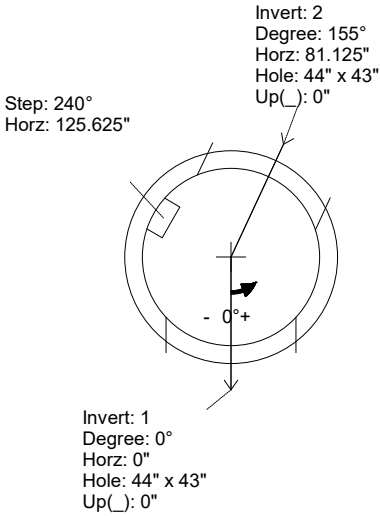

INSIDE WALL DIMENSIONS

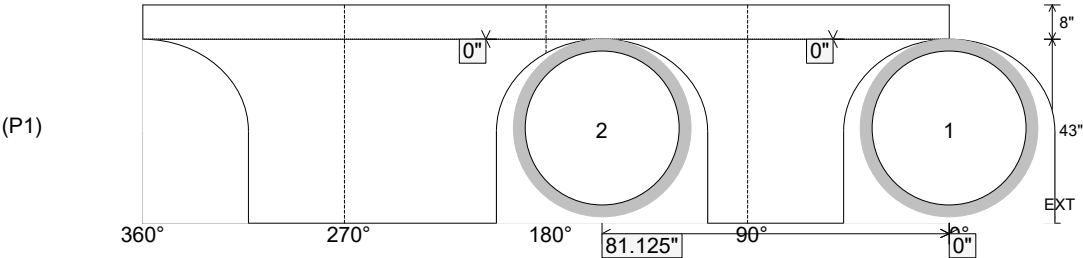

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 43" Height (Ext): 51"	Weight (Net): 5353 lb Volume (Net): 1.37cu.yd
----------------------------------	-------------------------------	--	--	--
