




Floor (Bot): 470.714'
Overall Height: 5.25'
Slack: 0.07"

	0 lb
	1615 lb
	5353 lb
	442 lb
	0 lb
	0 lb
	0 lb
	0 lb
	<u> </u>
Structure Total:	7410 lb

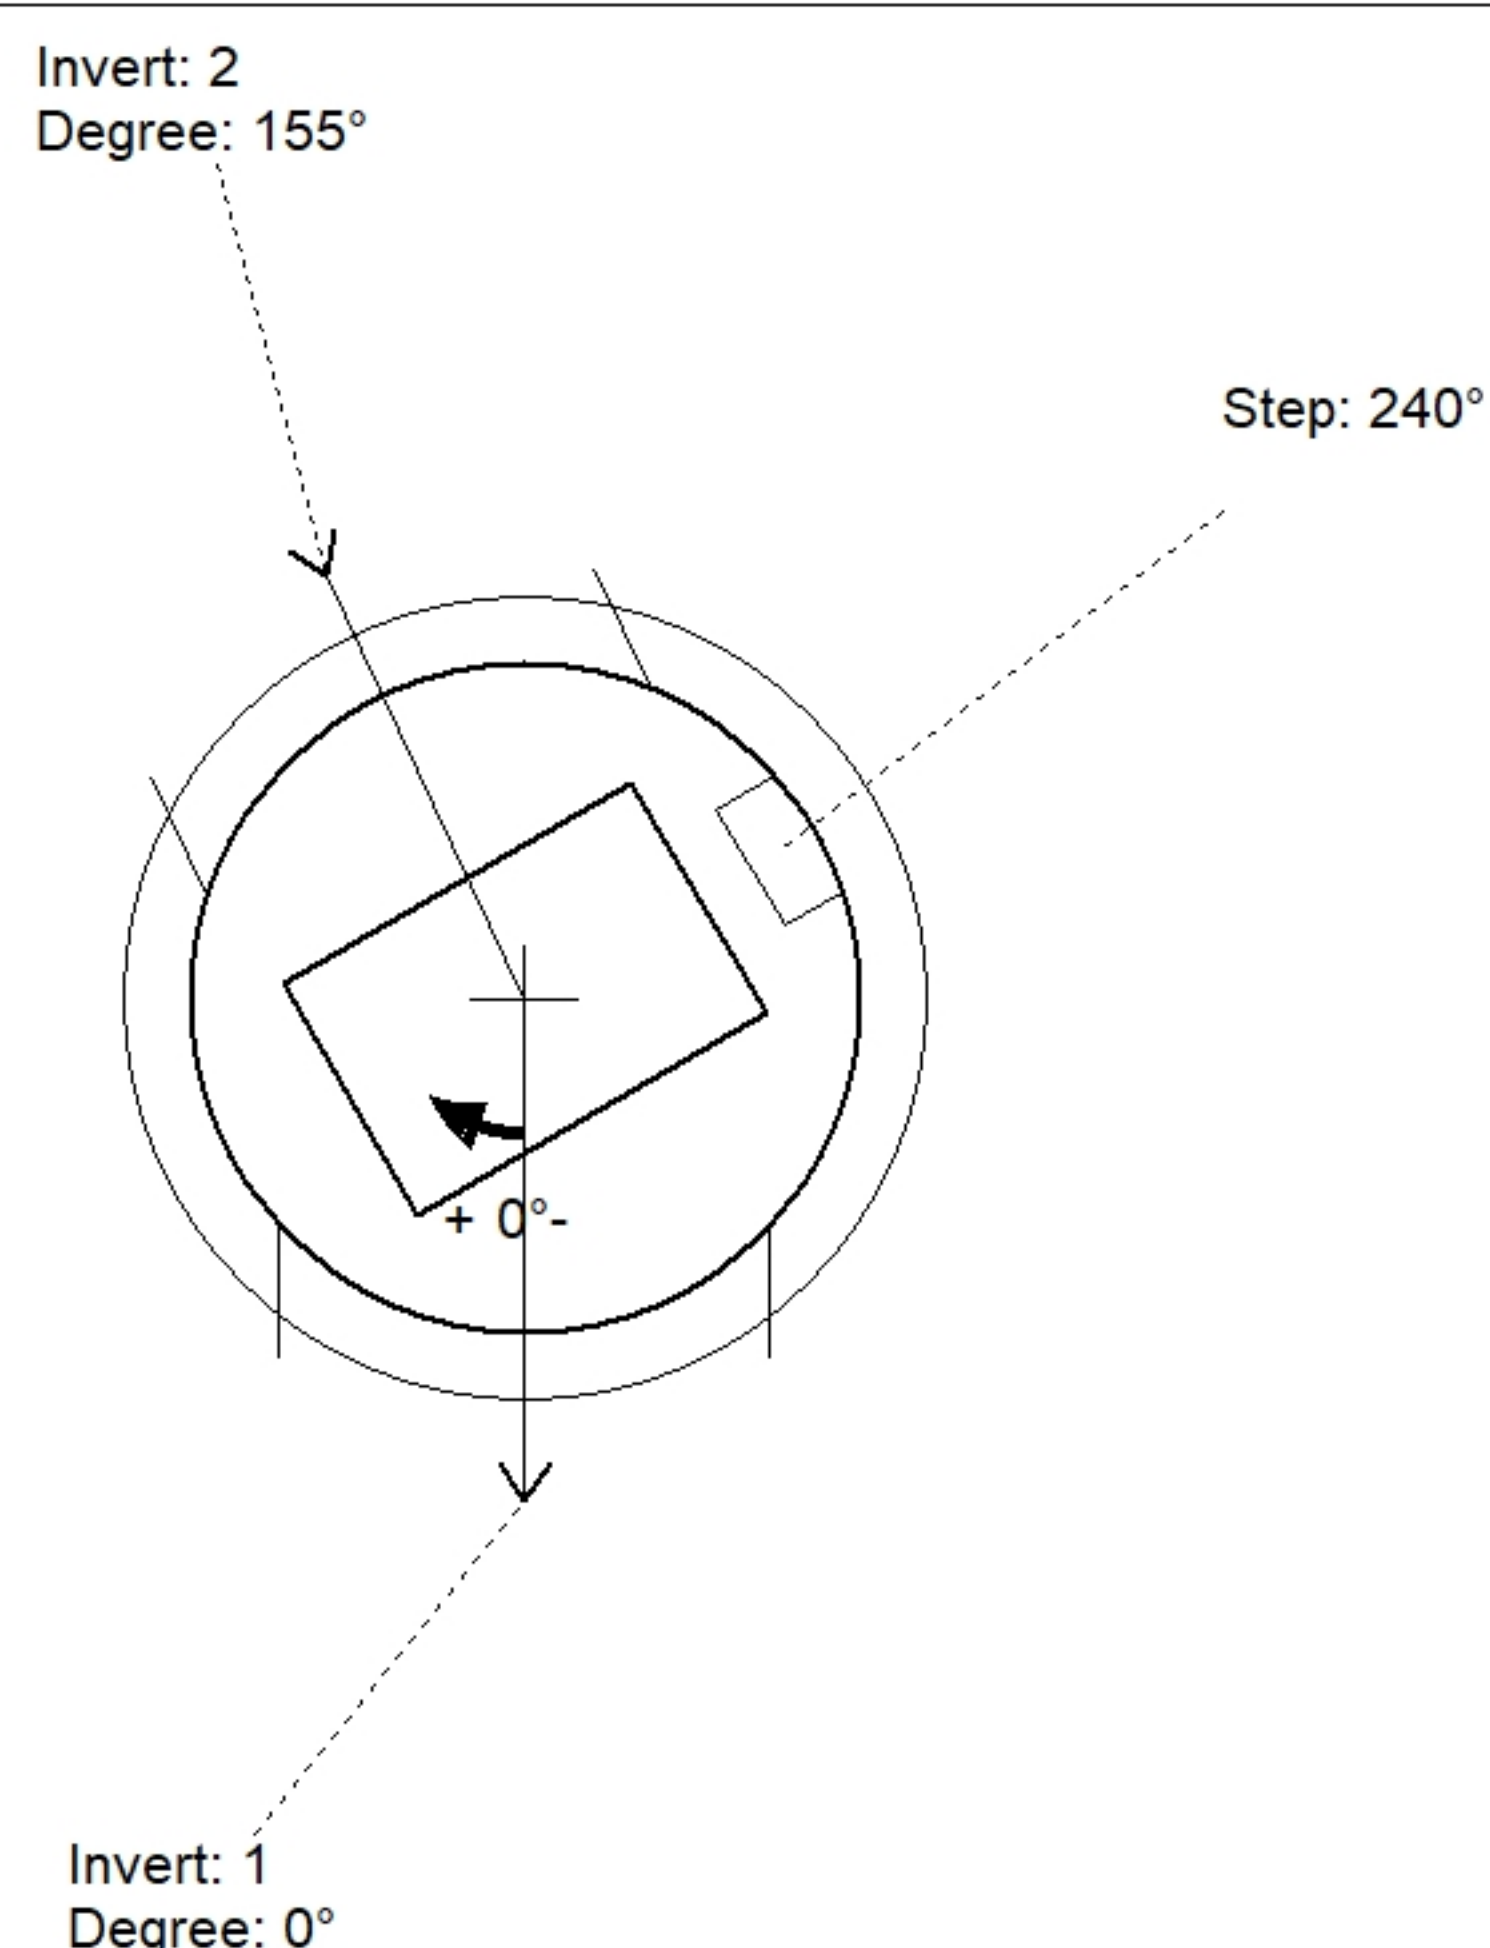


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	475.97'							
Reducer								
Invert 1	471.61'	0°	36" HP STORM	41.5"	44" x 43"	DOGHOUSE INVRTD 44"x43"	0"	P1
Invert 2	471.61'	155°	36" HP STORM	41.5"	44" x 43"	DOGHOUSE INVRTD 44"x43"	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

The diagram illustrates a manhole assembly with three distinct components. At the top is a hatched rectangular section labeled "24" x 36" - CASTING HEIGHT - 6" - (P3)". Below this is a white rectangular section labeled "60" - MH FLAT TOP SPEC. HT. (6") w/24"x36" Hole - 6" - (P2)". The bottom section is a large white rectangular area labeled "60" - MH BASE Custom Ht - 43" - (P1)". Dashed lines indicate the vertical alignment and boundaries between these components.

24" x 36" - CASTING HEIGHT - 6" - (P3)

60" - MH FLAT TOP SPEC. HT. (6") w/24"x36" Hole - 6" - (P2)

60" - MH BASE Custom Ht - 43" - (P1)

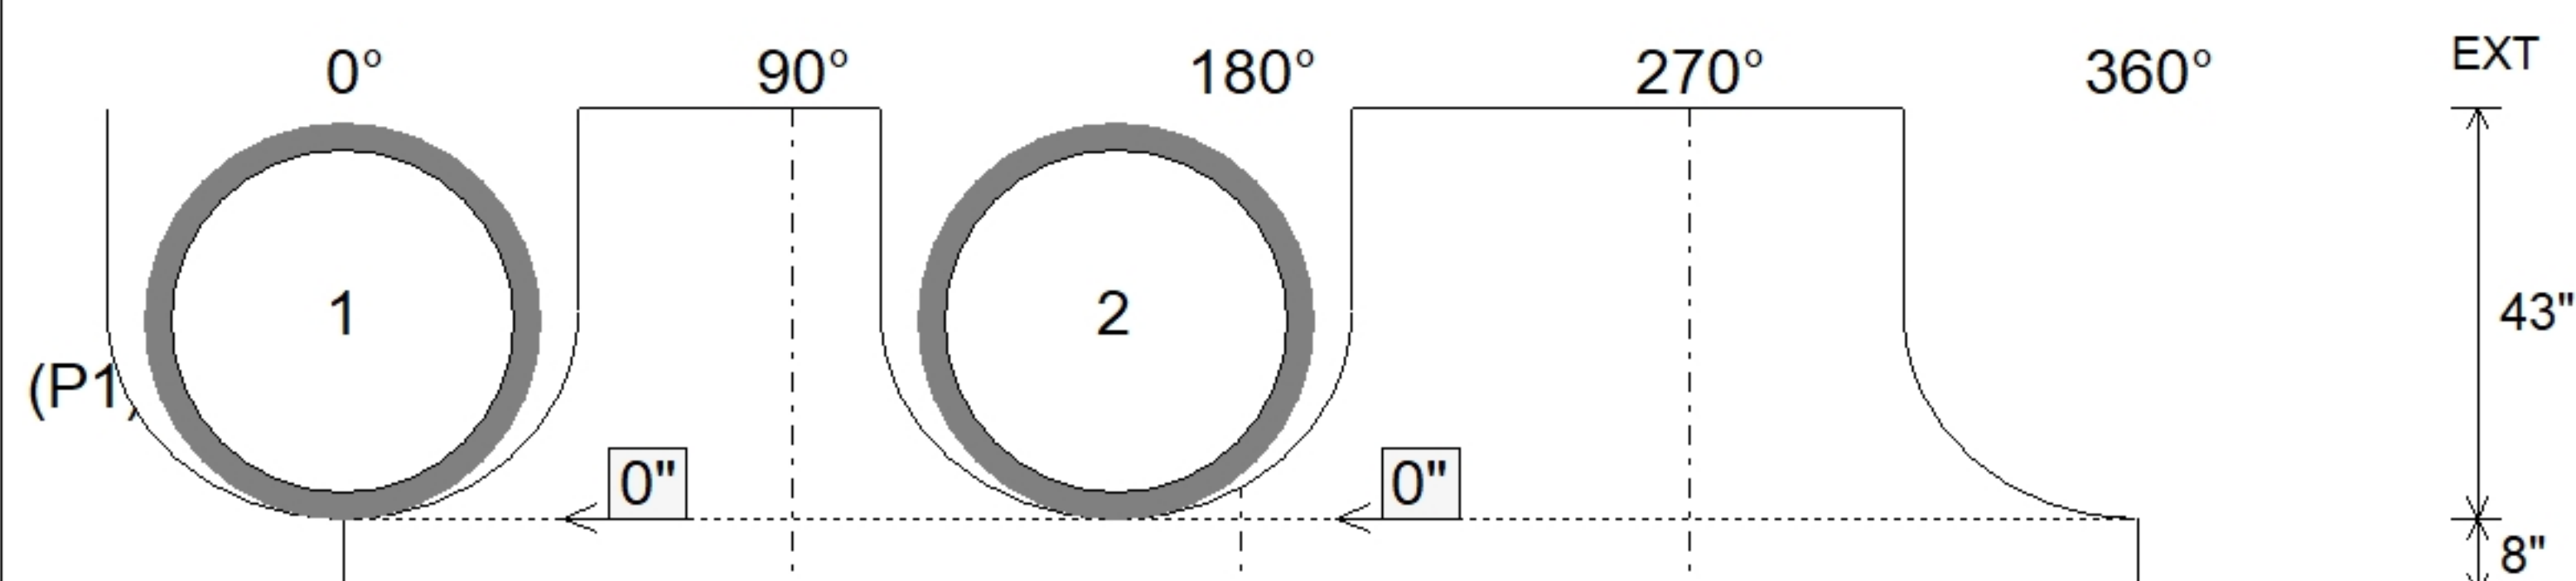

SUBMITTAL
APPROVED BY:
