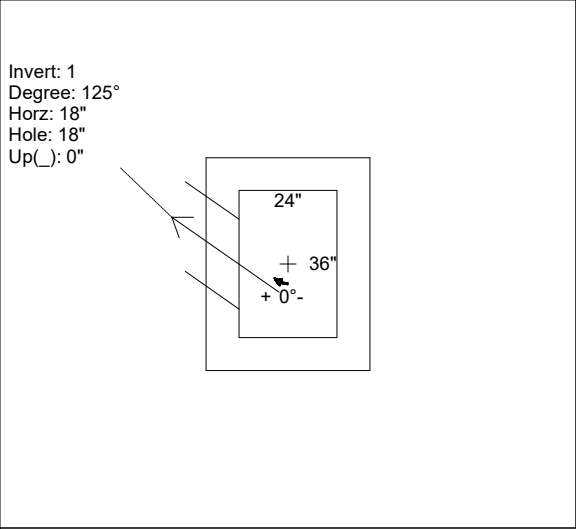
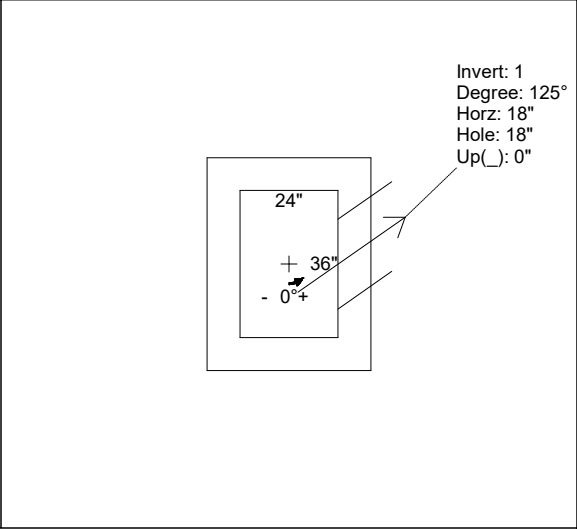
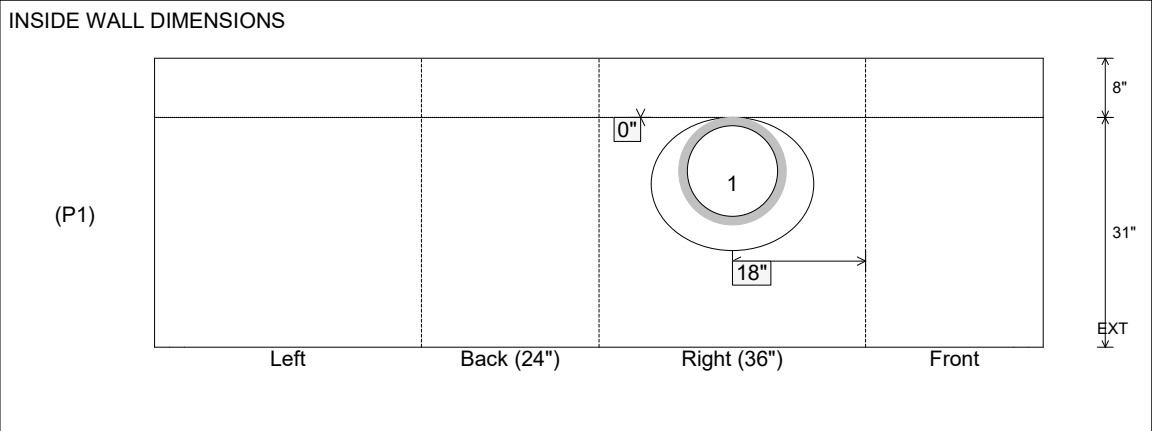


Job Name: 26-2756 - Lofts at Cadiz Job Location: Cadiz, KY 42241 Contractor: BTM Excavating, LLC				Plant: 100 9/17/2026 10:47:23 PM		Tech: Jared - F PC: T. Lewis					
Structure ID: CBI-4 ST-CI											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht F/n							
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 31" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18"				0 lb 4351 lb 442 lb 0 lb 0 lb ----- Structure Total: 4793 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.					
Rim: 477.58'				Rim to Invert: 3'		Slack: 0.125"		Sump: 1.125"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	474.58'	125°	31.625"	12" HP STORM	14.5"	Hole 18	18"	21.974"	0"	-6.9"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)  											
INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 31" Height (Ext): 39"		Weight (Net): 4351 lb Volume (Net): 1.11cu.yd		
