




Job Name: 26-2756 - Lofts at Cadiz Job Location: Cadiz, KY 42241 Contractor: BTM Excavating, LLC					Plant: 100 9/17/2026 10:47:10 PM		Tech: Jared - F PC: T. Lewis				
Structure ID: CBI-5 ST-CI											
P1 MH048BA36		MH BASE T/n									
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12" P1) 48" - MH BASE T/n - 36" 1) CASTING - HOE 525 LV SET (F/G/H) 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 18 3) MH Step ML-10-TDS-NCR - 10"					0 lb 1300 lb 3601 lb 442 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5343 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 LV SET (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 484.91' Rim to Invert: 4.63' Slack: 2.86" Sump: 1.3" Step Position: 90											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	480.28'	0°	0"	15" HP STORM	17.7"	Hole 20	20"	20.629"	0"	0"	
Invert 2	480.28'	209°	105.75"	12" HP STORM	14.5"	Hole 18	18"	18.451"	0.125"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

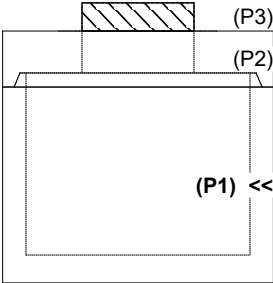


RIGHT-SIDE UP VIEW (int. dimensions)

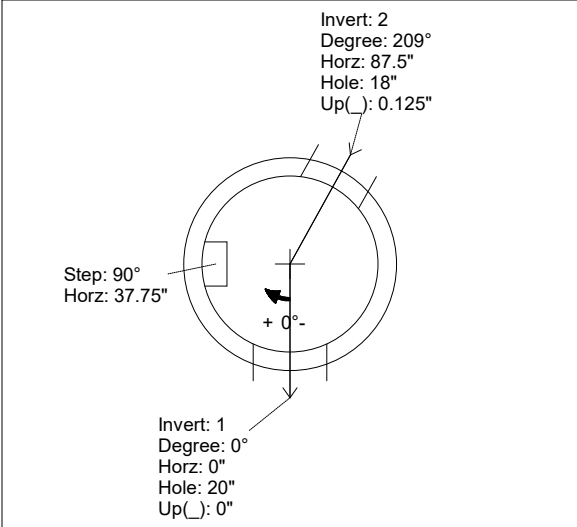

UPSIDE-DOWN VIEW (int. dimensions)

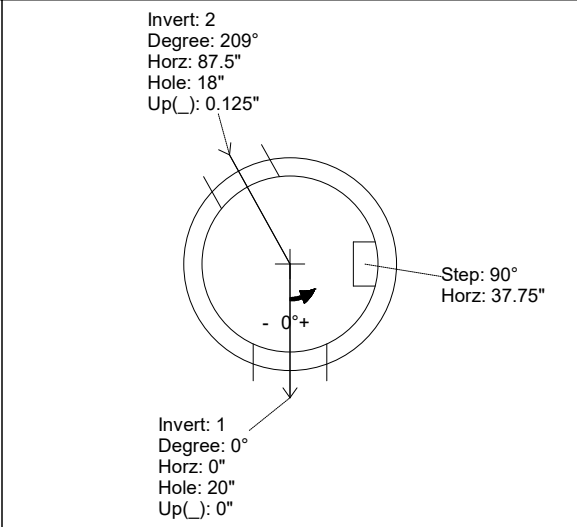

INSIDE WALL DIMENSIONS

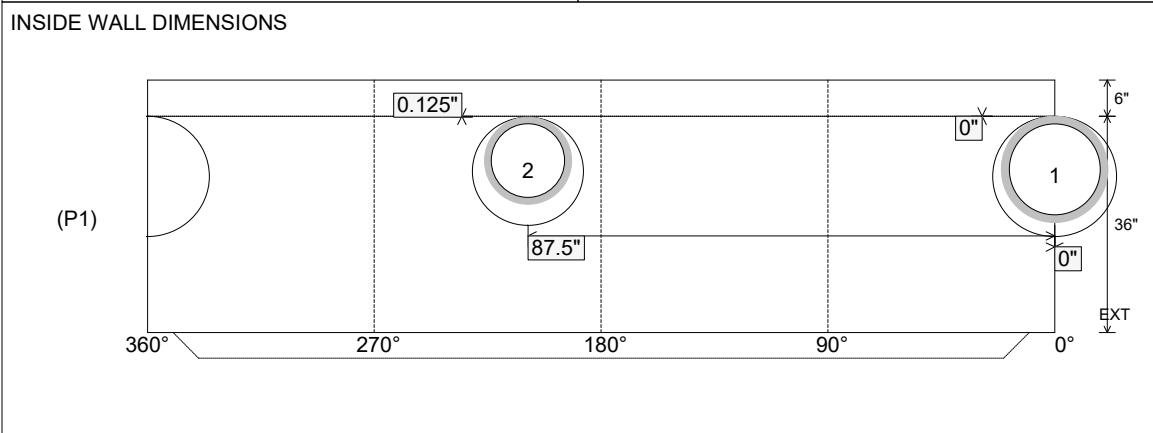

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3601 lb Volume (Net): 0.92cu.yd
----------------------------------	---------------------------------	--	--	--
