



Job Name: 26-2756 - Lofts at Cadiz Job Location: Cadiz, KY 42241 Contractor: BTM Excavating, LLC				Plant: 100 9/17/2026 10:47:13 PM		Tech: Jared - F PC: T. Lewis				
Structure ID: DBI-2 ST-DBI										
P1 BX2424-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n						
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 28" 1) CASTING - HOE-326-BH F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole (CMP Ellipt.) - 23"x19"						0 lb 3250 lb 289 lb 0 lb 0 lb ----- 3539 lb Structure Total:		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE-326-BH F/G)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.		
Rim: 481.6' Rim to Invert: 2.67' Slack: 0.54" Sump: 0.5" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	478.93'	0°	20"	20" x 16" CMP ELLIP.	21" x 17"	Hole (CMP Ellipt.) 23"x19"	23" x 19"	23"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

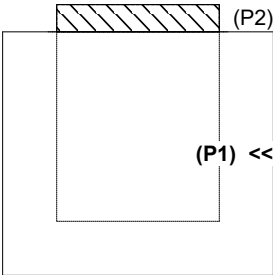

(P2)


(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)



Invert: 1
Degree: 0°
Horz: 12"
Hole: 23" x 19"
Up(): 0"


UPSIDE-DOWN VIEW (int. dimensions)



Invert: 1
Degree: 0°
Horz: 12"
Hole: 23" x 19"
Up(): 0"

INSIDE WALL DIMENSIONS

(P1)

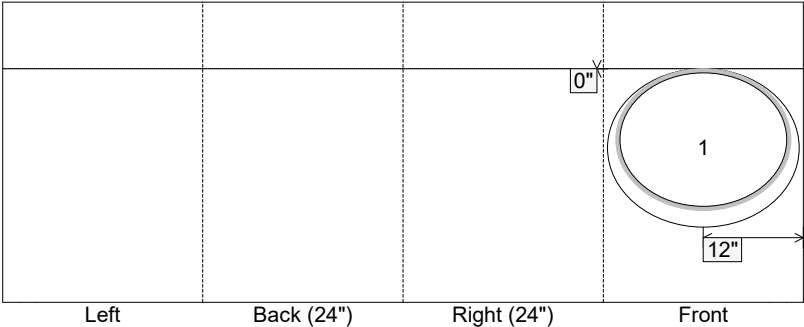

Left Back (24") Right (24") Front

8"

28"

EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 28" Height (Ext): 36"	Weight (Net): 3250 lb Volume (Net): 0.83cu.yd
----------------------------------	-------------------------------	--	--	--
