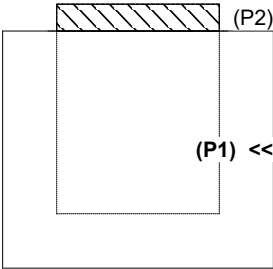
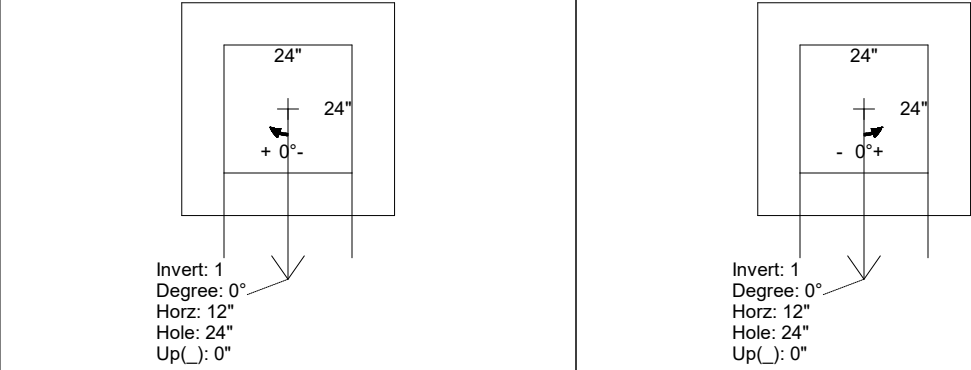
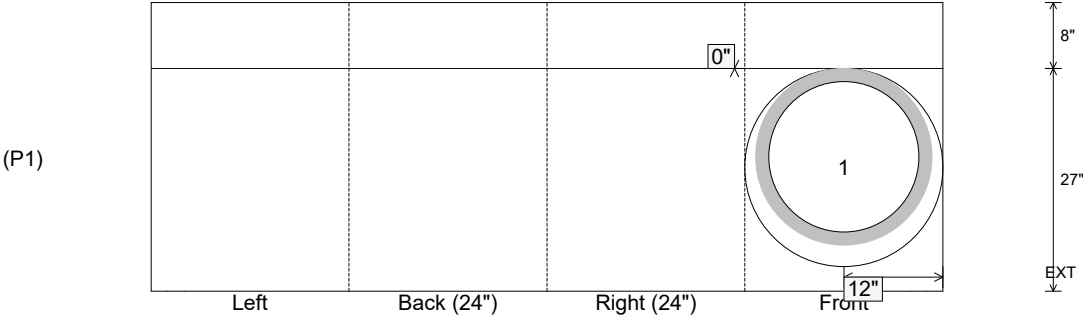


Job Name: 26-2756 - Lofts at Cadiz Job Location: Cadiz, KY 42241 Contractor: BTM Excavating, LLC				Plant: 100 9/17/2026 10:47:16 PM		Tech: Jared - F PC: T. Lewis					
Structure ID: DBI-5 ST-DBI											
P1 BX2424-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n							
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 27" 1) CASTING - HOE-326-BH F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 24				0 lb 3166 lb 289 lb 0 lb 0 lb ----- Structure Total: 3455 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE-326-BH F/G). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.					
Rim: 479.8' Rim to Invert: 2.5' Slack: 0.625" Sump: 1.625" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	477.3'	0°	20"	18" HP STORM	21.4"	Hole 24	24"	24"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 27" Height (Ext): 35"		Weight (Net): 3166 lb Volume (Net): 0.81cu.yd	
