




Job Name: 26-2756 - Lofts at Cadiz Job Location: Cadiz, KY 42241 Contractor: BTM Excavating, LLC				Plant: 100 9/17/2026 10:47:22 PM		Tech: Jared - F PC: T. Lewis				
Structure ID: DBI-6 ST-DBI										
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht F/n						
P3) 24" x 30" - CASTING HEIGHT - 3.75" P2) 24" x 36" - BX FLAT LID 8inW w/24"x30" HOLE F/F - 8" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 22" 1) CASTING - HOE KY-460-11 F/G (DBI 11) 1) 24" x 36" - Conseal CS-102 1.00" 1) 24" x 30" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 24"x21.75" 1) Hole - 20				0 lb 913 lb 3044 lb 421 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4378 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE KY-460-11 F/G). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 476.21' Rim to Invert: 2.73' Slack: 0.635' Sump: 1.625' Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	473.48'	305°	31.5"	18" HP STORM	21.4"	DOGHOUSE INVRTD 24"x21.75"	24" x 21.75"	29.299"	0"	-7"
Invert 2	473.48'	90°	26"	15" HP STORM	17.7"	Hole 20	20"	20"	0.375"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

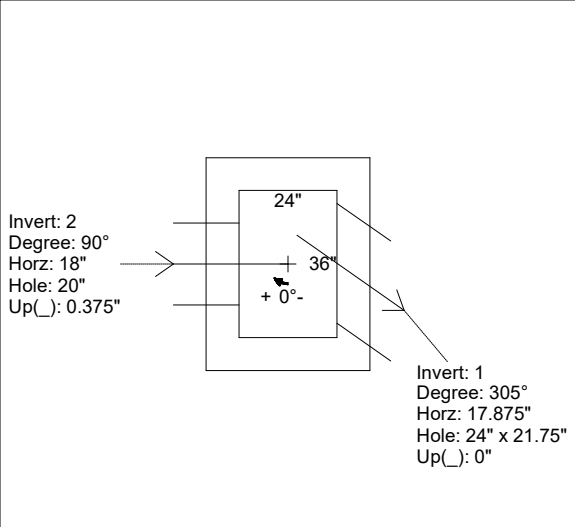

RIGHT-SIDE UP VIEW (int. dimensions)

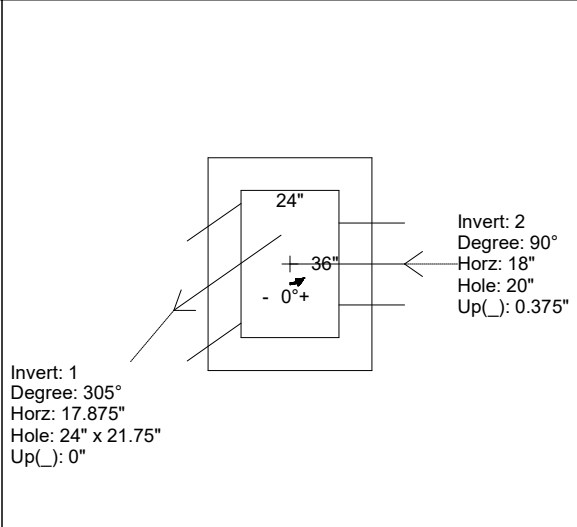


UPSIDE-DOWN VIEW (int. dimensions)

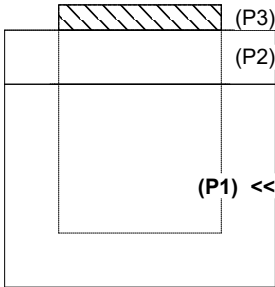

(P1) <<

INSIDE WALL DIMENSIONS



(P1)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 22" Height (Ext): 30"	Weight (Net): 3044 lb Volume (Net): 0.78cu.yd
----------------------------------	-------------------------------	--	--	--
