




Job Name: 26-2756 - Lofts at Cadiz Job Location: Cadiz, KY 42241 Contractor: BTM Excavating, LLC				Plant: 100 9/17/2026 10:47:19 PM		Tech: Jared - F PC: T. Lewis				
Structure ID: DBI-7 ST-DBI										
P1 BX2424-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n						
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 28" 1) CASTING - HOE-326-BH F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 18				0 lb 3098 lb 289 lb 0 lb 0 lb 0 lb ----- Structure Total: 3387 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE-326-BH F/G). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 476.2' Rim to Invert: 2.57' Slack: 0.09" Sump: 1.25" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	473.63'	0°	20"	15" HP STORM	17.7"	Hole 20	20"	20"	0"	0"
Invert 2	473.63'	180°	20"	12" HP STORM	14.5"	Hole 18	18"	18"	0.125"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

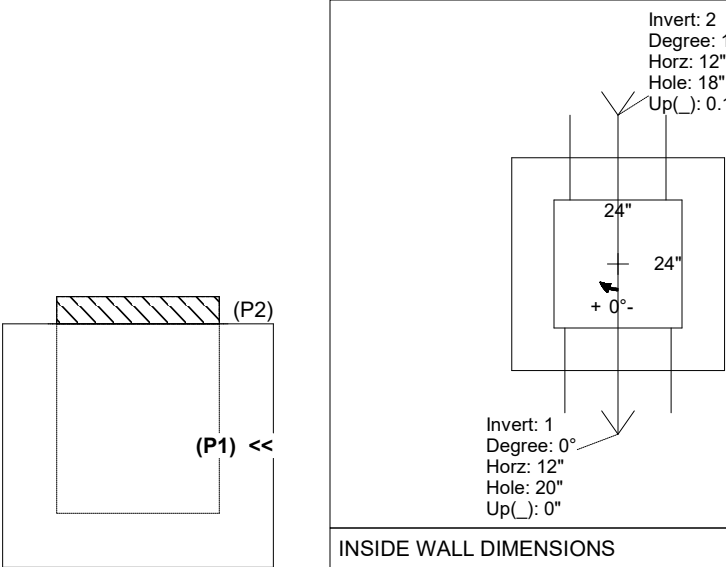

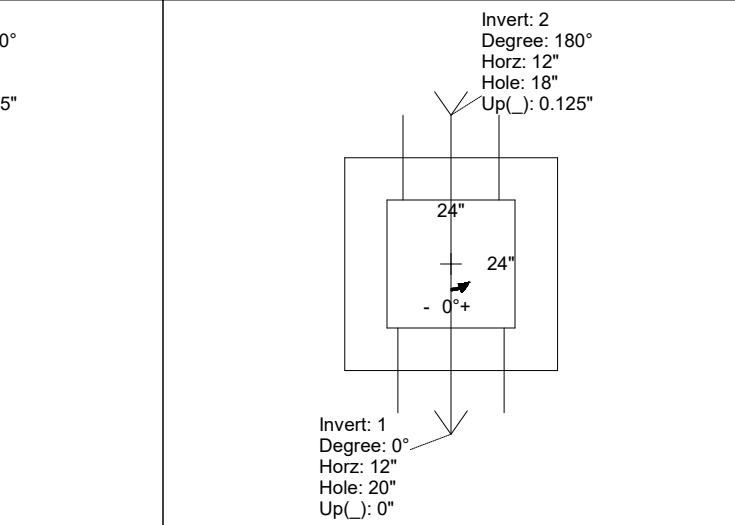

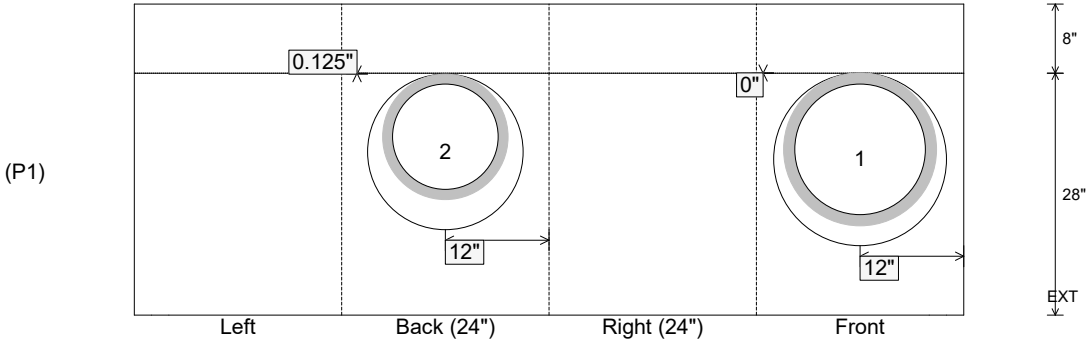

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 28" Height (Ext): 36"	Weight (Net): 3098 lb Volume (Net): 0.79cu.yd
----------------------------------	-------------------------------	--	--	--
