




Job Name: 26-2756 - Lofts at Cadiz Job Location: Cadiz, KY 42241 Contractor: BTM Excavating, LLC				Plant: 100 9/17/2026 10:47:20 PM		Tech: Jared - F PC: T. Lewis				
Structure ID: DBI-8 ST-DBI										
P1 BX2424-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n						
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 17" 1) CASTING - HOE-326-BH F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 18"x17"						0 lb 2351 lb 289 lb 0 lb 0 lb ----- Structure Total: 2640 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE-326-BH F/G) . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.		
Rim: 476.2' Rim to Invert: 1.7' Slack: 0.525" Sump: 1.125" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	474.5'	0°	20"	12" HP STORM	14.5"	DOGHOUSE INVRTD 18"x17"	18" x 17"	18"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										



Invert: 1
Degree: 0°
Horz: 12"
Hole: 18" x 17"
Up(): 0"



Invert: 1
Degree: 0°
Horz: 12"
Hole: 18" x 17"
Up(): 0"

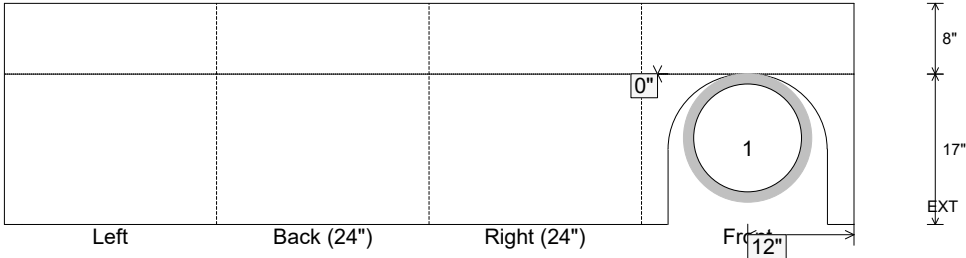

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 17" Height (Ext): 25"	Weight (Net): 2351 lb Volume (Net): 0.6cu.yd
----------------------------------	-------------------------------	--	--	---
