




Job Name: 26-2756 - Lofts at Cadiz Job Location: Cadiz, KY 42241 Contractor: BTM Excavating, LLC				Plant: 100 9/17/2026 10:47:24 PM		Tech: Jared - F PC: T. Lewis				
Structure ID: MH-2 ST-MH										
P1 MH048BAVF		MH BASE Custom Ht F/n								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 47" 1) CASTING - HOE MC-315 F/C Storm 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) Hole - 30 1) DOGHOUSE INVRTD - 20"x21" 1) DOGHOUSE INVRTD - 32"x31" 1) Hole - 18 4) MH Step ML-10-TDS-NCR - 10"						0 lb 1286 lb 3622 lb 258 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 5166 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE MC-315 F/C STORM). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 478.45'		Rim to Invert: 4.99'		Slack: 0.83"		Sump: 1.95"		Step Position: 243°		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	473.46'	0°	0"	24" HP STORM	28"	Hole 30	30"	32.406"	0"	0"
Invert 2	475.57'	90°	45.5"	15" HP STORM	17.7"	DOGHOUSE INVRTD 20"x21"	20" x 21"	20.629"	26"	0"
Invert 3	474.78'	180°	91.125"	24" HP STORM	28"	DOGHOUSE INVRTD 32"x31"	32" x 31"	35.027"	15.875"	0"
Invert 4	474.46'	305°	149.375"	12" HP STORM	14.5"	Hole 18	18"	18.967"	12.75"	-5"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

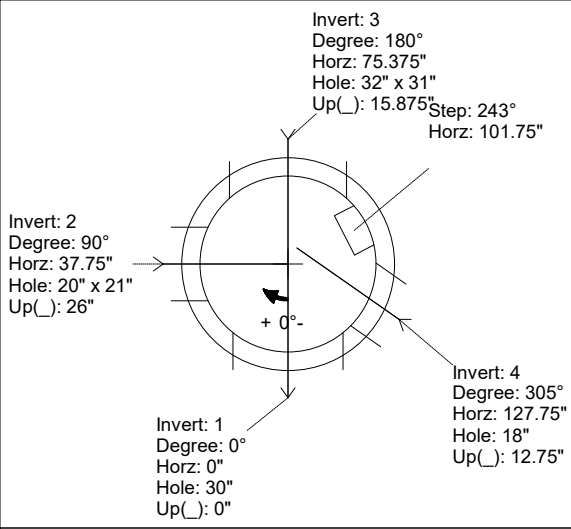

RIGHT-SIDE UP VIEW (int. dimensions)

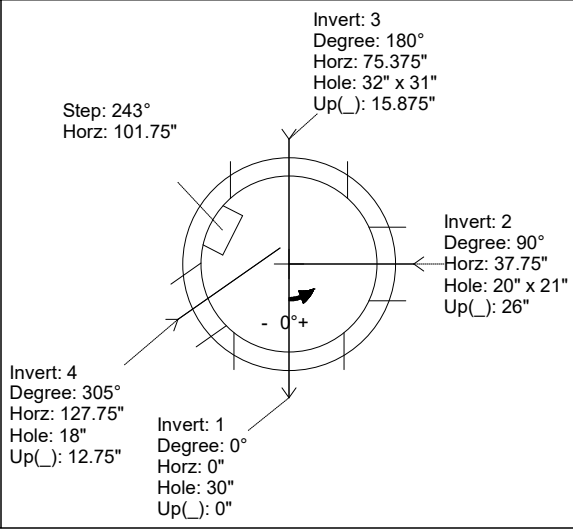

UPSIDE-DOWN VIEW (int. dimensions)

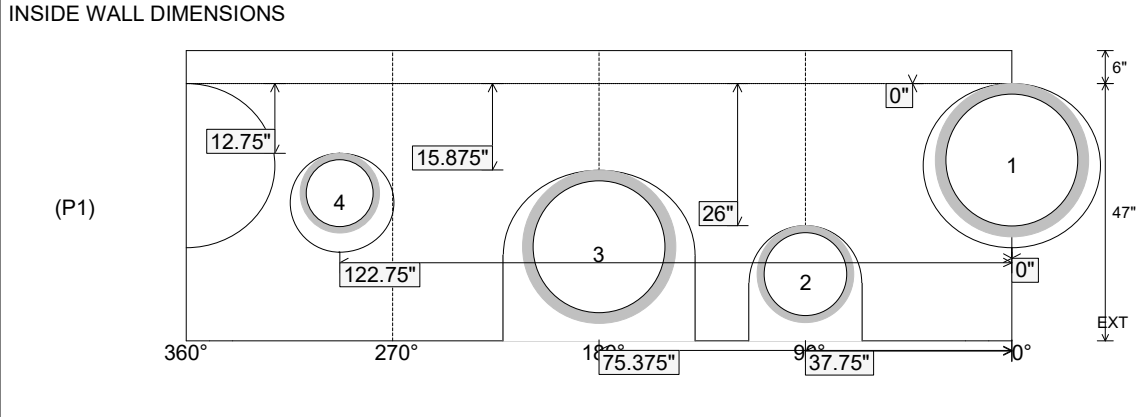

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 47" Height (Ext): 53"	Weight (Net): 3622 lb Volume (Net): 0.92cu.yd
----------------------------------	-------------------------------	--	--	--
