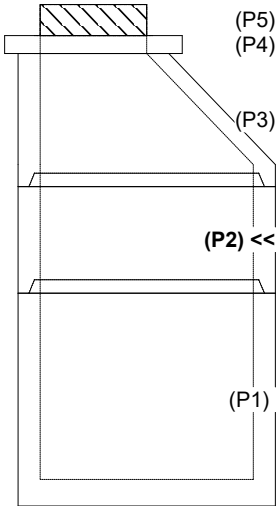




Job Name: 26-2756 - Lofts at Cadiz Job Location: Cadiz, KY 42241 Contractor: BTM Excavating, LLC					Plant: 100 9/15/2026 9:01:47 PM		Tech: Jared - F PC: T. Lewis						
Structure ID: SSMH-D SS-MH													
P2		MH048RS24		MH RISER T/G									
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING F/F - 4" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER T/G - 24" P1) 48" - MH BASE T/h - 42" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 8) MH Step ML-10-TDS-NCR - 10" Structure Total: 9879 lb						0 lb 270 lb 2050 lb 1677 lb 4169 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 0 lb 16 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-315 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #4 BARS AT 12" C.C.E.W.					
Rim: 482.91'		Rim to Invert: 8.88'		Slack: 1.56"		Sump: 2"		Step Position: 0°					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 24" Height (Ext): 24"		Weight (Net): 1677 lb Volume (Net): 0.43cu.yd				
