



Job Name: 26-2763 - The Flats of Martin Job Location: Paris, TN 38242 Contractor: BTM Excavating, LLC					Plant: 100 7/14/2026 11:10:25 AM		Tech: Jared - F PC: T. Lewis				
Structure ID: 2 ST-AD											
P1 BX28280606VH		BOX BASE 6inW, 6inF, Variable Ht F/n									
P2) 28" x 28" - CASTING HEIGHT - 6" P1) 28" x 28" - BOX BASE 6inW, 6inF, Variable Ht F/n - 25" 1) CASTING - JBS 4310 F/G 1) 28" x 28" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 18					0 lb 2231 lb 500 lb 0 lb 0 lb 0 lb ----- Structure Total: 2731 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (JBS 4310 F/G). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 353.8' Rim to Invert: 2.5' Slack: 0.25" Sump: 1.25" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	351.3'	0°	20"	15" HP STORM	17.7"	Hole 20	20"	20"	0"	0"	
Invert 2	351.3'	180°	20"	12" HP STORM	14.5"	Hole 18	18"	18"	0.125"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

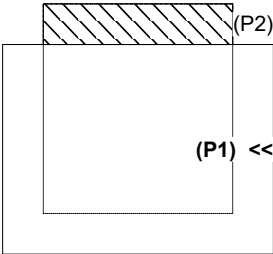

(P1) << (P2)


RIGHT-SIDE UP VIEW (int. dimensions)

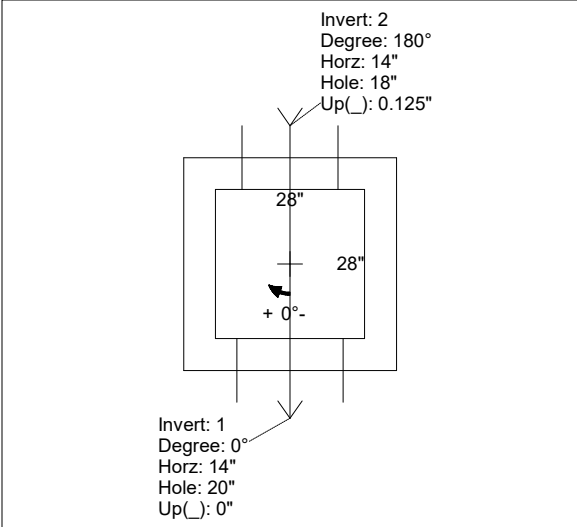

Invert: 2
Degree: 180°
Horz: 14"
Hole: 18"
Up(): 0.125"

Invert: 1
Degree: 0°
Horz: 14"
Hole: 20"
Up(): 0"


UPSIDE-DOWN VIEW (int. dimensions)

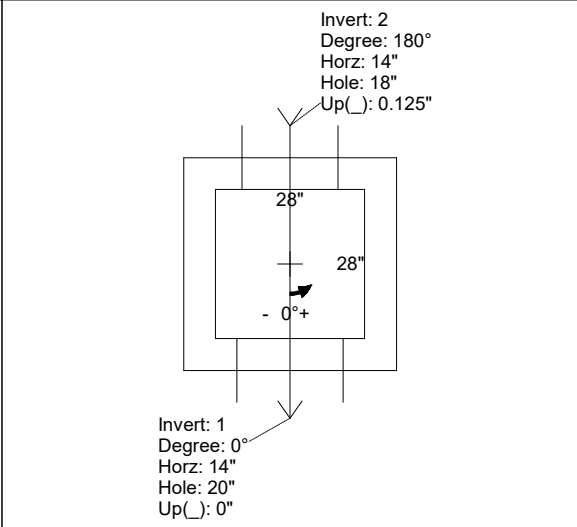

Invert: 2
Degree: 180°
Horz: 14"
Hole: 18"
Up(): 0.125"

Invert: 1
Degree: 0°
Horz: 14"
Hole: 20"
Up(): 0"

INSIDE WALL DIMENSIONS

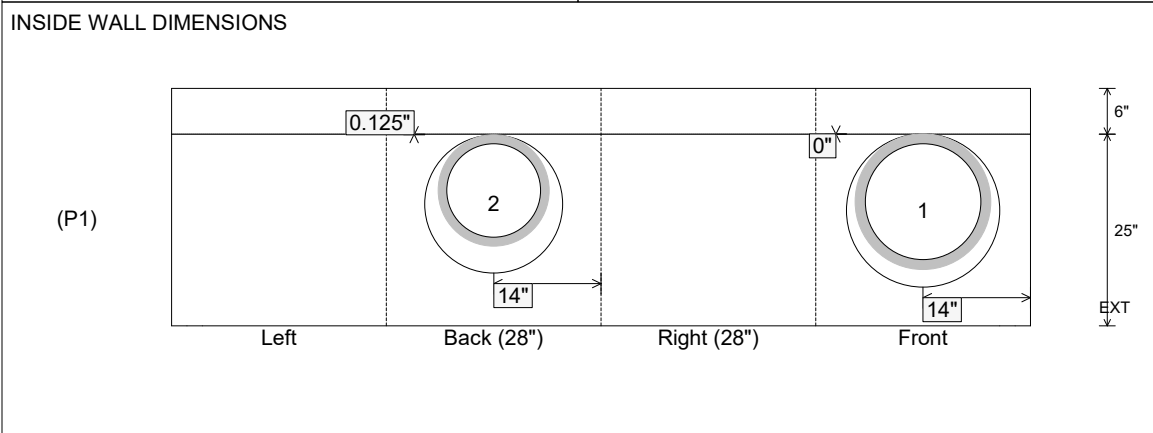

(P1)

Left Back (28") Right (28") Front

0.125" 14" 14" 25" 6" EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 6"	Height (Int): 25" Height (Ext): 31"	Weight (Net): 2231 lb Volume (Net): 0.57cu.yd
----------------------------------	-------------------------------	--	--	--
