

Contractor: BTM Excavating, LLC

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 5.68'

Floor Height: 6"



Slack: 0.16"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

2) PSX - 12-08 NYLO


16 lb

Structure Total: 7071 lb

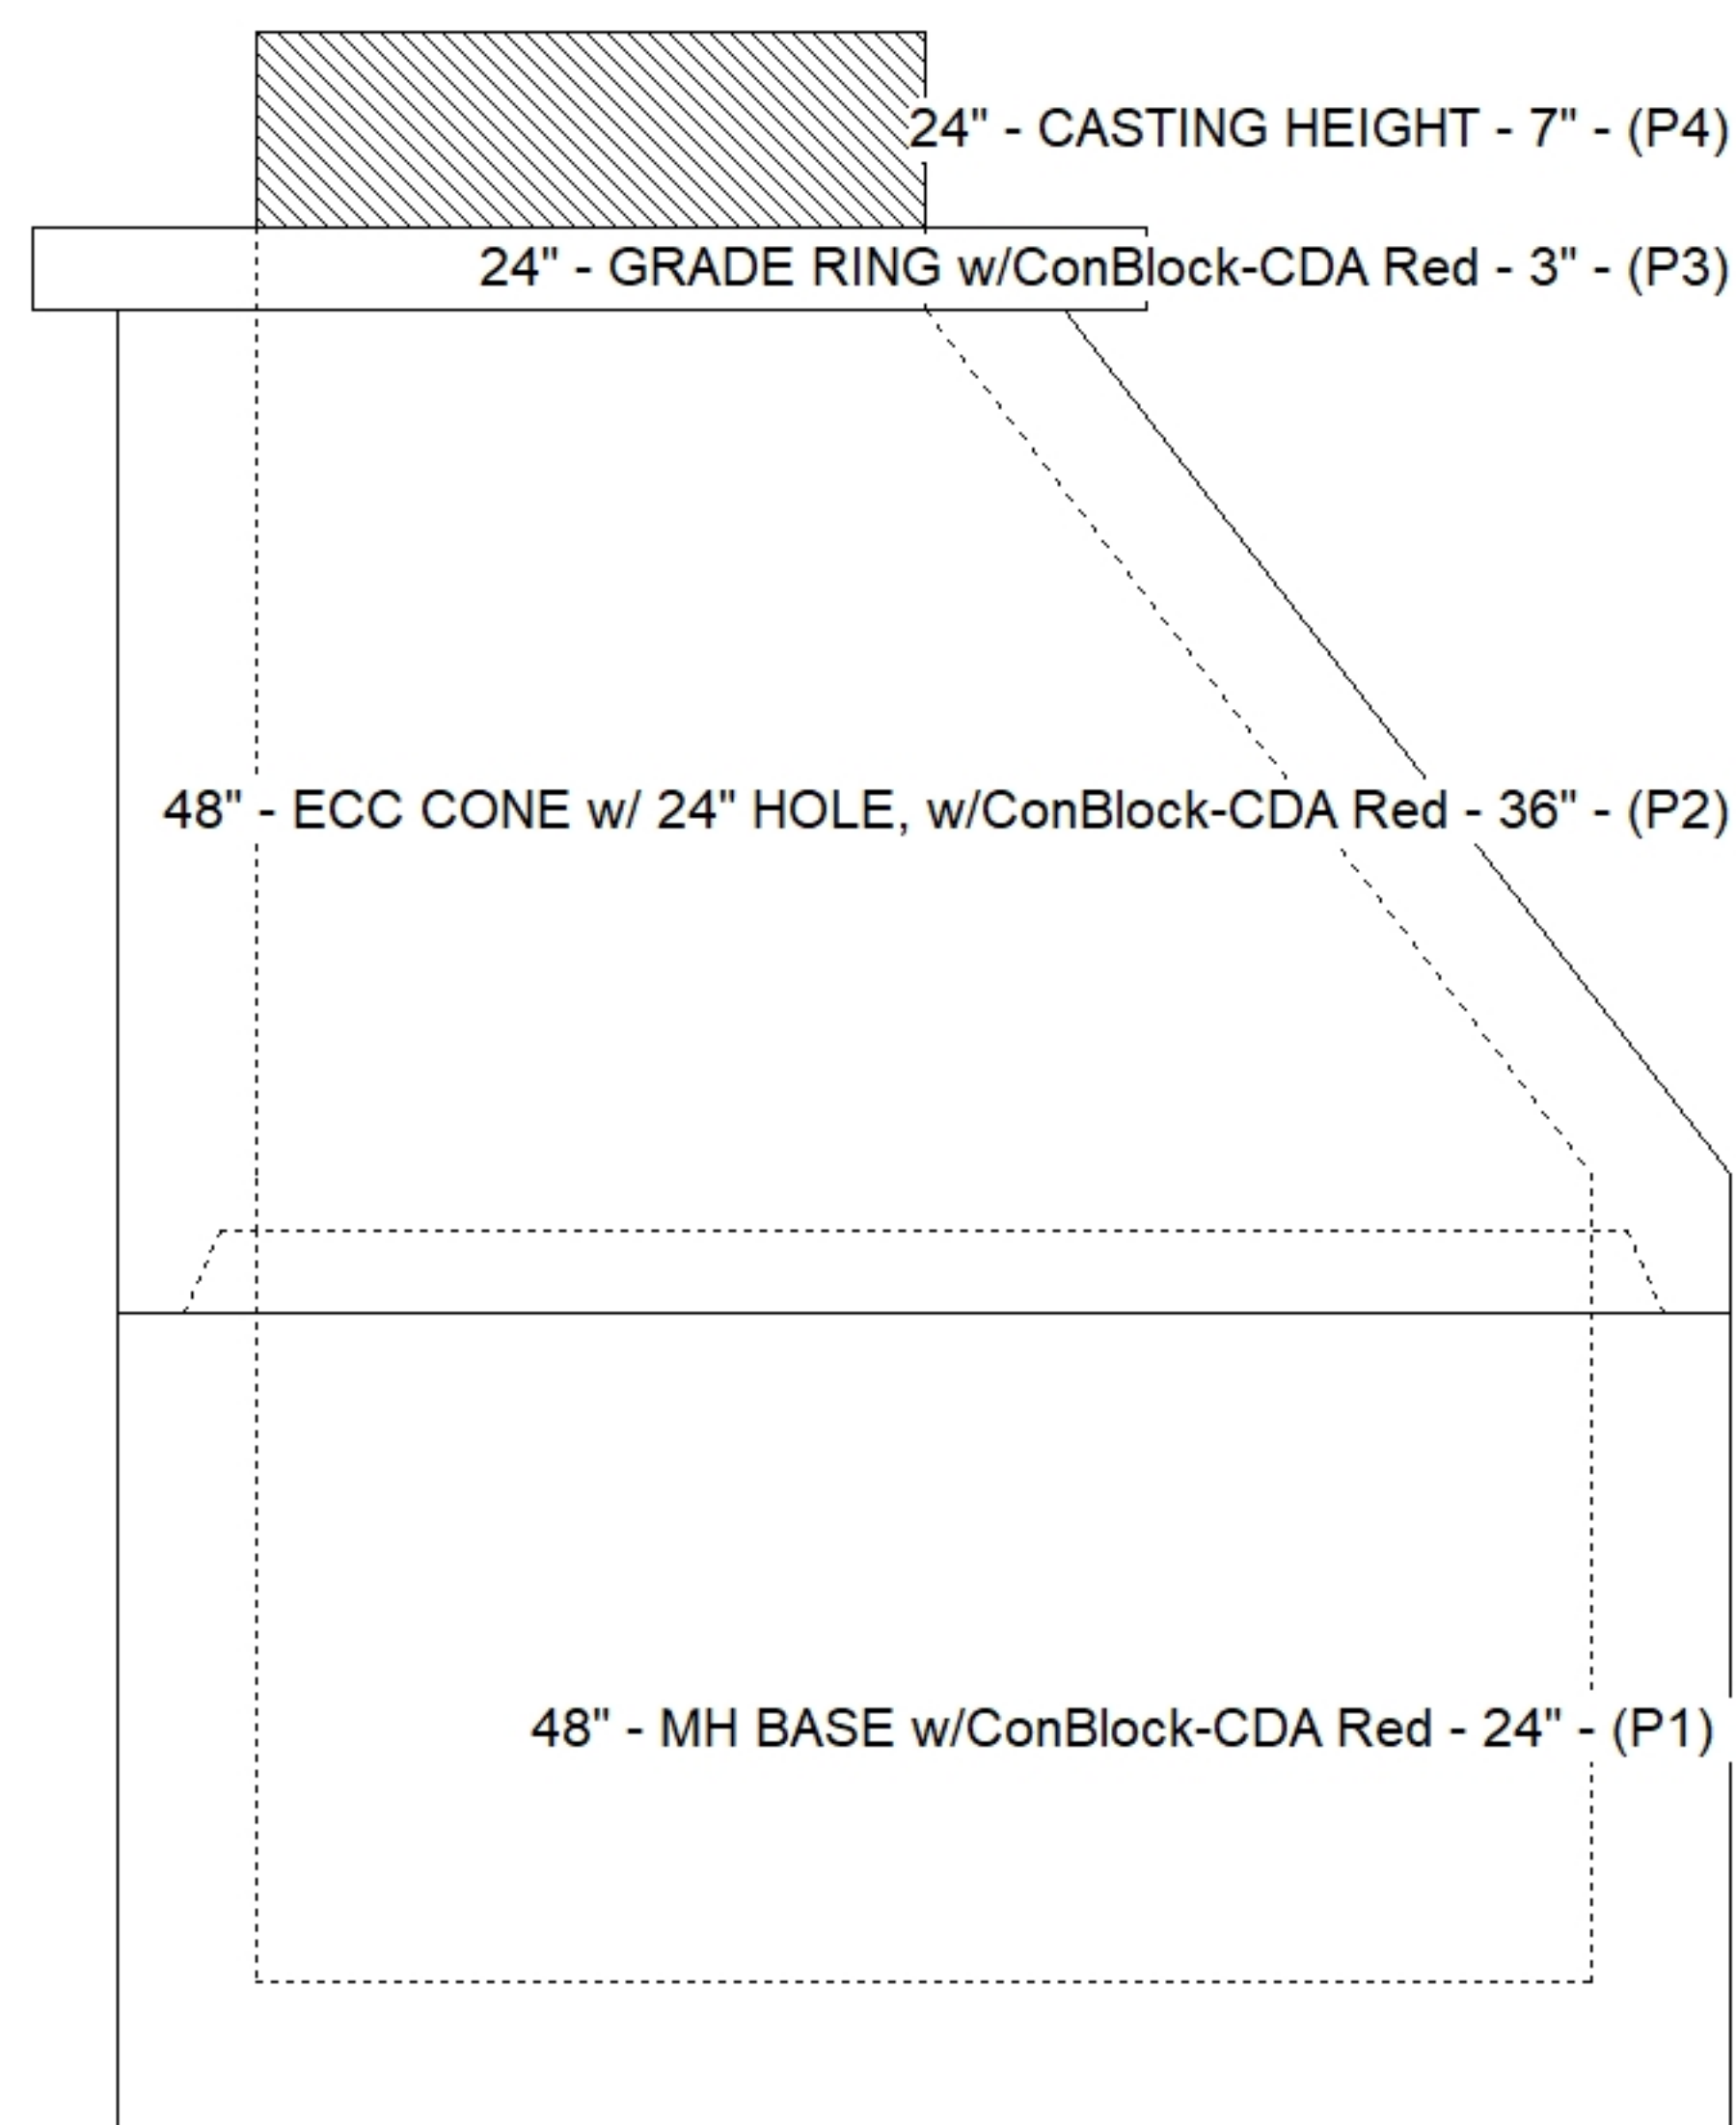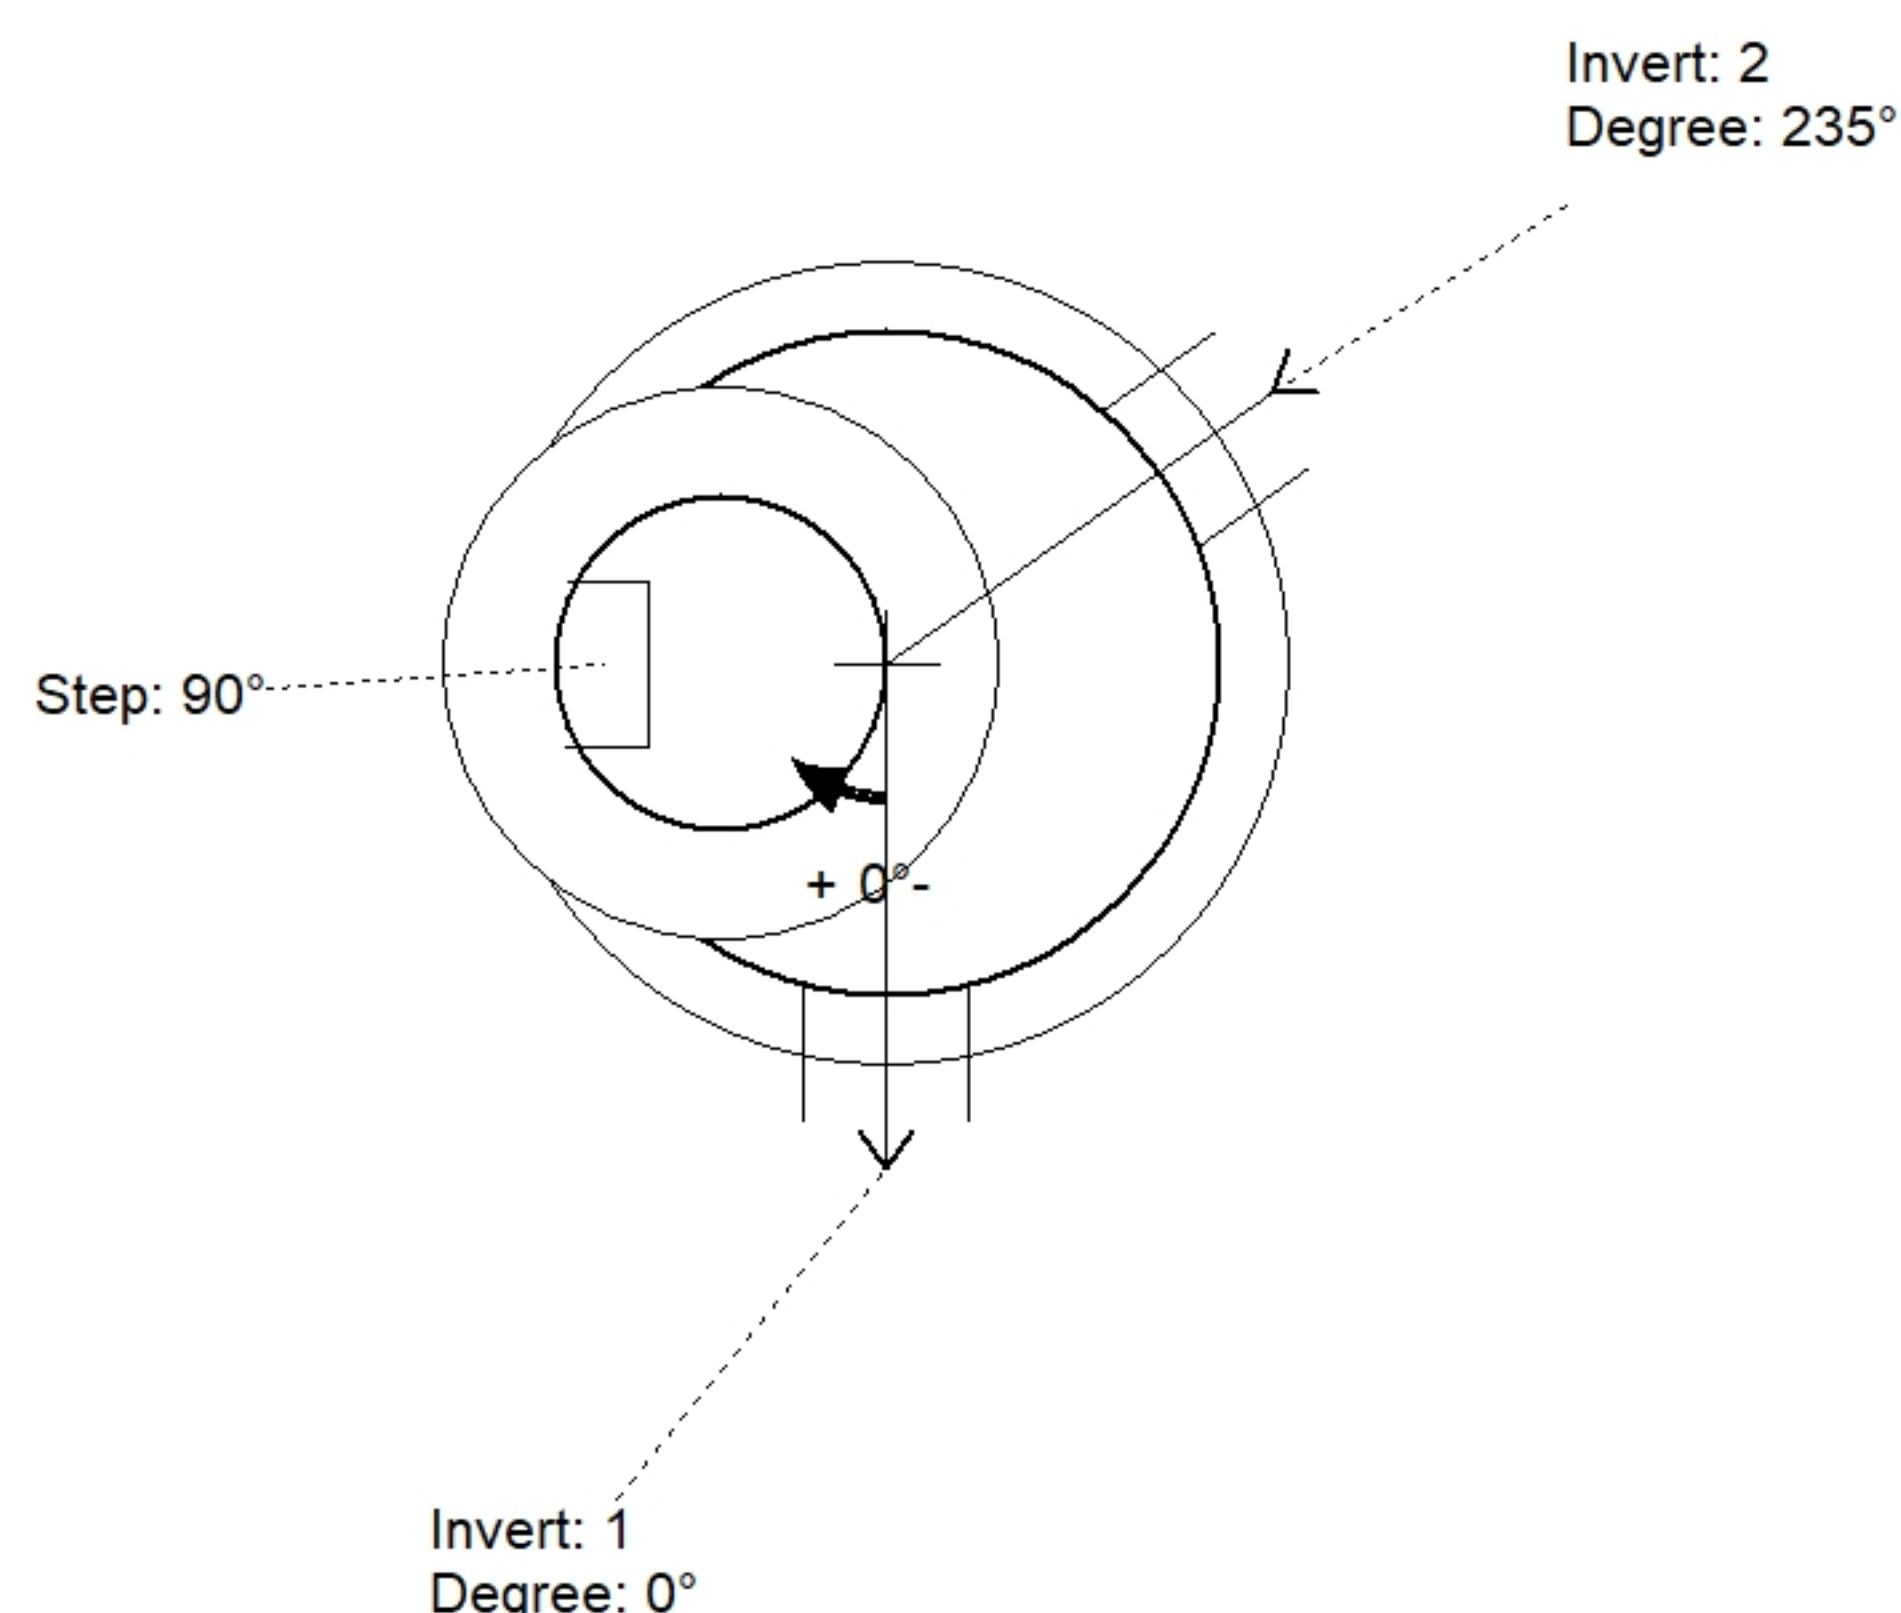

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	357.2'							
Reducer								
Invert 1	351.52'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	351.62'	235°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

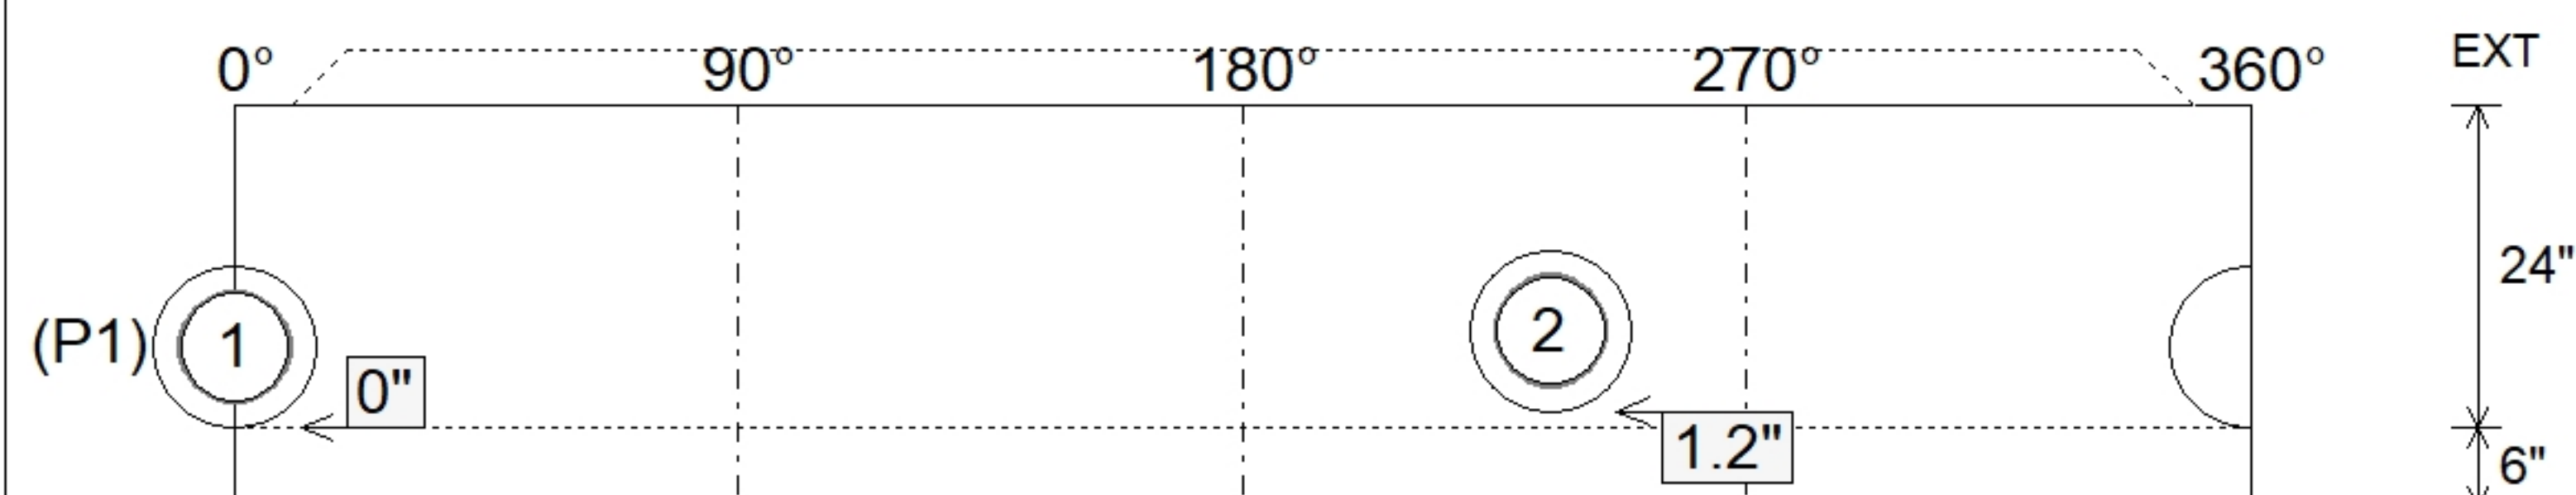

SUBMITTAL
APPROVED BY:
