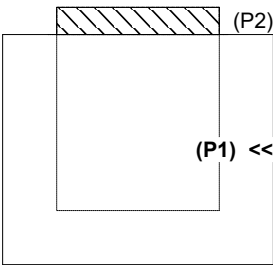
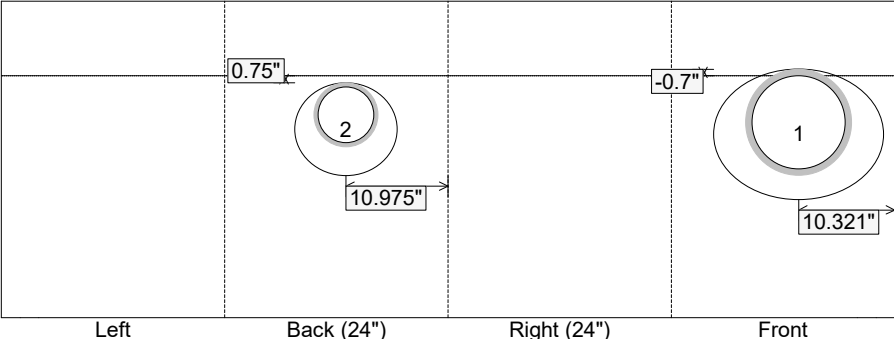


Job Name: 26-2783 - Kentucky Livestock Innovation Center Job Location: Versailles, KY Contractor: Lagco Inc.					Plant: Beaver Dam 10/13/2026 12:57:13 PM		Tech: J. Coppage PC: M. Sullivan				
Structure ID: DI-4A4											
P1 BX2424-08BAVF BOX BASE 8inW, 8inF, Variable Ht											
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht - 26" 1) CASTING - HOE 280 ADA F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 14 1) Hole - 10						0 lb 3115 lb 138 lb 0 lb 0 lb 0 lb ----- Structure Total: 3253 lb		Structure Notes: 1. JR HOE HOE-280 ADA F/G PROVIDED BY ICAST. 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 855.3' Rim to Invert: 2.5' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	852.8'	40°	25.033"	10" HDPE	11.4"	Hole 14	14"	18.276"	-0.7"	-9"	
Invert 2	852.9'	205°	22.706"	6" HDPE	6.9"	Hole 10	10"	11.034"	0.75"	-6"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions)  (P2) (P1) << Invert: 2 Degree: 205° Horz: 10.975" Hole: 10" Up(_): 0.75" Invert: 1 Degree: 40° Horz: 10.321" Hole: 14" Up(_): -0.7" Invert: 2 Degree: 205° Horz: 10.975" Hole: 10" Up(_): 0.75" Invert: 1 Degree: 40° Horz: 10.321" Hole: 14" Up(_): -0.7"											
INSIDE WALL DIMENSIONS  (P1) Left Back (24") Right (24") Front EXT											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 26" Height (Ext): 34"		Weight (Net): 3115 lb Volume (Net): 0.8cu.yd		
