

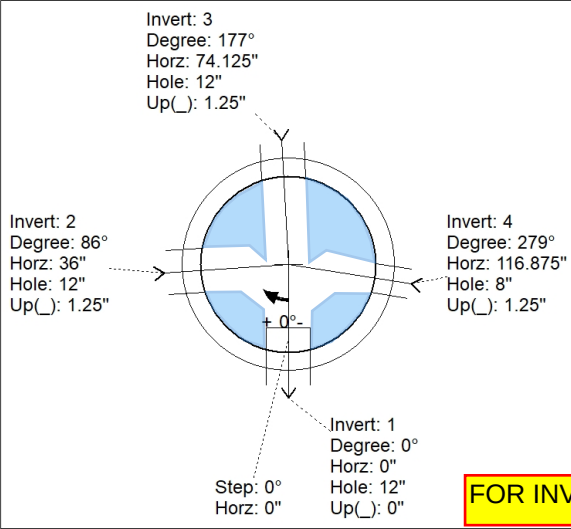
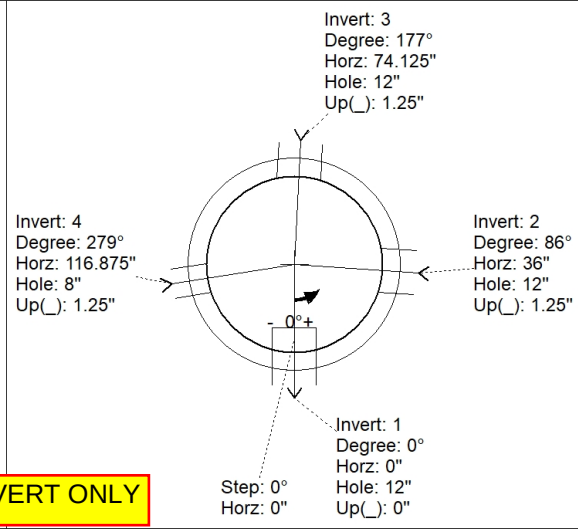
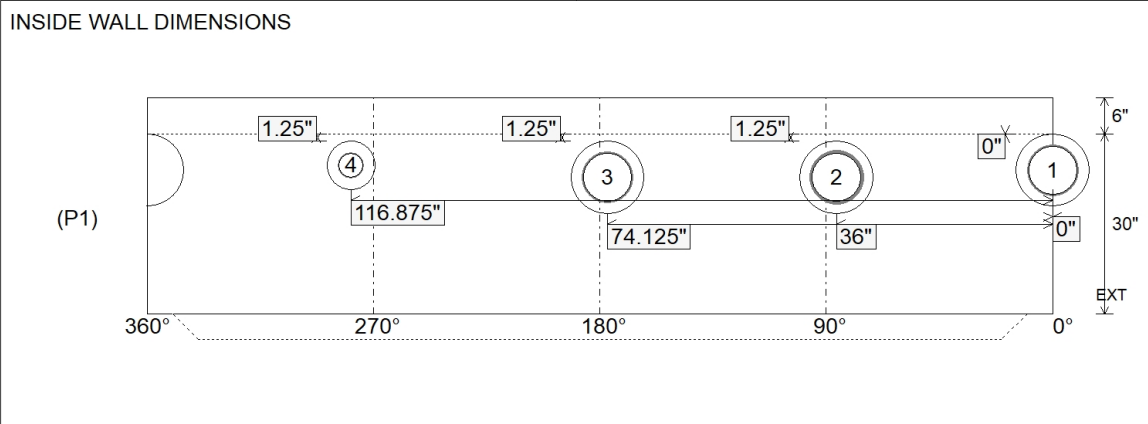
Job Name: 26-2793 - Nathan Way Area Sewer Improvements Job Location: Lawrenceburg, KY Contractor: Shouse Excavating					Plant: 100		Tech: J. Horsley			
					10/8/2026 12:15:42 PM		PC: E. Bradley			
Structure ID: B-4 SS-MH										
P1 MH048BA30					MH BASE T/n					
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 30" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) PSX - 12M NYLO 1) PSX - 8QRS-S NYLO 5) MH Step ML-10-TDS-NCR - 10"					0 lb 3000 lb 3261 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 0 lb 16 lb 8 lb 6 lb 0 lb Structure Total: 8037 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C "SAN"). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 780' Rim to Invert: 6.04' Slack: 1.48" Sump: 2" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	773.96'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	774.06'	86°	43.5"	8" DI	9"	PSX 12M NYLO	12"	12.129"	1.25"	0"
Invert 3	774.06'	177°	89.625"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"
Invert 4	774.06'	279°	141.25"	4" PVC SDR35	4.25"	PSX 8QRS-S NYLO	8"	8.038"	1.25"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int):	Seam Up: Tongue	Wall Thickness: 5"	Height (Int): 30"	Weight (Net): 3261 lb
Coating (Ext):	Seam Dn: n/a	Floor Height: 6"	Height (Ext): 36"	Volume (Net): 0.83cu.yd

Job Name: 26-2793 - Nathan Way Area Sewer Improvements				Plant: 100		Tech: J. Horsley					
Job Location: Lawrenceburg, KY				10/8/2026 12:15:42 PM		PC: E. Bradley					
Contractor: Shouse Excavating											
Structure ID: B-4 SS-MH											
P1A MH048BA30				MH BASE T/n							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 30" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) PSX - 12M NYLO 1) PSX - 8QRS-S NYLO 5) MH Step ML-10-TDS-NCR - 10"				0 lb 3000 lb 3261 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 0 lb 16 lb 8 lb 6 lb 0 lb Structure Total: 8037 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C "SAN"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 780' Rim to Invert: 6.04' Slack: 1.48' Sump: 2' Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	773.96'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	774.06'	86°	43.5"	8" DI	9"	PSX 12M NYLO	12"	12.129"	1.25"	0"	
Invert 3	774.06'	177°	89.625"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"	
Invert 4	774.06'	279°	141.25"	4" PVC SDR35	4.25"	PSX 8QRS-S NYLO	8"	8.038"	1.25"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  FOR INVERT ONLY INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 30" Height (Ext): 36"		Weight (Net): 3261 lb Volume (Net): 0.83cu.yd	
