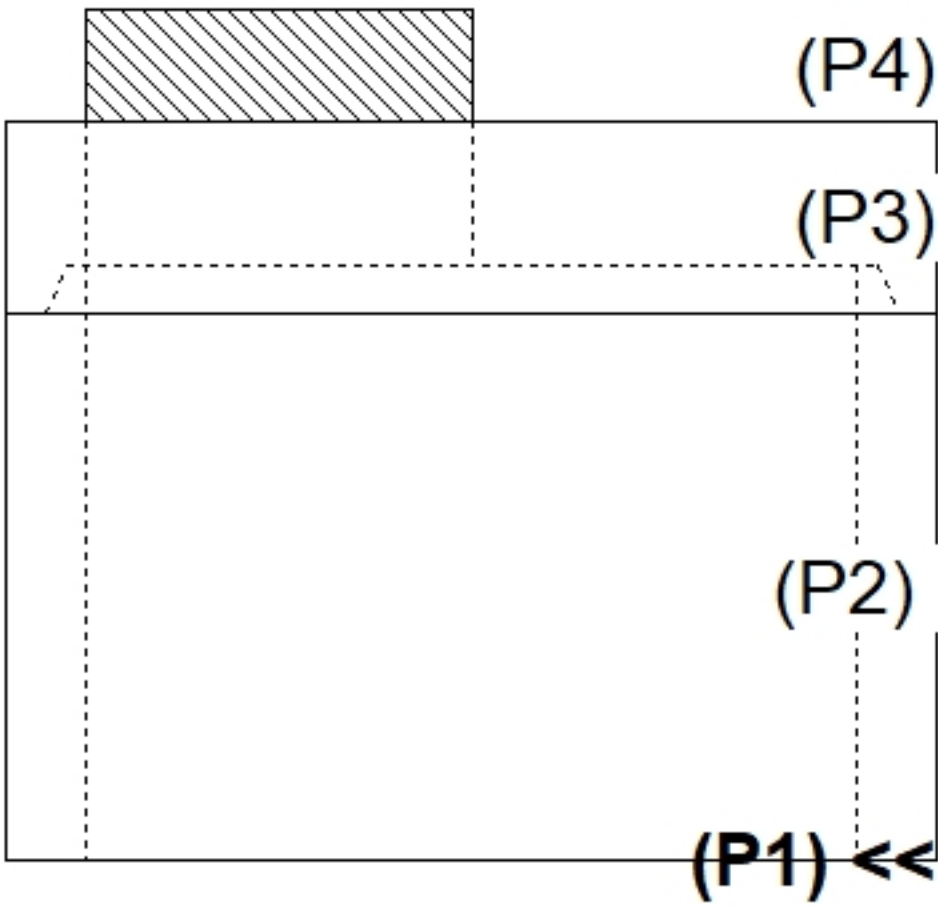
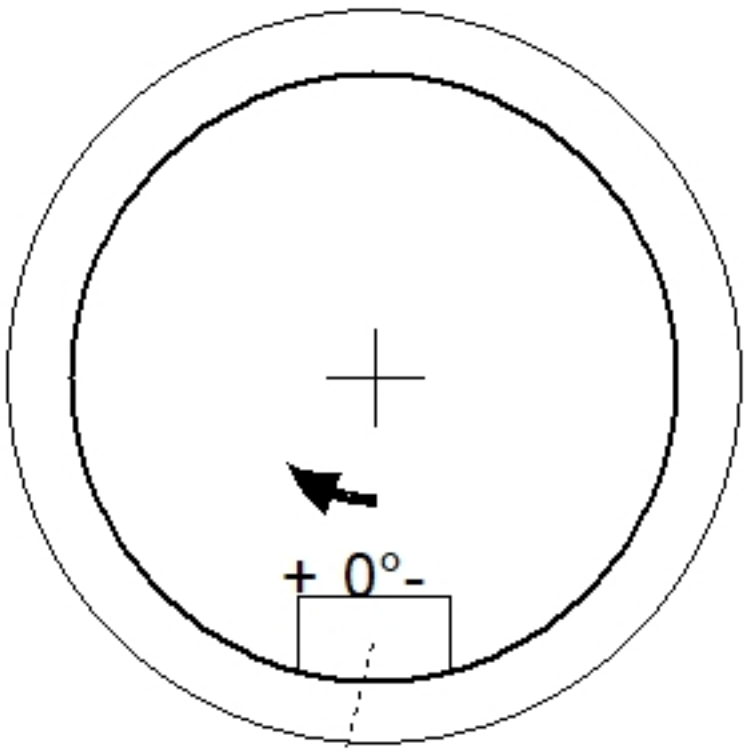


Job Name: 26-2793 - Nathan Way Area Sewer Improvements					Plant: 100		Tech: J. Horsley				
Job Location: Lawrenceburg, KY					10/8/2026 12:15:42 PM		PC: E. Bradley				
Contractor: Shouse Excavating											
Structure ID: B-5 SS-MH											
P1 P.I.P. BY OTHERS - BTM SLAB F/n											
P4) 24" - CASTING HEIGHT - 7" P3) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P2) 48" - MH DH RISER Custom Ht T/F - 34" P1) 48" - P.I.P. BY OTHERS - BTM SLAB F/n - 0" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 2) 48" - DBL 1"x14.5' Butyl (2x) 2) PSX - 12-08 NYLO 2) DOGHOUSE - 12"x12" 3) MH Step ML-10-TDS-NCR - 10"						0 lb 1561 lb 2118 lb 0 lb 0 lb 0 lb 305 lb 0 lb 16 lb 0 lb 0 lb ----- Structure Total: 4000 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C "SAN"). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 779'		Rim to Invert: 3.93'		Slack: 0.16"		Sump: 6"		Step Position: 0°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
						RIGHT-SIDE UP VIEW (int. dimensions)			UPSIDE-DOWN VIEW (int. dimenions)		
						 Step: 0° Horz: 0"					
INSIDE WALL DIMENSIONS											
						(P1) 0° 90° 180° 270° 360° EXT 0"					
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 5" Floor Height: 0"		Height (Int): 0" Height (Ext): 0"		Weight (Net): 0 lb Volume (Net): 0cu.yd		
