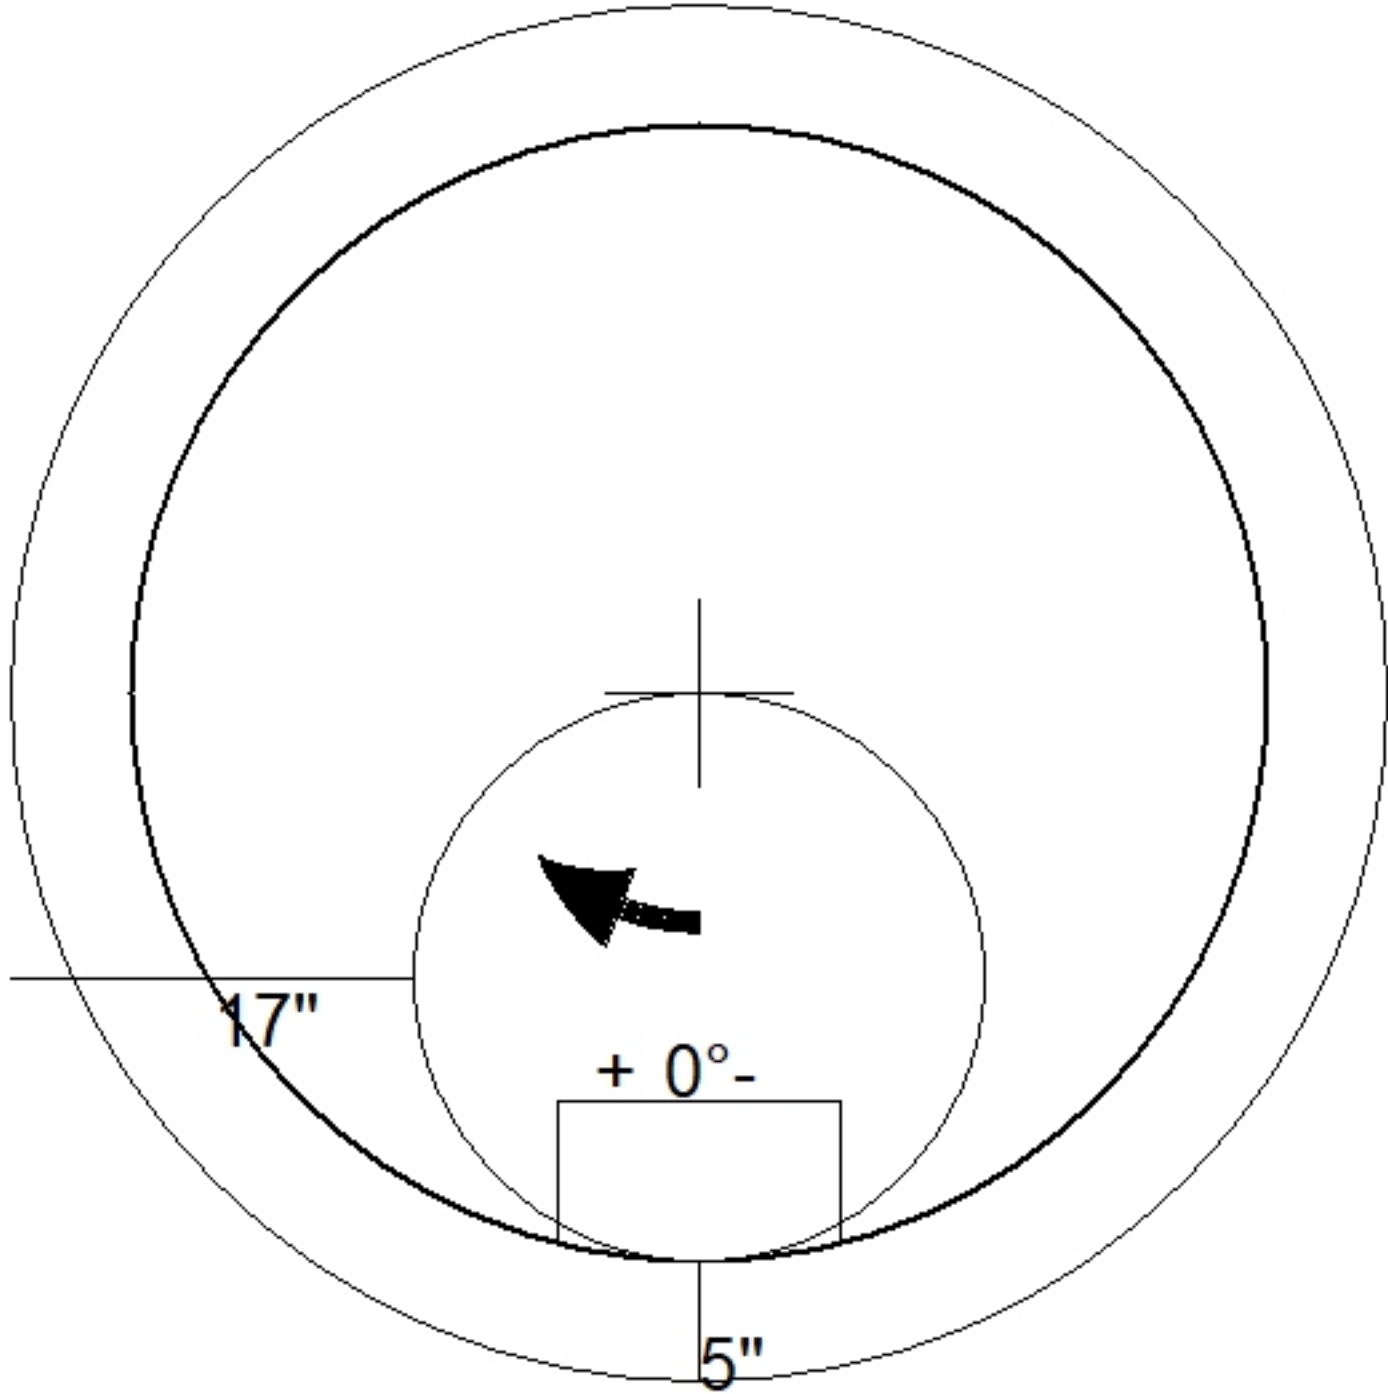
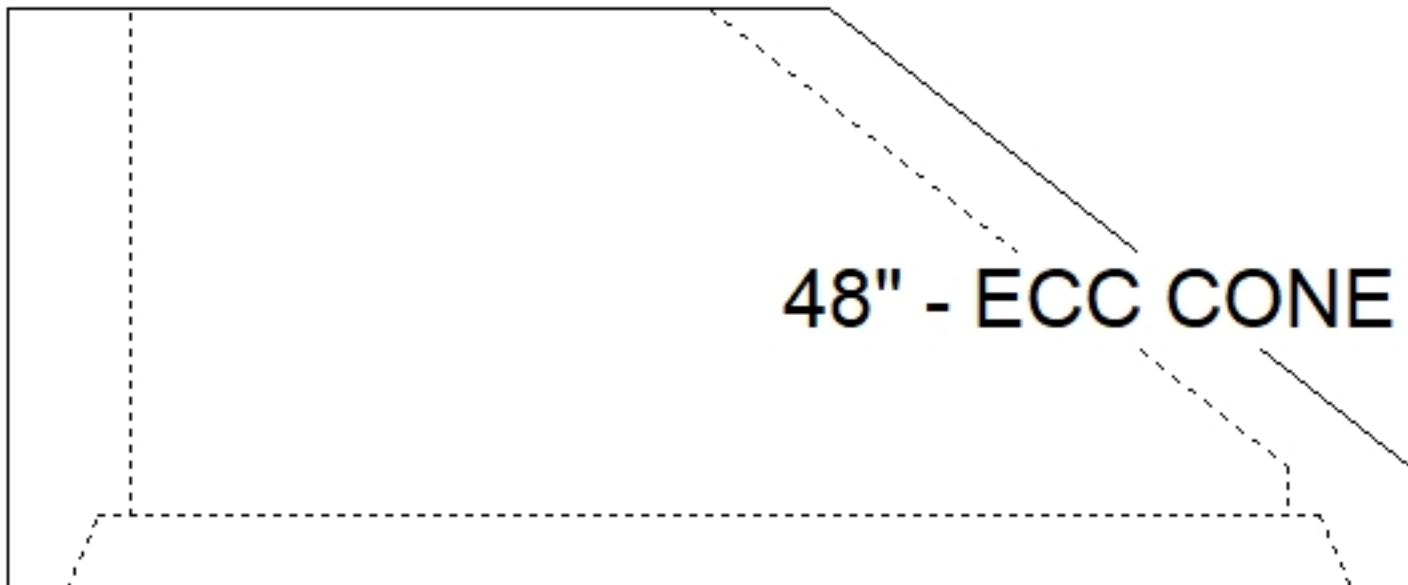


Job Name: 26-2793 - Nathan Way Area Sewer Improvements		Plant: 100	Tech: J. Horsley	
Job Location: Lawrenceburg, KY Contractor: Shouse Excavating		10/8/2026 12:17:11 PM	PC: E. Bradley	
Structure ID: D-1 SS-MH				
P2 MH048CN24		ECC CONE w/ 24" HOLE F/G		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 24" P1) 48" - MH BASE T/n - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12M NYLO 1) PSX - 12-08 NYLO 3) MH Step ML-10-TDS-NCR - 10"		0 lb 1550 lb 2911 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 0 lb 8 lb 8 lb 0 lb ----- 6222 lb Structure Total:	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C "SAN"). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE F/G - 24" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1550 lb Volume (Net): 0.33cu.yd
