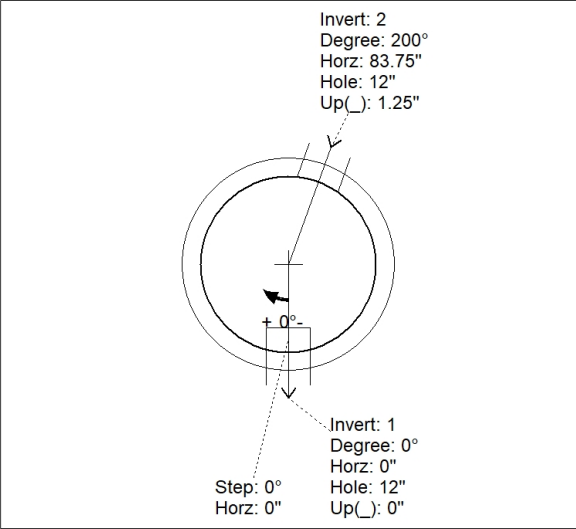
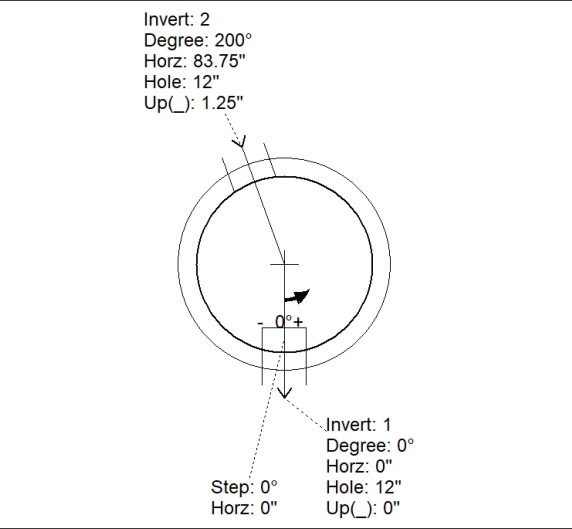
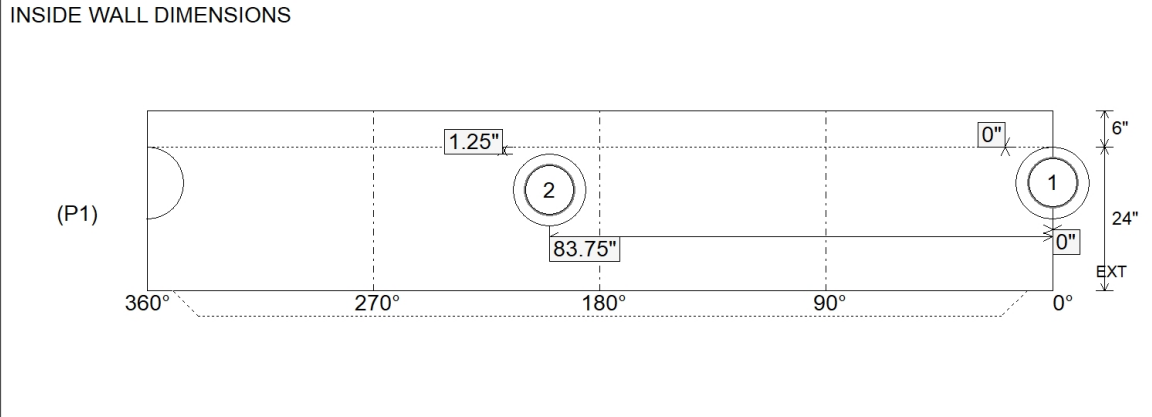


Job Name: 26-2793 - Nathan Way Area Sewer Improvements Job Location: Lawrenceburg, KY Contractor: Shouse Excavating					Plant: 100 10/8/2026 12:15:44 PM		Tech: J. Horsley PC: E. Bradley				
Structure ID: E-1 SS-MH											
P1 MH048BA24		MH BASE T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P1) 48" - MH BASE T/n - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) MH Step ML-10-TDS-NCR - 10"					0 lb 1561 lb 2911 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 6233 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C "SAN"). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 805.96' Rim to Invert: 3.55' Slack: 1.604" Sump: 2.004" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	802.41'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	802.51'	200°	101.25"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 24" Height (Ext): 30"		Weight (Net): 2911 lb Volume (Net): 0.74cu.yd		

Job Name: 26-2793 - Nathan Way Area Sewer Improvements

Job Location: Lawrenceburg, KY

Contractor: Shouse Excavating

Plant: 100

10/8/2026 12:15:44 PM

Tech: J. Horsley

PC: E. Bradley



Structure ID: E-1 SS-MH

P1A MH048BA24

MH BASE T/n

P3) 24" - CASTING HEIGHT - 7"

P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12"

P1) 48" - MH BASE T/n - 24"

1) 48" - MH INVERT CHANNEL - FULL HEIGHT

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) CASTING - HOE MC-350 F/C Sanitary

1) 48" - Conseal CS-102 1.00" (Double)

1) 24" - Conseal CS-102 1.00" (Double)

2) PSX - 12-08 NYLO

1) MH Step ML-10-TDS-NCR - 10"

0 lb

1561 lb

2911 lb

1440 lb

0 lb

0 lb

305 lb

0 lb

0 lb

16 lb

0 lb

Structure Total: 6233 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. CASTING BY ICAST (HOE MC-350 F/C "SAN").

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 805.96'

Rim to Invert: 3.55'


Slack: 1.604"

Sump: 2.004"


Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	802.41'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	802.51'	200°	101.25"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

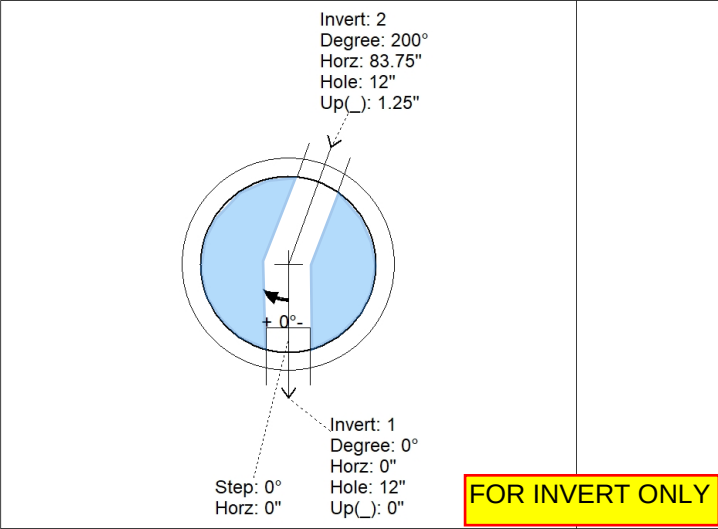

UPSIDE-DOWN VIEW (int. dimensions)

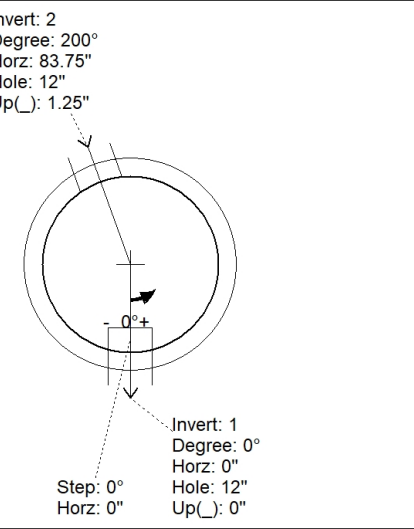

INSIDE WALL DIMENSIONS

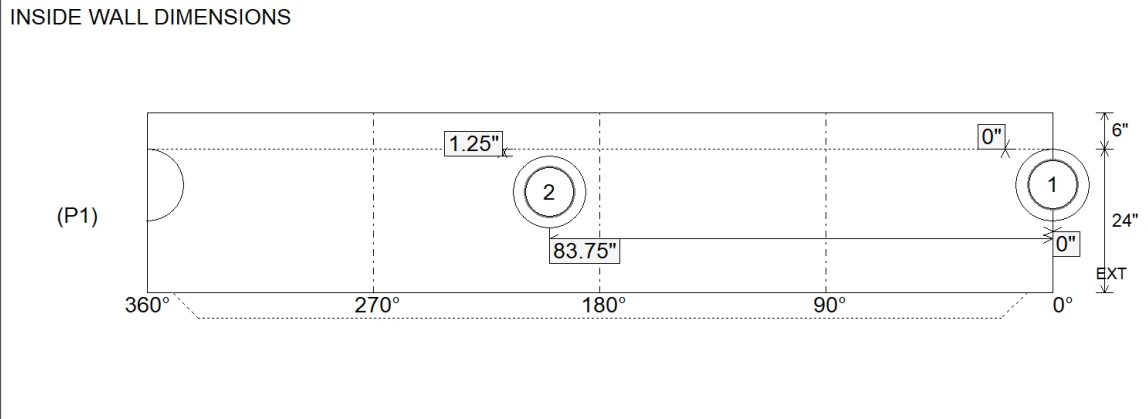

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 5"

Floor Height: 6"

Height (Int): 24"

Height (Ext): 30"

Weight (Net): 2911 lb

Volume (Net): 0.74cu.yd
