




Job Name: 26-2793 - Nathan Way Area Sewer Improvements Job Location: Lawrenceburg, KY Contractor: Shouse Excavating					Plant: 100 10/8/2026 12:15:44 PM		Tech: J. Horsley PC: E. Bradley				
Structure ID: F-2 SS-MH											
P1 MH048BA18		MH BASE T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 24" P1) 48" - MH BASE T/n - 18" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 3) MH Step ML-10-TDS-NCR - 10"					0 lb 1550 lb 2540 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 0 lb 8 lb 0 lb Structure Total: 5843 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C "SAN"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 823.17' Rim to Invert: 4' Slack: 1.004" Sump: 2.004" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	819.17'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

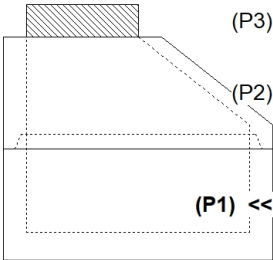


RIGHT-SIDE UP VIEW (int. dimensions)



UPSIDE-DOWN VIEW (int. dimensions)



INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):


Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 18"
Height (Ext): 24"


Weight (Net): 2540 lb
Volume (Net): 0.65cu.yd

Job Name: 26-2793 - Nathan Way Area Sewer Improvements Job Location: Lawrenceburg, KY Contractor: Shouse Excavating					Plant: 100 10/8/2026 12:15:44 PM		Tech: J. Horsley PC: E. Bradley			
Structure ID: F-2 SS-MH										
P1A MH048BA18			MH BASE T/n							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 24" P1) 48" - MH BASE T/n - 18" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 3) MH Step ML-10-TDS-NCR - 10"					0 lb 1550 lb 2540 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 0 lb 8 lb 0 lb Structure Total: 5843 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C "SAN"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 823.17' Rim to Invert: 4' Slack: 1.004" Sump: 2.004" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	819.17'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

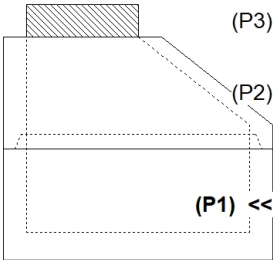

(P3)
(P2)
(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)



Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"

UPSIDE-DOWN VIEW (int. dimensions)




Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"

FOR INVERT ONLY

INSIDE WALL DIMENSIONS



(P1)

360° 270° 180° 90° 0°

6" 18" EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 18" Height (Ext): 24"	Weight (Net): 2540 lb Volume (Net): 0.65cu.yd
----------------------------------	---------------------------------	--	--	--
