
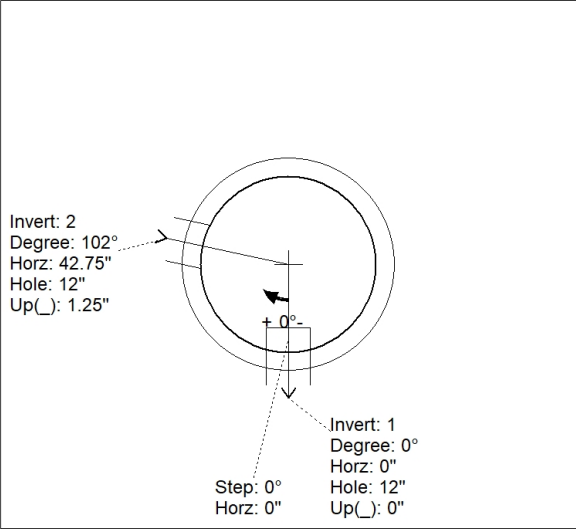
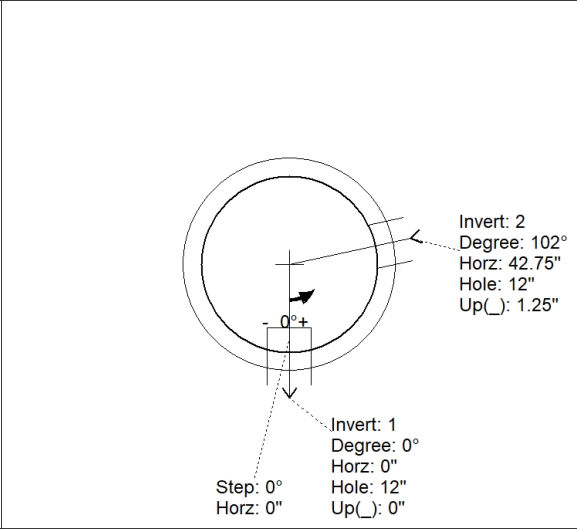
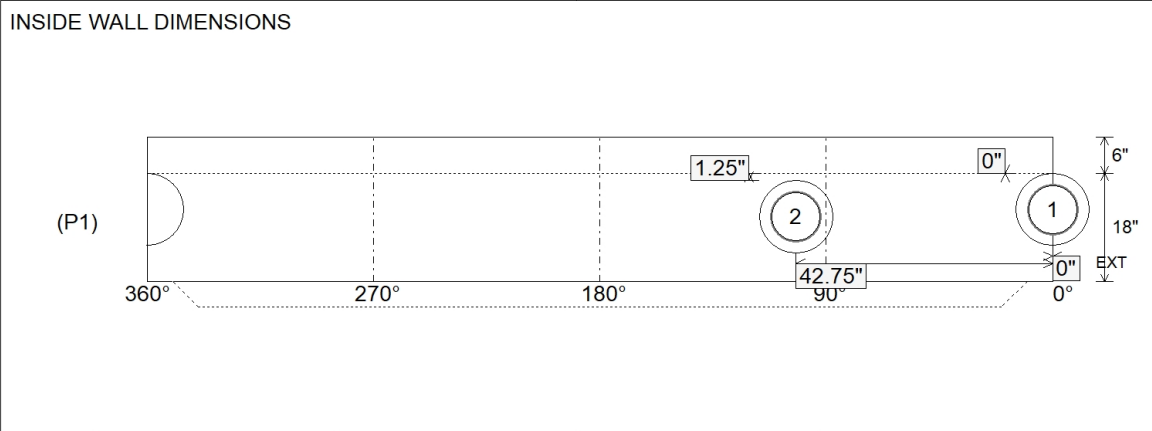


Job Name: 26-2793 - Nathan Way Area Sewer Improvements Job Location: Lawrenceburg, KY Contractor: Shouse Excavating					Plant: 100 10/8/2026 12:15:45 PM		Tech: J. Horsley PC: E. Bradley				
Structure ID: Prop. MH A SS-MH											
P1 MH048BA18			MH BASE T/n								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 24" P1) 48" - MH BASE T/n - 18" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) MH Step ML-10-TDS-NCR - 10"					0 lb 1550 lb 2492 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 0 lb 0 lb 16 lb 0 lb Structure Total: 5803 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C "SAN"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 760' Rim to Invert: 4' Slack: 1.004" Sump: 2.004" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	756'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	756.1'	102°	51.625"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 18" Height (Ext): 24"		Weight (Net): 2492 lb Volume (Net): 0.64cu.yd	

Job Name: 26-2793 - Nathan Way Area Sewer Improvements Job Location: Lawrenceburg, KY Contractor: Shouse Excavating					Plant: 100 10/8/2026 12:15:45 PM		Tech: J. Horsley PC: E. Bradley				
Structure ID: Prop. MH A SS-MH											
P1A MH048BA18			MH BASE T/n								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 24" P1) 48" - MH BASE T/n - 18" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) MH Step ML-10-TDS-NCR - 10"					0 lb 1550 lb 2492 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 0 lb 16 lb 0 lb Structure Total: 5803 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C "SAN"). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 760' Rim to Invert: 4' Slack: 1.004" Sump: 2.004" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	756'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	756.1'	102°	51.625"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

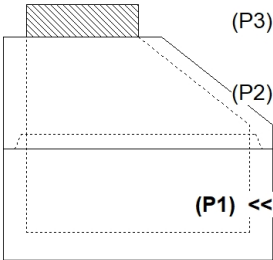


(P3)

(P2)

(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

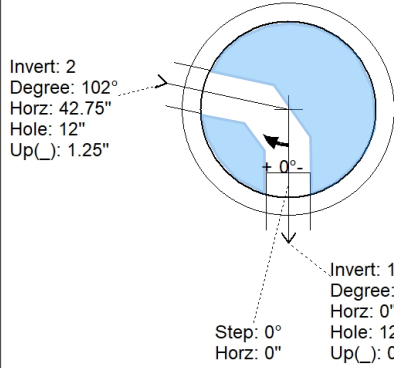


Invert: 2
Degree: 102°
Horz: 42.75"
Hole: 12"
Up(): 1.25"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"

UPSIDE-DOWN VIEW (int. dimensions)

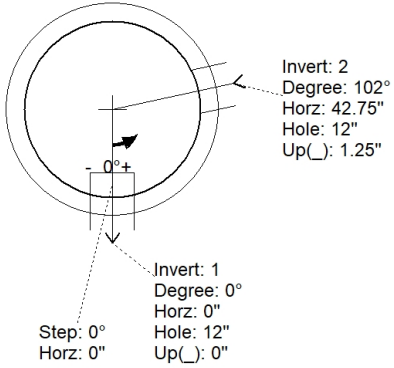


Invert: 2
Degree: 102°
Horz: 42.75"
Hole: 12"
Up(): 1.25"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

Step: 0°
Horz: 0"

FOR INVERT ONLY

INSIDE WALL DIMENSIONS



(P1)

360° 270° 180° 90° 0°

42.75" 1.25" 0"

6" 18" EXT 0"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 18" Height (Ext): 24"	Weight (Net): 2492 lb Volume (Net): 0.64cu.yd
----------------------------------	---------------------------------	--	--	--
