

Job Name: 26-2801 900640 QuikTrip No. 0680
Job Location: CPU
Contractor: Contech Engineering Solutions

Plant: Beaver Dam

Tech: S. Felletter

6/25/2026 11:00:46 AM

PC: C. Goff



Structure ID: 15-CS-4

P5 MH048LD12-30

MH FLAT LID w/30in ECC Hole F/G



P6) 30" - CASTING HEIGHT - 4"
P5) 48" - MH FLAT LID w/30in ECC Hole F/G - 12"
P4) 48" - MH RISER Custom Ht T/G - 33"
P3) 48" - MH RISER T/G - 48"
P2) 48" - MH RISER SPECIAL T/G - 72"
P1) 48" - MH BASE T/n - 18"
1) ASSEMBLY REQUIRED
1) CVSTENCILING
4) 48" - Conseal CS-102 1.00"
2) PSX - 12-08 NYLO

Structure Total:

0 lb
1413 lb
2305 lb
3353 lb
4934 lb
2588 lb
0 lb
0 lb
0 lb
16 lb

14610 lb

Structure Notes:
4" CASTING BY OTHERS
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICAST TO INSTALL THE INTERNALS
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE

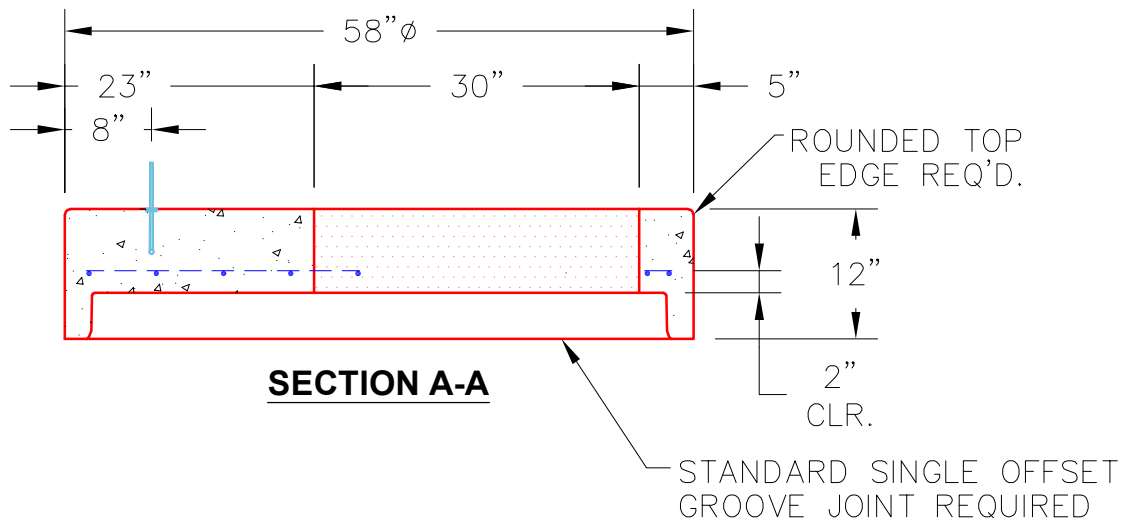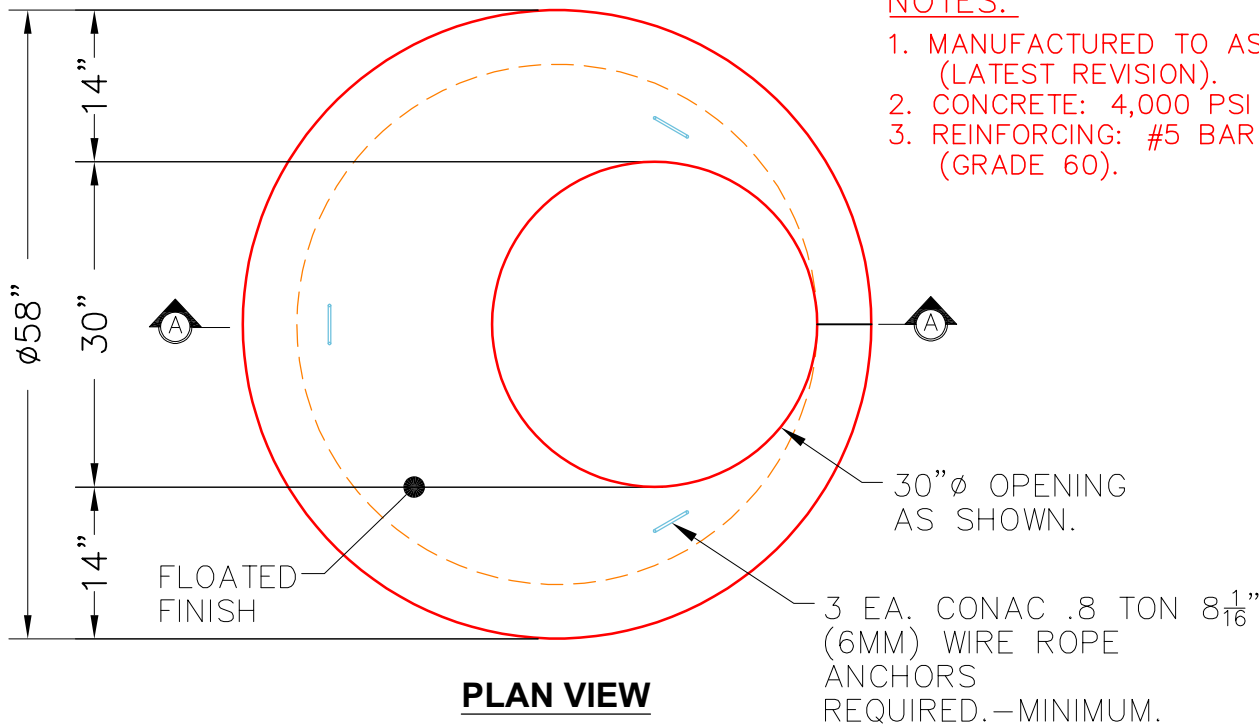

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1413 lb
Volume (Net): 0.36cu.yd
