

Job Name: 26-2809 - Yorkshire Estates Ph 1-4 Job Location: Mt. Juliet, TN Contractor: Harakas		Plant: Beaver Dam 10/7/2026 11:50:38 AM	Tech: J. Coppage PC: E. Bradley	


Structure ID: MH-A0B SS-MH

P2MH048CCN36CDARED

CON CONE w/24" HOLE, w/ConBlock-CDA Red

P4) 24" - CASTING HEIGHT - 6"	0 lb	Structure Notes: 1. JBS 1155 SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = CONBLOCK CDA RED. 5. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
P3) 24" - GRADE RING w/ConBlock-CDA Red - 6"	405 lb	
P2) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red - 36"	2251 lb	
P1) 48" - MH BASE w/ConBlock-CDA Red - 36"	3749 lb	
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb	
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb	
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT	1440 lb	
1) CASTING - JBS 1155 F/C SANITARY	250 lb	
1) 48" - Conseal CS-102 1.00" (Double)	0 lb	
2) 24" - Conseal CS-102 1.00" (Double)	0 lb	
2) PSX - 12-08 NYLO	16 lb	
6) MH Step ML-10-TDS-NCR - 10"	0 lb	

Structure Total:	8111 lb	

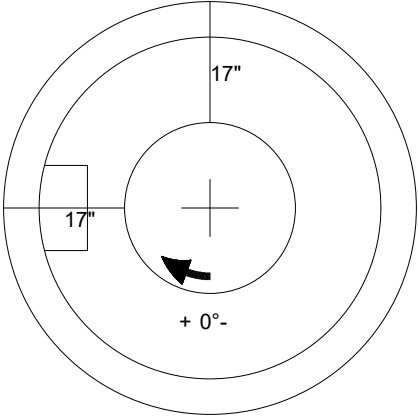

48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red - 36" - (P2)



Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	--
