

Job Name: 26-2809 - Yorkshire Estates Ph 1-4 Job Location: Mt. Juliet, TN Contractor: Harakas		Plant: Beaver Dam 10/7/2026 11:50:40 AM	Tech: J. Coppage PC: E. Bradley	

Structure ID: MH-A1 SS-MH

P3 MH048CCN36CDARED

CON CONE w/24" HOLE, w/ConBlock-CDA Red

P4) 24" - CASTING HEIGHT - 6"

P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red - 36"

P2) 48" - MH RISER w/ConBlock-CDA Red - 48"

P1) 48" - MH BASE w/ConBlock-CDA Red - 24"

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT

1) CASTING - JBS 1155 F/C SANITARY

2) 48" - Conseal CS-102 1.00" (Double)

1) 24" - Conseal CS-102 1.00" (Double)

3) PSX - 12-08 NYLO

9) MH Step ML-10-TDS-NCR - 10"

0 lb

2251 lb

3353 lb

2863 lb

0 lb

0 lb

1440 lb

250 lb

0 lb

0 lb

24 lb

0 lb

Structure Total: 10182 lb

Structure Notes: .

1. JBS 1155 SANITARY PROVIDED BY ICAST.

2. PER ASTM C478 SPECIFICATIONS.

3. CONCRETE = 4,000 PSI AT 28 DAYS.


4. ADMIXTURE = CONBLOCK CDA RED.

5. REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

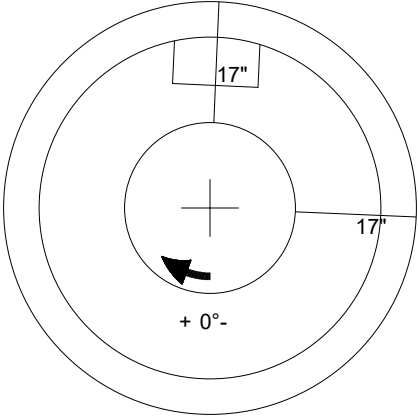



48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red - 36" - (P3)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	--
