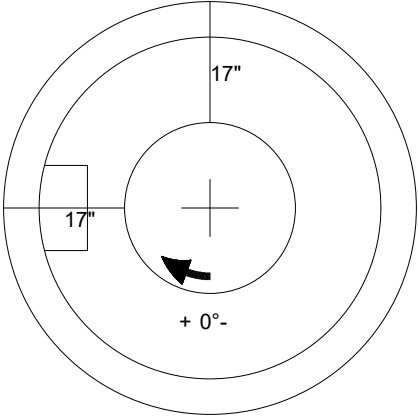


Job Name: 26-2809 - Yorkshire Estates Ph 1-4 Job Location: Mt. Juliet, TN Contractor: Harakas		Plant: Beaver Dam 10/7/2026 11:50:49 AM	Tech: J. Coppage PC: E. Bradley		
Structure ID: MH-A15 SS-MHD					
P3 MH048CCN36CDARED		CON CONE w/24" HOLE, w/ConBlock-CDA Red			
P5) 24" - CASTING HEIGHT - 6" P4) 24" - GRADE RING w/ConBlock-CDA Red - 4" P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red - 36" P2) 48" - MH RISER w/DROP/ConBlock-CDA Red - 60" P1) 48" - MH BASE w/DROP/ConBlock-CDA Red - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - JBS 1155 F/C SANITARY 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 1) Drop Tee - 8" PVC 1) Drop Elbow - 8" PVC 11) MH Step ML-10-TDS-NCR - 10"		0 lb 270 lb 2251 lb 4168 lb 3725 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb 0 lb 0 lb 0 lb	<u>Structure Notes:</u> . 1. JBS 1155 SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = CONBLOCK CDA RED. 5. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Structure Total:		12120 lb			
					
 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red - 36" - (P3)					
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd	
