


Job Name: 26-2809 - Yorkshire Estates Ph 1-4 Job Location: Mt. Juliet, TN Contractor: Harakas					Plant: Beaver Dam 10/7/2026 11:36:43 AM		Tech: J. Coppage PC: E. Bradley				
Structure ID: MH-C1 SS-MH											
P2 MH048RS48CDARED			MH RISER w/ConBlock-CDA Red								
P4) 24" - CASTING HEIGHT - 6" P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red - 36" P2) 48" - MH RISER w/ConBlock-CDA Red - 48" P1) 48" - MH BASE w/ConBlock-CDA Red - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 2) CASTING - JBS 1155 F/C SANITARY 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 9) MH Step ML-10-TDS-NCR - 10"						0 lb 2251 lb 3353 lb 3330 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 16 lb 0 lb		Structure Notes: 1. JBS 1155 SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = CONBLOCK CDA RED. 5. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Structure Total:						10641 lb					
Rim: 495.7' Rim to Invert: 9.9' Slack: 0.8" Sump: 2" Step Position: 255.5°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

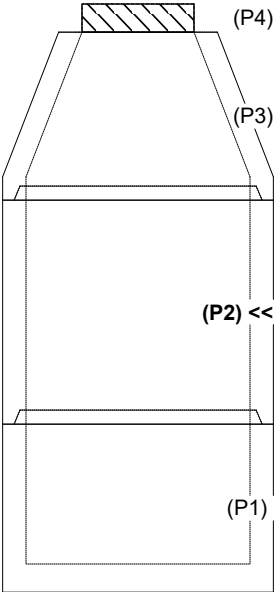


(P4)

(P3)

(P2) <<

(P1)


RIGHT-SIDE UP VIEW (int. dimensions)



Step: 255.5°
Horz: 107.024"

+ 0°-

INSIDE WALL DIMENSIONS

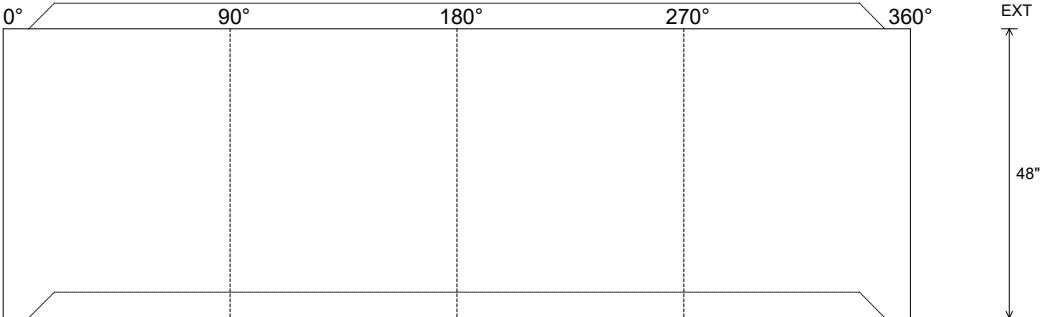

0° 90° 180° 270° 360°

EXT

48"

(P2)

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3353 lb Volume (Net): 0.86cu.yd
----------------------------------	------------------------------------	--	--	--
