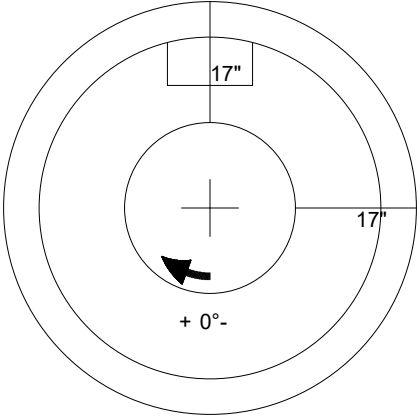



Job Name: 26-2809 - Yorkshire Estates Ph 1-4 Job Location: Mt. Juliet, TN Contractor: Harakas		Plant: Beaver Dam 10/7/2026 11:50:59 AM	Tech: J. Coppage PC: E. Bradley	
Structure ID: MH-F2 SS-MH				
P3 MH048CCN24CDARED		CON CONE w/24" HOLE, w/ConBlock-CDA Red		
P5) 24" - CASTING HEIGHT - 6" P4) 24" - GRADE RING w/ConBlock-CDA Red - 3" P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red - 24" P2) 48" - MH RISER w/ConBlock-CDA Red - 36" P1) 48" - MH BASE w/ConBlock-CDA Red - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - JBS 1155 F/C SANITARY 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 7) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 1297 lb 2515 lb 2959 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 0 lb 8 lb 0 lb ----- 8671 lb	<u>Structure Notes:</u> . 1. JBS 1155 SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = CONBLOCK CDA RED. 5. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1297 lb Volume (Net): 0.33cu.yd
