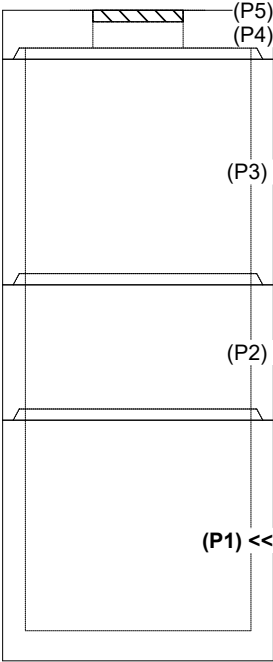


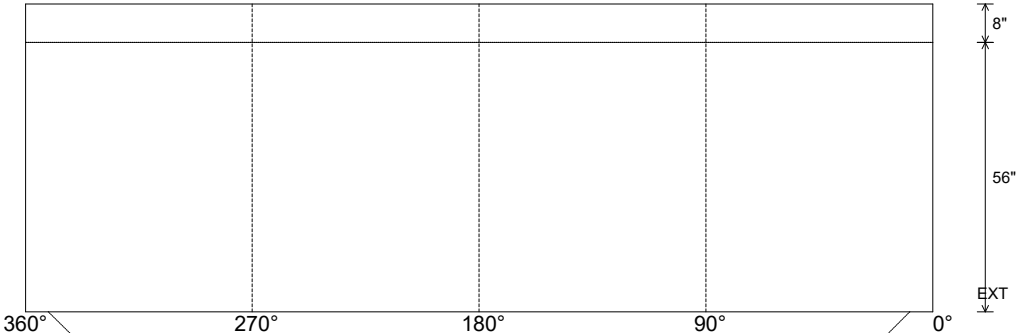


Job Name: 26-2820 - Utility Relocation Job Location: Jackson, KY Contractor: Triton Construction				Plant: 100 8/18/2026 6:25:34 PM		Tech: Jared - F PC: E. Bradley				
Structure ID: QL1										
P1		MH060BAVF		MH BASE Custom Ht T/n						
P5) 24" x 36" - HATCH (CAST FLUSH) - 3" P4) 60" - MH FLAT TOP w/24"x36" Hatch F/G - 13" P3) 60" - MH RISER SPECIAL T/G - 60" P2) 60" - MH RISER SPECIAL T/G - 36" P1) 60" - MH BASE Custom Ht T/n - 56" 1) HATCH (Alum.) - HALLIDAY W1S 24"x36" 3) JOINT WRAP - 12" WD x 060" MAC WRAP 3) 60" - Conseal CS-231 1.00" (Double) 3) PSX - 8QRS-S NYLO 2) PSX - 12-08 NYLO				100 lb 2478 lb 6128 lb 3701 lb 8579 lb 61 lb 0 lb 0 lb 20 lb 16 lb ----- Structure Total: 21082 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,500 PSI AT 28 DAYS. 3. HALLIDAY W1S 36" X24" HATCH TO BE SUPPLIED BY ICAST & CAST-IN INTO TOP SLAB BY ICAST. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .24) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. NOTE: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING – INSTALLED AT 0, 90, 180, & 270, 18" FROM TOP OF WALLS				
Rim: 736.74' Rim to Invert: 7.31' Slack: 0.48" Sump: 77.76" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)    INSIDE WALL DIMENSIONS  Coating (Int): Coating (Ext): Seam Up: Tongue Seam Dn: n/a Wall Thickness: 6" Floor Height: 8" Height (Int): 56" Height (Ext): 64" Weight (Net): 8579 lb Volume (Net): 2.19cu.yd										
