

Job Name: 26-2820 - Utility Relocation
Job Location: Jackson, KY
Contractor: Triton Construction

Plant: 100

8/19/2026 11:09:13 AM

Tech: Jared - F
PC: E. Bradley



Structure ID: QL1

P4 MH060LD13S

MH FLAT TOP w/24"x36" Hatch F/G

P5) 24" x 36" - HATCH (CAST FLUSH) - 3"
P4) 60" - MH FLAT TOP w/24"x36" Hatch F/G - 13"
P3) 60" - MH RISER SPECIAL T/G - 60"
P2) 60" - MH RISER SPECIAL T/G - 36"
P1) 60" - MH BASE Custom Ht T/n - 56"
1) HATCH (Alum.) - HALLIDAY W1S 24"x36"
3) JOINT WRAP - 12" WD x 060" MAC WRAP
3) 60" - Conseal CS-231 1.00" (Double)
3) PSX - 8QRS-S NYLO
2) PSX - 12-08 NYLO


100 lb
2478 lb
6128 lb
3701 lb
8579 lb
61 lb
0 lb
0 lb
20 lb
16 lb

Structure Total: 21082 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,500 PSI AT 28 DAYS.
3. HALLIDAY W1S 36" X24" HATCH TO BE SUPPLIED BY ICAST & CAST-IN INTO TOP SLAB BY ICAST.

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .24)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

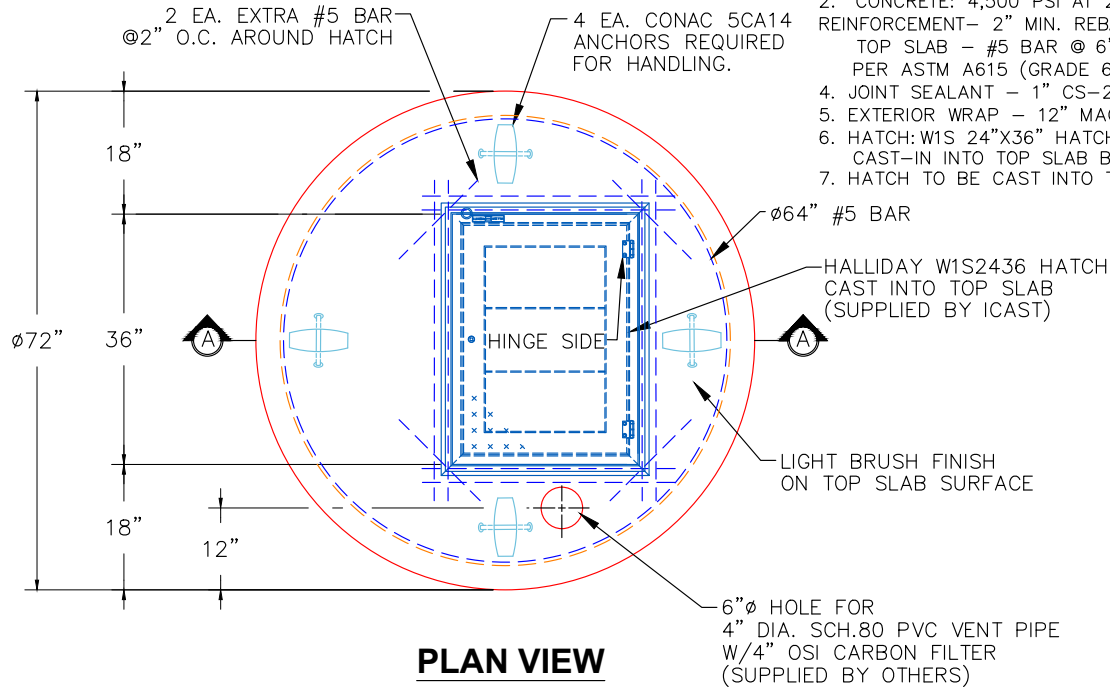

NOTES:

1. PER ASTM C-478 LATEST REVISION
2. CONCRETE: 4,500 PSI AT 28 DAYS.
- REINFORCEMENT- 2" MIN. REBAR CLEARANCE (TYP):
TOP SLAB - #5 BAR @ 6" C.C.E.W.
PER ASTM A615 (GRADE 60)
4. JOINT SEALANT - 1" CS-231-DOUBLE
5. EXTERIOR WRAP - 12" MACWRAP. (SUPPLIED BY ICAST).
6. HATCH: W1S 24"x36" HATCH IS PROVIDED BY ICAST & CAST-IN INTO TOP SLAB BY ICAST
7. HATCH TO BE CAST INTO TOP SLAB.

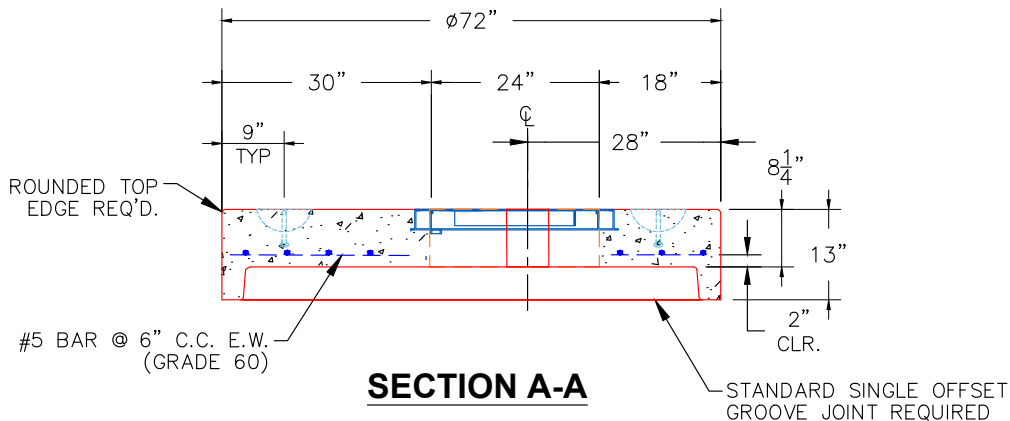

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 6"

Height (Ext): 13"

Weight (Net): 2478 lb
Volume (Net): 0.63cu.yd
