

Job Name: 26-2821 - Raising Cane's C1594
Job Location: Evansville, IN 47715
Contractor: Stemaly Excavating Inc.

Plant: 100

9/30/2026 12:09:40 PM

Tech: Jared - F

PC: T. Lewis



Structure ID: QL12 GT1500

P1 BX072144-06W06F-VF

BOX BASE 6inW, 6inF, Variable Ht F/n

- P3) 24" - CASTING HEIGHT - 7"
P2) 72" x 144" - CB FLAT TOP 6"W w/(2) 24" HOLES (Grease Trap) F/F - 8"
P1) 72" x 144" - BOX BASE 6inW, 6inF, Variable Ht F/n - 48"
1) 72" x 46" - BAFFLE WALL (GT-1500 GAL.) - 4"
2) CASTING - HOE MC-375 F/C Grease
1) 72" x 144" - Con Seal CS-102 1.00" (Double)
1) 24" - Con Seal CS-102 1.00" (Double)
2) Kor-N-Seal1 - S106-8SRWS


0 lb
9083 lb
19267 lb
1073 lb
271 lb
0 lb
0 lb
0 lb
13 lb

Structure Total: 29978 lb

Structure Notes:

1. PER ASTM C-890-13 SPECIFICATIONS.
 2. CONCRETE = 5,000 PSI AT 28 DAYS.
 3. NO STEPS AND NO FLOW CHANNEL.
 4. CASTING BY ICAST (2EA. HOE MC-375 F/C GREASE)
 5. SECONDARY POUR REQ'D - BAFFLE WALL.
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .47) #5 BARS AT 8" C.C.E.W.
- WALLS (As .47) #5 BARS AT 8" C.C.E.W.
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Rim: 5.25' Rim to Invert: 2.42' Slack: 0" Sump: 33.96" Step Position:

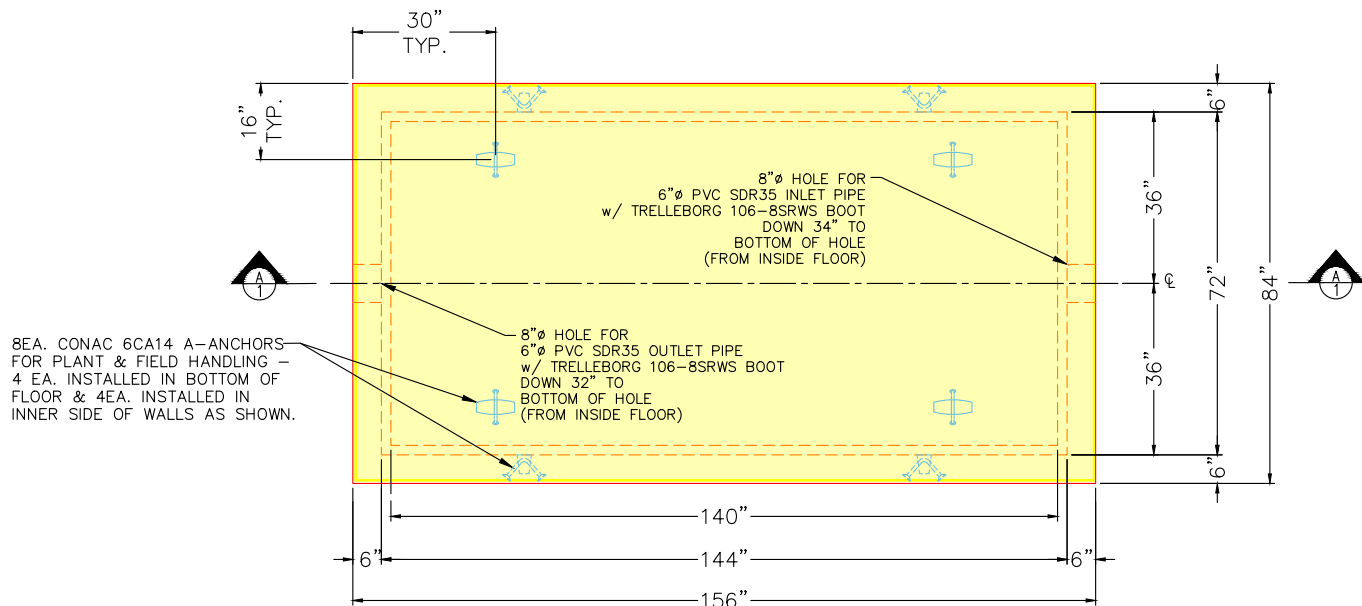


PLAN VIEW
(UPSIDE-DOWN)

FIRST POUR DRAWING

8EA. CONAC 6CA14 A-ANCHORS
FOR PLANT & FIELD HANDLING -
4 EA. INSTALLED IN BOTTOM OF
FLOOR & 4EA. INSTALLED IN
INNER SIDE OF WALLS AS SHOWN.

#5 BAR @ 8" C/C E.W.
1 1/2" CONCRETE COVER MIN.
(WALLS & FLOOR TYP.)

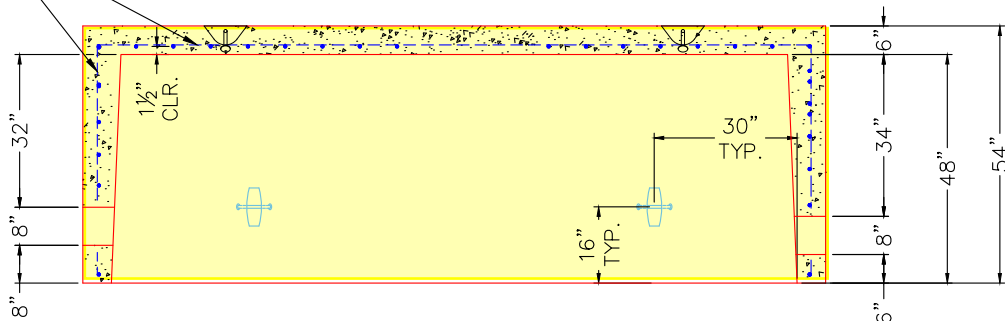

SECTION A-A
(UPSIDE-DOWN)

NOTES:

1. PER ASTM C-890-13 LATEST REVISION.
2. CONCRETE = 5,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60).
(H-20 TRAFFIC RATED DESIGN)
4. SEALED WITH 1" CS-102 (DOUBLE). (6 EA. 14.5' ROLLS REQ'D.)
5. POUR BASE, THEN POUR INTERIOR BAFFLE.
6. FIRST POUR (BASE) - 19,267 LBS

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 6"
Floor Height: 6"

Height (Int): 48"
Height (Ext): 54"

Weight (Net): 19267 lb
Volume (Net): 4.92cu.yd

Job Name: 26-2821 - Raising Cane's C1594
Job Location: Evansville, IN 47715
Contractor: Stemaly Excavating Inc.

Plant: 100

9/30/2026 12:09:40 PM

Tech: Jared - F

PC: T. Lewis



Structure ID: QL12 GT1500

P1 BX072144-06W06F-VF

BOX BASE 6inW, 6inF, Variable Ht F/n

- P3) 24" - CASTING HEIGHT - 7"
P2) 72" x 144" - CB FLAT TOP 6"W w/(2) 24" HOLES (Grease Trap) F/F - 8"
P1) 72" x 144" - BOX BASE 6inW, 6inF, Variable Ht F/n - 48"
1) 72" x 46" - BAFFLE WALL (GT-1500 GAL.) - 4"
2) CASTING - HOE MC-375 F/C Grease
1) 72" x 144" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
2) Kor-N-Seal1 - S106-8SRWS


0 lb
9083 lb
19267 lb
1073 lb
271 lb
0 lb
0 lb
13 lb

Structure Total: 29978 lb

Structure Notes:


1. PER ASTM C-890-13 SPECIFICATIONS.
 2. CONCRETE = 5,000 PSI AT 28 DAYS.
 3. NO STEPS AND NO FLOW CHANNEL.
 4. CASTING BY ICAST (2EA. HOE MC-375 F/C GREASE)
 5. SECONDARY POUR REQ'D - BAFFLE WALL.
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .47) #5 BARS AT 8" C.C.E.W.
- WALLS (As .47) #5 BARS AT 8" C.C.E.W.
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Rim: 5.25' Rim to Invert: 2.42' Slack: 0' Sump: 33.96' Step Position:

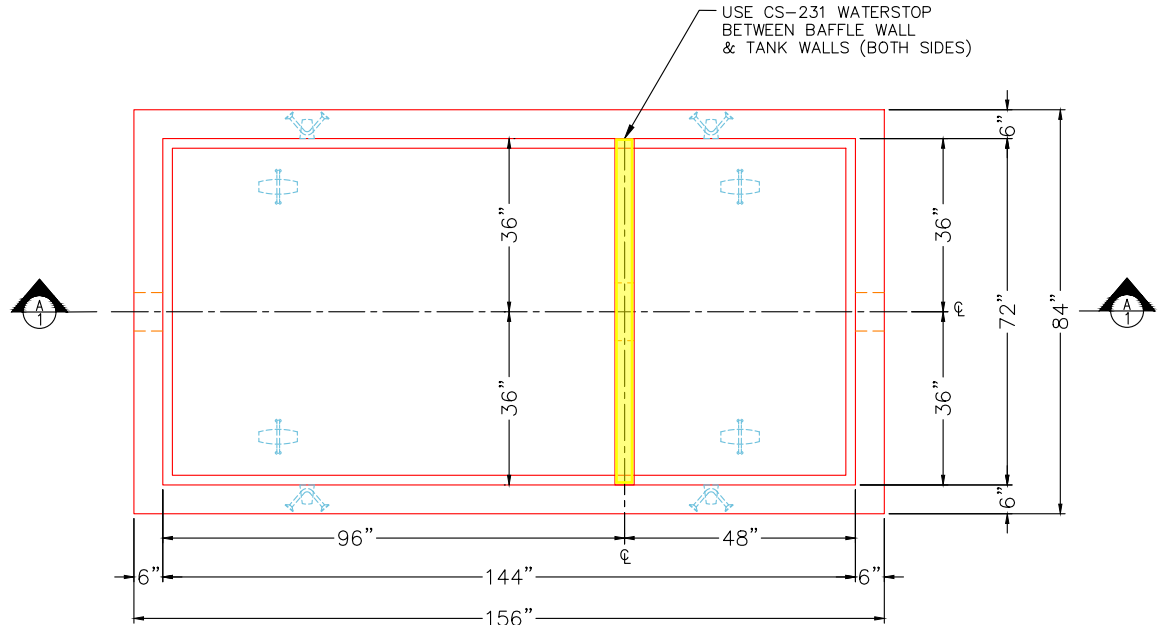

PLAN VIEW
(RIGHTSIDE-UP)

SECOND POUR DRAWING

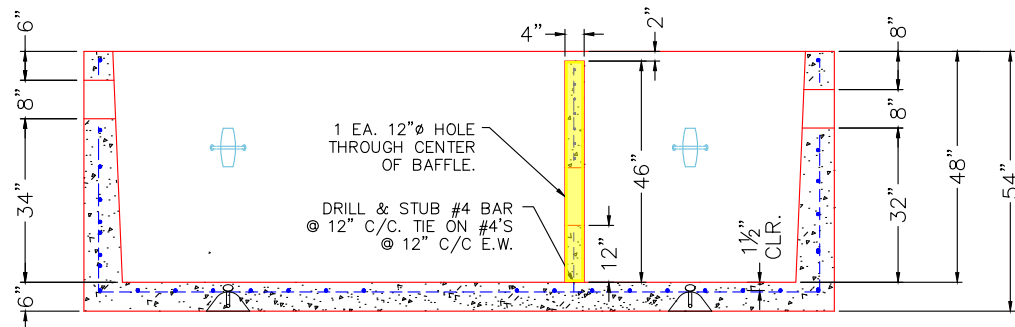

SECTION A-A
(RIGHTSIDE-UP)

NOTES:

1. PER ASTM C-890-13 LATEST REVISION.
2. CONCRETE = 5,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60). (H-20 TRAFFIC RATED DESIGN)
4. SEALED WITH 1" CS-102 (DOUBLE). (6 EA. 14.5' ROLLS REQ'D.)
5. POUR BASE THEN POUR INTERIOR BAFFLE
6. SECOND POUR (BAFFLE WALL) - 1,073 LBS

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 6"
Floor Height: 6"

Height (Int): 48"
Height (Ext): 54"

Weight (Net): 19267 lb
Volume (Net): 4.92cu.yd
