

Job Name: 26-2840 - Cumberland Pipeline Platform Lids
Job Location: Ohio County,KY
Contractor: Cumberland Pipeline LLC

Plant: 100

7/22/2026 2:43:11 PM

Tech: Jared - F

PC: E. Bradley



Structure ID: QL1-2

P1 CTS

87IN X 87IN OD FLAT TOP SPEC. (w/ 24IN ECC HOLE)

P1) 87" x 87" - 87IN X 87IN OD FLAT TOP SPEC. (w/ 24IN ECC HOLE) - 8"



Structure Total:

4777 lb

4777 lb

GENERAL NOTES:

1. MANUFACTURED PER ASTM C913 SPECIFICATIONS.
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60)
TOP SLAB = #5 BARS AT 6" C.C.E.W.
4. WEIGHTS:
TOP SLAB.....4,785 LBS.

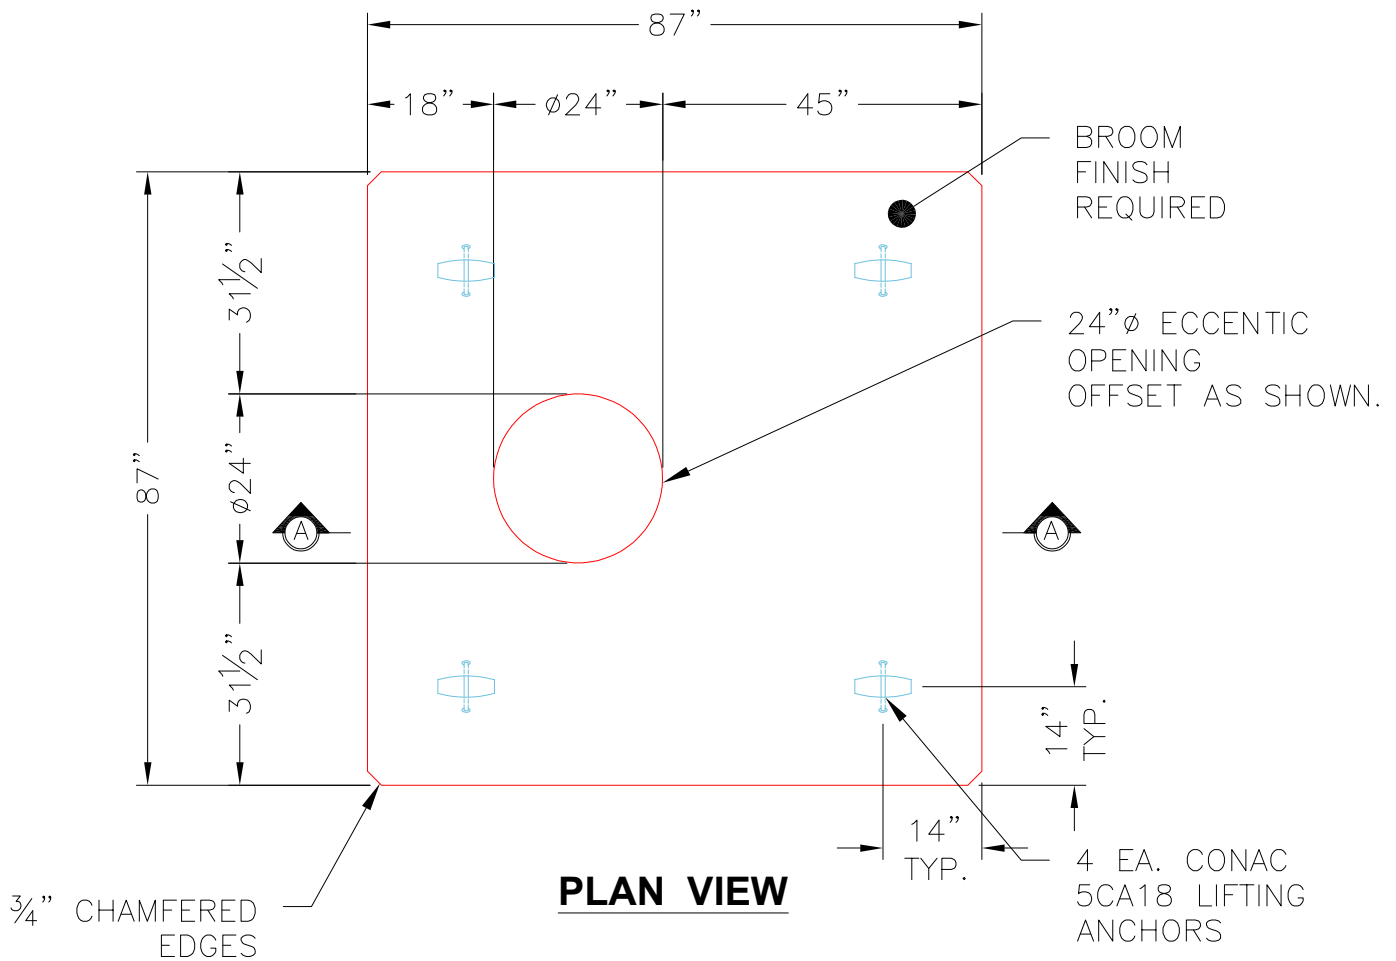

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 0"

Height (Ext): 8"

Weight (Net): 4777 lb
Volume (Net): 1.22cu.yd
