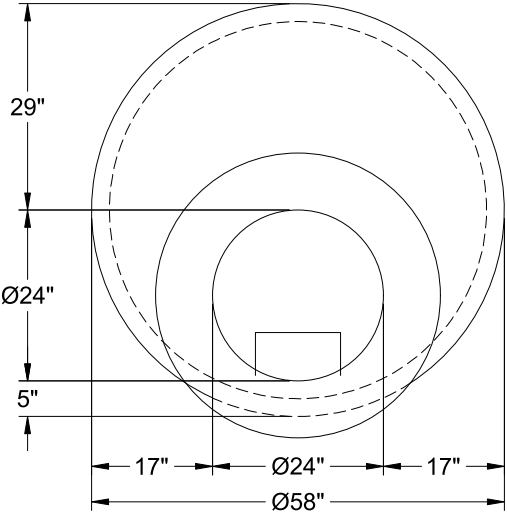



Job Name: 26-2863 - ORA Rail Improvemnet Job Location: Owensboro, KY Contractor: Scotty's Contracting & Stone, LLC		Plant: Beaver Dam, KY 9/15/2026 8:33:03 AM	Tech: J. Ross PC: M. Sullivan	
Structure ID: QL2 MHB				
P4 MH048CN30		ECC CONE w/ 24" HOLE F/G		
P5) 24" - CASTING HEIGHT - 8" P4) 48" - ECC CONE w/ 24" HOLE F/G - 30" P3) 48" - MH RISER T/G - 36" P2) 72" - MH Transition Slab 48" Hole T/G - 15" P1) 72" - MH BASE (10"F) Custom Ht T/n - 84" 1) CASTING - HOE KY-510 F/C (KY TY2) 1) 72" - Conseal CS-102 1.00" 2) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 54 14) MH Step ML-10-TDS-NCR - 10"		0 lb 2050 lb 2515 lb 3864 lb 14144 lb 510 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 23083 lb	<u>Structure Notes:</u> 1. PER KYTC MH B / ASTM C478 SPEC'S 2. CONCRETE = 4,000 PSI AT 28 DAYS 3. REINFORCING PER ASTM A615 (GRADE 60) 4. HOE KY-510 F/C (KY TY2) CASTING PROVIDED BY ICAST	
				
 48" - ECC CONE w/ 24" HOLE F/G - 30" - (P4)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 2050 lb Volume (Net): 0.41cu.yd
