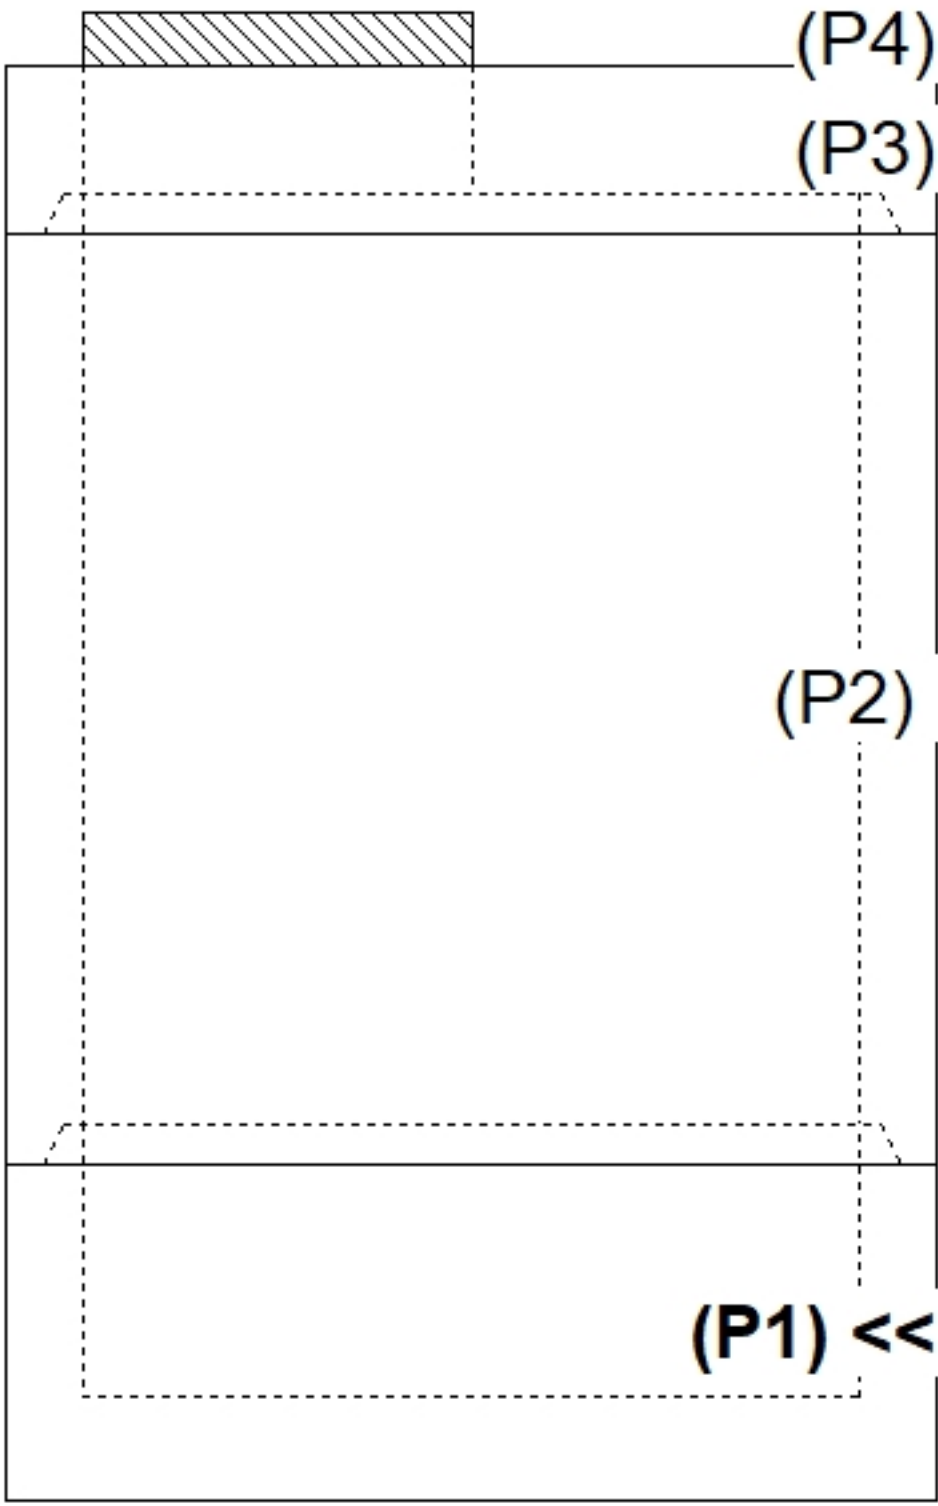
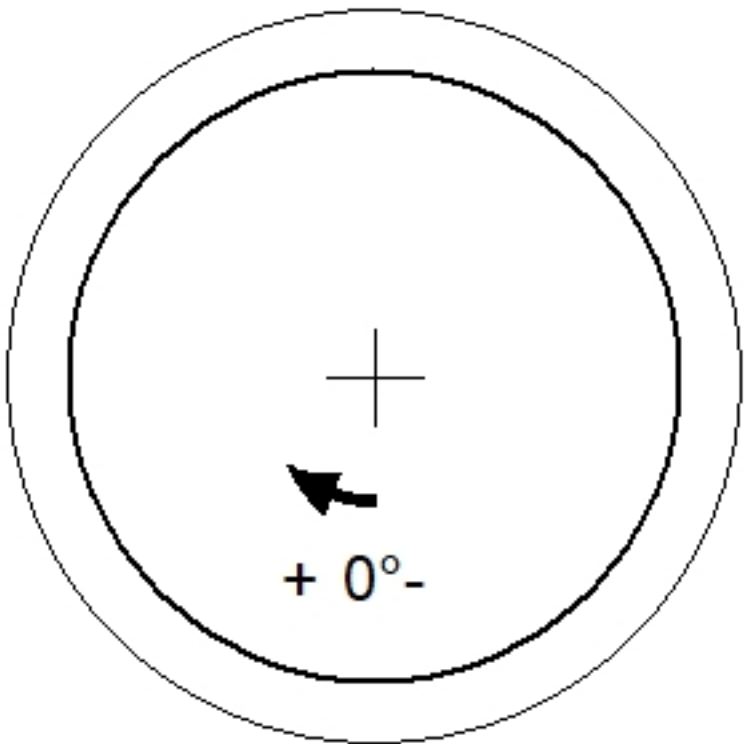
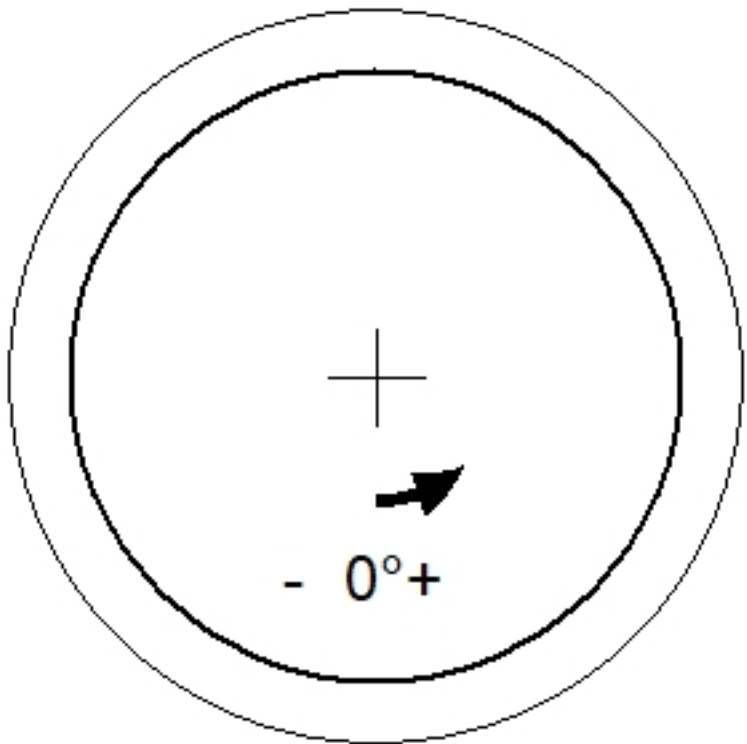
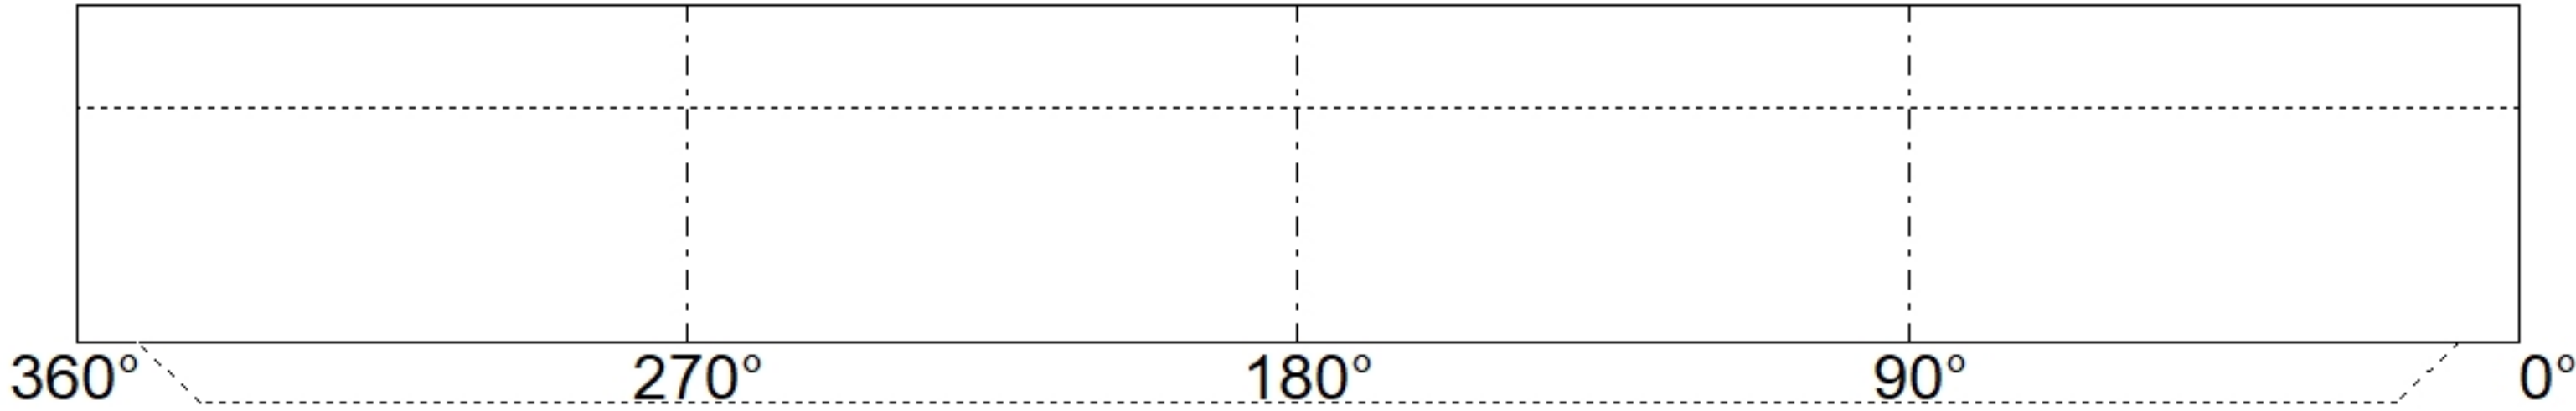


Job Name: 26-2877 839248 Aloft Job Location: Paducah, KY Contractor: Contech Engineering Solutions						Plant: Beaver Dam 7/1/2026 10:01:59 AM		Tech: S. Felletter PC: C. Goff			
Structure ID: 25-CS-5											
P1		MH060BA18		MH BASE T/n							
P4) 30" - CASTING HEIGHT - 4" P3) 60" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 13" P2) 60" - MH RISER SPECIAL T/G - 72" P1) 60" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 2) 60" - Conseal CS-102 1.00" 2) Hole - 36						0 lb 2589 lb 6430 lb 4612 lb 0 lb 0 lb 0 lb 0 lb ----- 13631 lb Structure Total:		Structure Notes: 4" CASTING BY OTHERS LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE ICAST TO INSTALL THE INTERNALS CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE			
Rim: 335.66' Rim to Invert: 4.06' Slack: -0.164" Sump: 58.116" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
						RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS  8" 18" EXT					
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 6" Floor Height: 8"		Height (Int): 18" Height (Ext): 26"		Weight (Net): 4612 lb Volume (Net): 1.18cu.yd		
