

Job Name: 26-2884 - Toyota Boshoku Parking Lot
Job Location: Lebanon, KY 40033
Contractor: McCain Bros Excavating LLC

Plant: 100

7/21/2026 11:13:12 AM

Tech: Jared - F
PC: M. Sullivan



Structure ID: KY-S-7 MHA

P2 BX024024-08LD08

CB FLAT TOP 8"W SOLID

- P2) 24" x 24" - CB FLAT TOP 8"W SOLID - 8"
P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht - 21"
1) 24" x 24" - Conseal CS-102 1.00"
1) DOGHOUSE INVRTD - 24"x22"
1) DOGHOUSE INVRTD - 20"x21"
1) Hole - 12


1074 lb
2295 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 3369 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. SOLID TOP SLAB - NO CASTING.

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As. 62) #5 BARS AT 6" C.C.E.W.
- WALLS (As. 31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As. 31) #5 BARS AT 12" C.C.E.W.

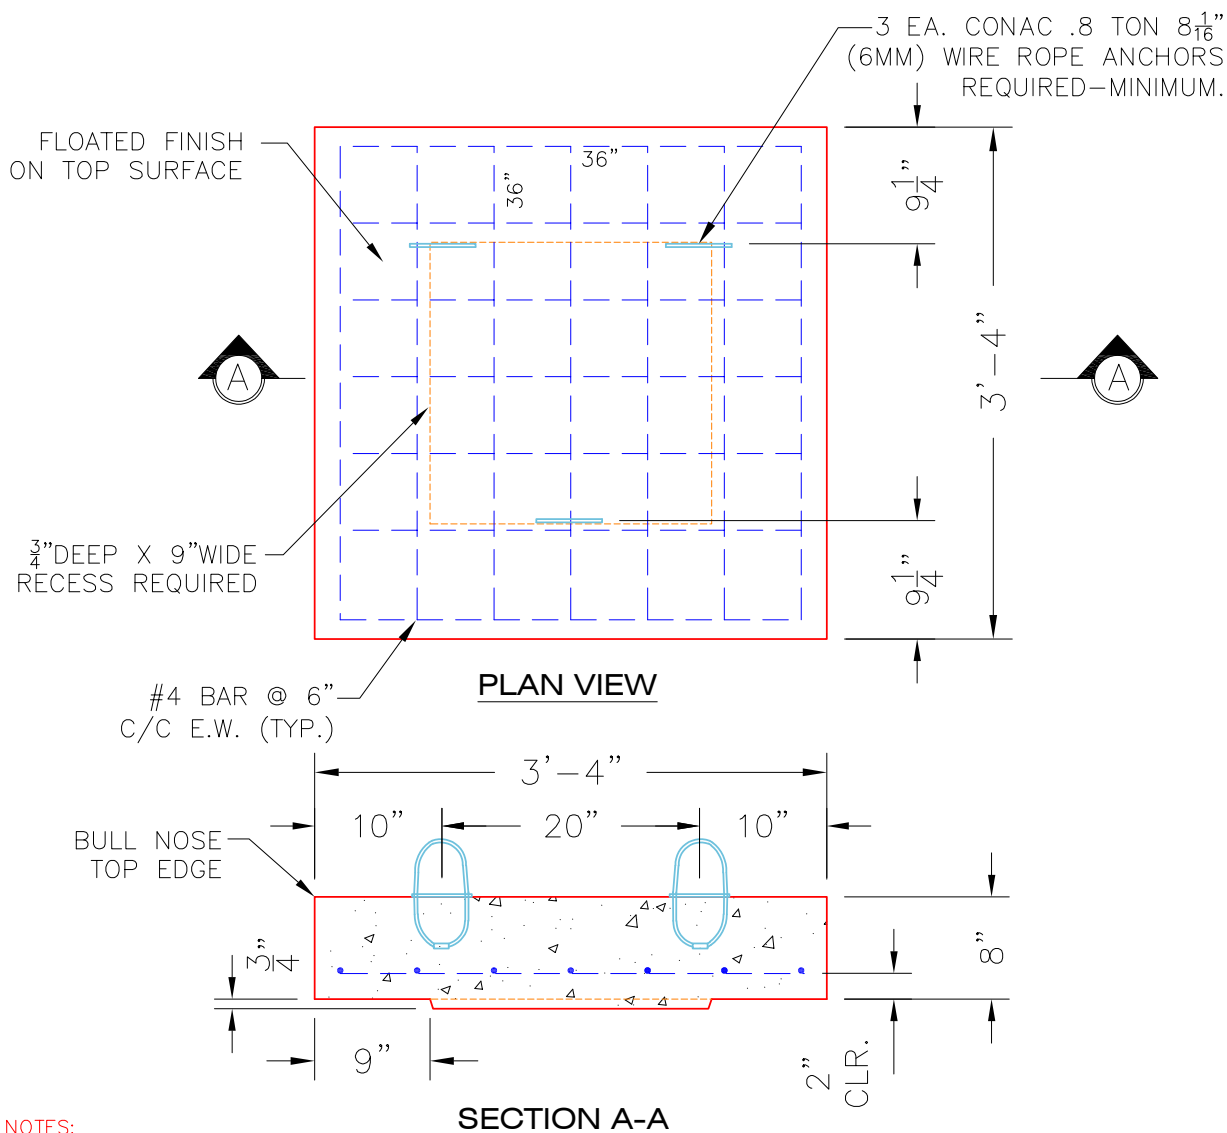

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- MANUFACTURE TO KYTC SPECIFICATIONS.
- REINFORCING: #4 BAR @ 6" C/C E.W.-GRADE 60.
(BOTTOM LAYER ONLY)
- 3 EA. CONAC WIRE LOOP LIFTERS REQUIRED.

#4 BAR CUT LIST
14 EA. @ 36"

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1074 lb
Volume (Net): 0.27cu.yd
