



Job Name: 26-2889 - 1605 Seminary Street Job Location: Nashville, TN 37207 Contractor: Hayes Pipe Supply					Plant: 100 7/27/2026 8:29:01 PM		Tech: Jared - F PC: E. Bradley				
Structure ID: One SS-MH											
P1 MH048BA36CDARED			MH BASE w/ConBlock-CDA Red T/n								
P4) 32" - CASTING HEIGHT - 6" P3) 32" - GRADE RING w/ConBlock-CDA Red F/F - 4" P2) 48" - MH FLAT TOP w/32" Hole CC w/ConBlock-CDA Red F/G - 12" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 3) MH Step ML-10-TDS-NCR - 10"					0 lb 337 lb 1351 lb 3797 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 8 lb 0 lb ----- 6934 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS (NASH LOGO SAN SEWER F&C). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62)#5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 447.62' Rim to Invert: 4.67' Slack: 0.04" Sump: 2" Step Position: 180°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	442.95'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

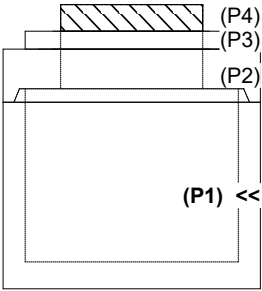

(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

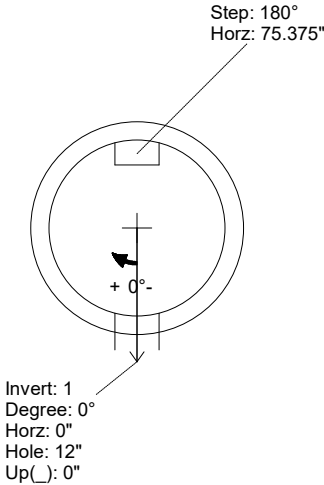

Step: 180°
Horz: 75.375"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"


UPSIDE-DOWN VIEW (int. dimensions)

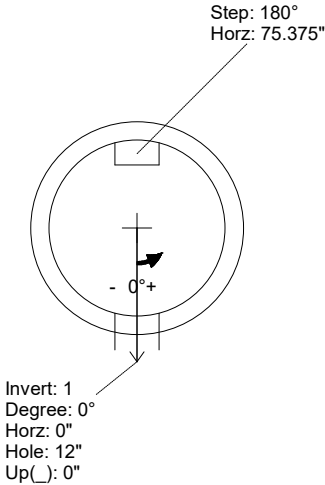

Step: 180°
Horz: 75.375"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

INSIDE WALL DIMENSIONS

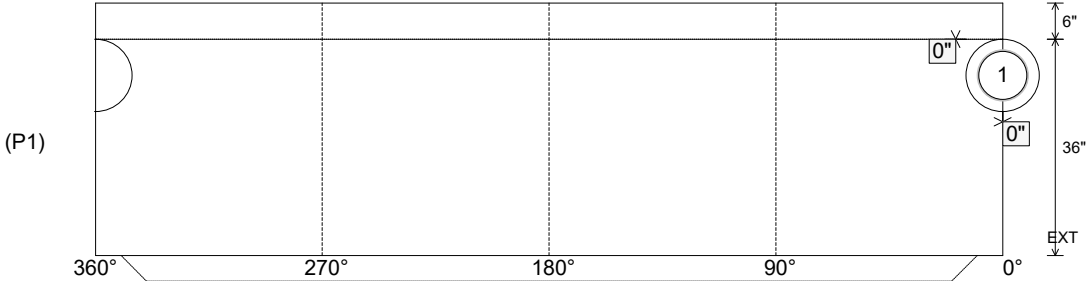


(P1)


360° 270° 180° 90° 0°


0" 36" 6" EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3797 lb Volume (Net): 0.97cu.yd
----------------------------------	---------------------------------	--	--	--


Job Name: 26-2889 - 1605 Seminary Street Job Location: Nashville, TN 37207 Contractor: Hayes Pipe Supply					Plant: 100 7/27/2026 8:29:01 PM		Tech: Jared - F PC: E. Bradley						
Structure ID: One SS-MH													
P1 MH048BA36CDARED			MH BASE w/ConBlock-CDA Red T/n										
P4) 32" - CASTING HEIGHT - 6" P3) 32" - GRADE RING w/ConBlock-CDA Red F/F - 4" P2) 48" - MH FLAT TOP w/32" Hole CC w/ConBlock-CDA Red F/G - 12" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 3) MH Step ML-10-TDS-NCR - 10"						0 lb 337 lb 1351 lb 3797 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 8 lb 0 lb ----- 6934 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS (NASH LOGO SAN SEWER F&C). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62)#5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 447.62' Rim to Invert: 4.67' Slack: 0.04" Sump: 2" Step Position: 180°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	442.95'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"			
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													

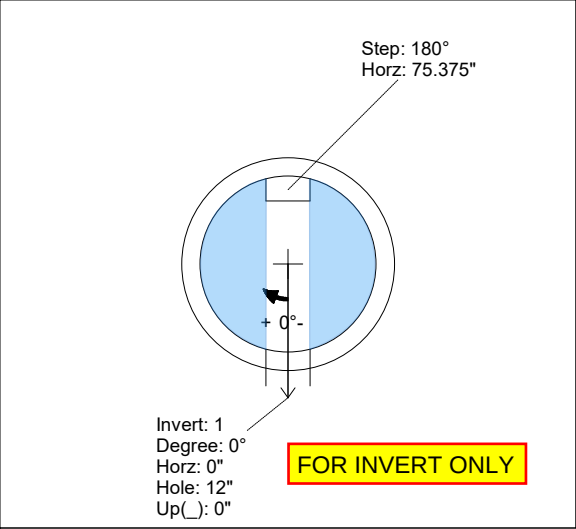

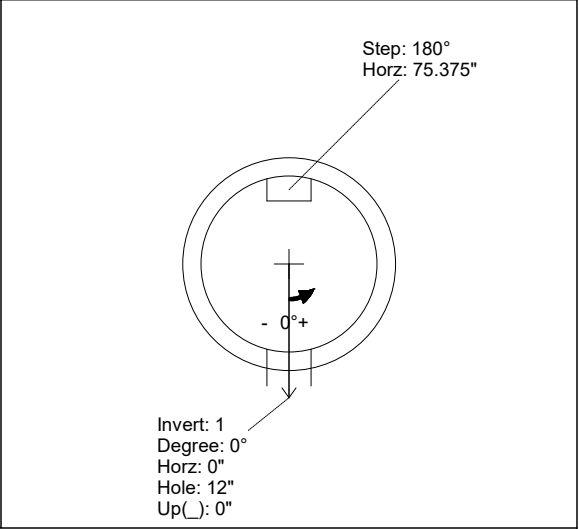

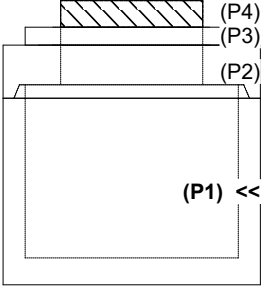

INSIDE WALL DIMENSIONS

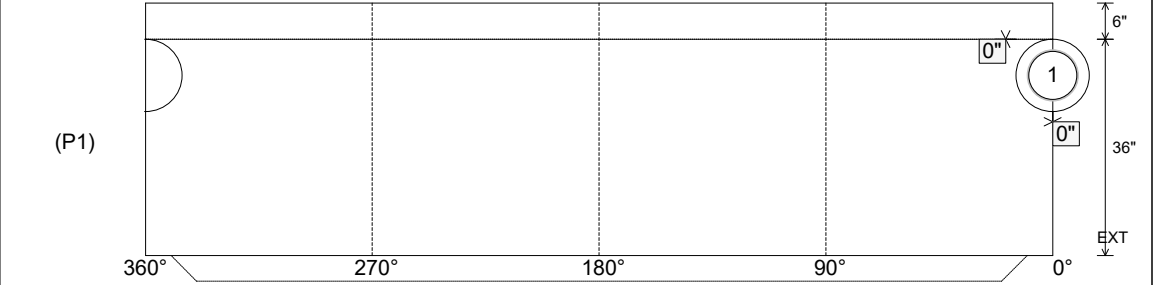

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3797 lb Volume (Net): 0.97cu.yd
----------------------------------	---------------------------------	--	--	--
