

Job Name: 26-2889 - 1605 Seminary Street
Job Location: Nashville, TN 37207
Contractor: Hayes Pipe Supply

Plant: 100

7/27/2026 8:29:17 PM

Tech: Jared - F
PC: E. Bradley



Structure ID: One SS-MH

P2 MH048LD12SCDARED

MH FLAT TOP w/32" Hole CC w/ConBlock-CDA Red F/G

- P4) 32" - CASTING HEIGHT - 6"
P3) 32" - GRADE RING w/ConBlock-CDA Red F/F - 4"
P2) 48" - MH FLAT TOP w/32" Hole CC w/ConBlock-CDA Red F/G - 12"
P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 36"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
1) ADMIXTURE CONBLOCK CDA RED
1) 48" - Conseal CS-102 1.00" (Double)
1) PSX - 12-08 NYLO
3) MH Step ML-10-TDS-NCR - 10"

0 lb
337 lb
1351 lb
3797 lb
0 lb
0 lb
1440 lb
0 lb
0 lb
0 lb
8 lb
0 lb


Structure Total: 6934 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING SUPPLIED BY OTHERS (NASH LOGO SAN SEWER F&C).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62)#5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

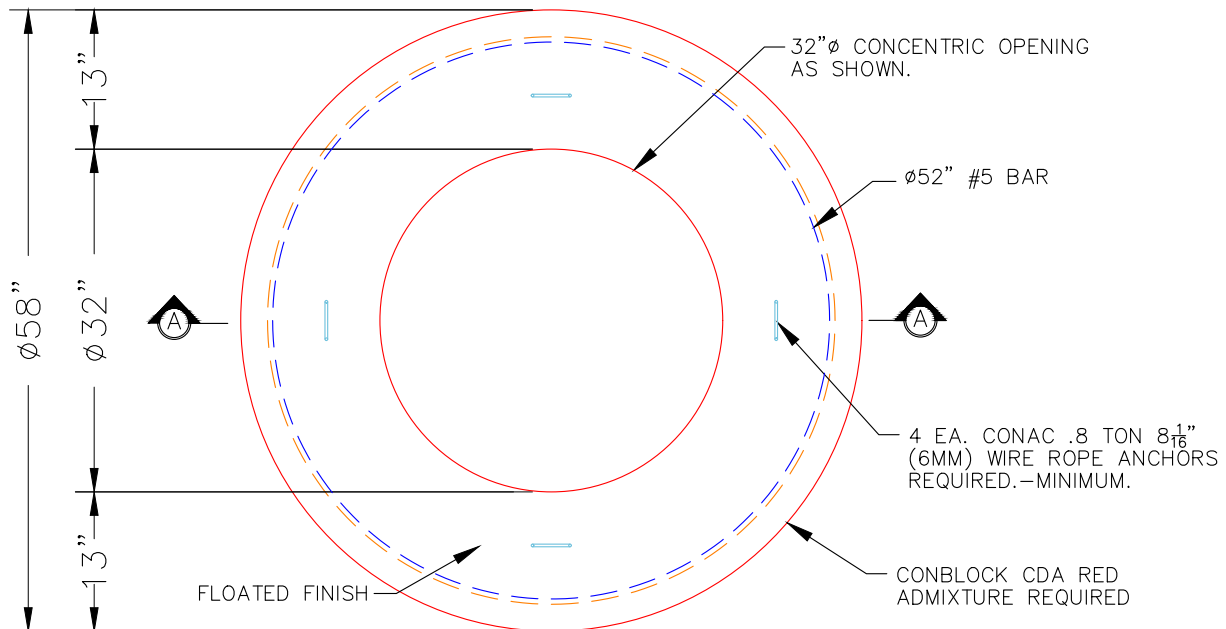

PLAN VIEW

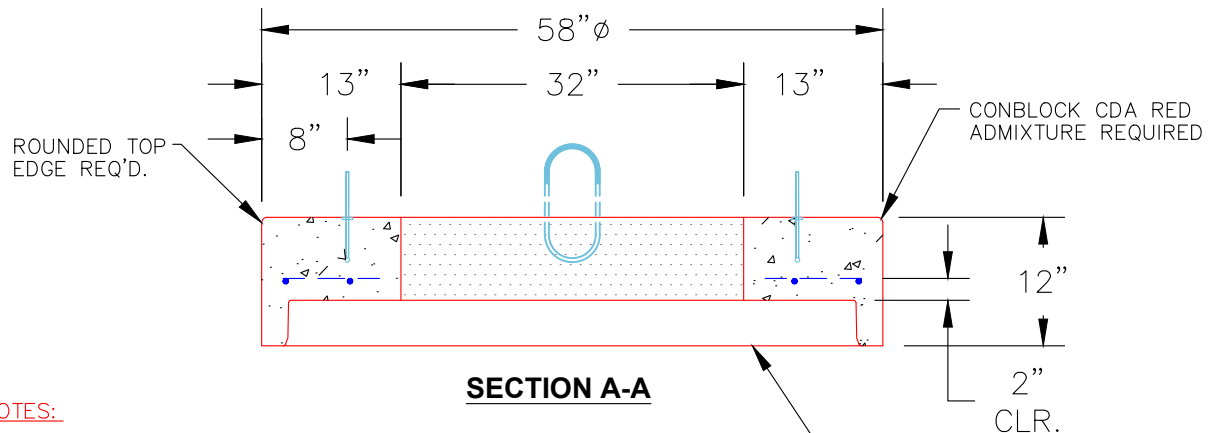

SECTION A-A

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1351 lb
Volume (Net): 0.34cu.yd
