

Contractor: City of Leitchfield

TECH: S. Felleter

Plant: Beaver Dam



Spec: Sanitary
Type: SAN.MH
Size: 48"


Rim: 1.333'
Invert: 0'
Rim to Invert: 1.333'

Sump: 2"
Floor (Top): -0.167'
Floor Height: 6"

Floor (Bot): -0.667'
Overall Height: 2'
Slack: 0"


REINFORCING PER ASTM A615 (GRADE 60).
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 3948 lb

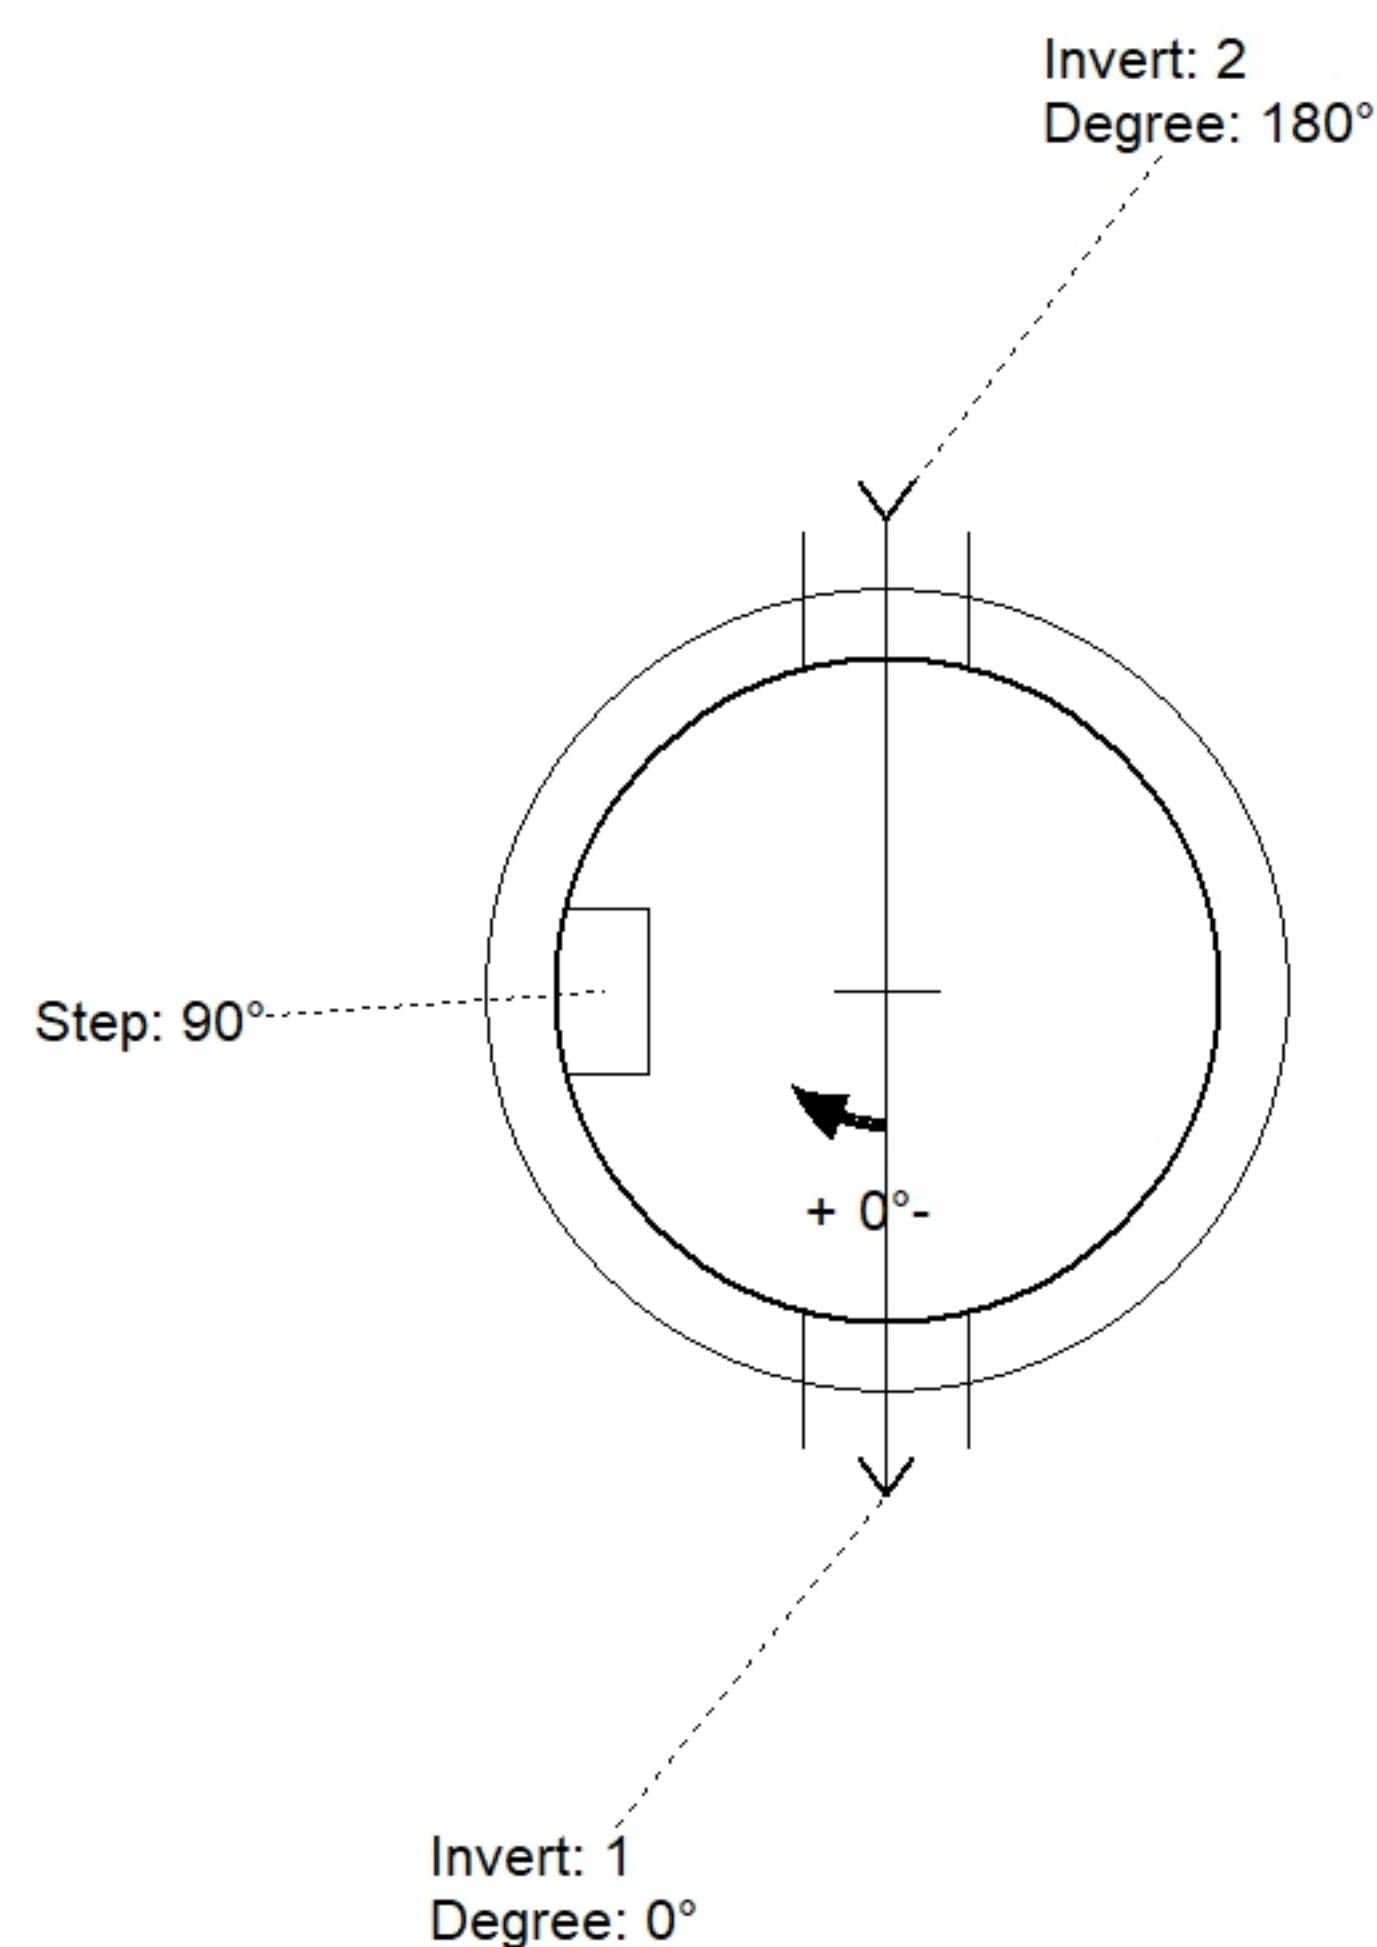

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	1.333'							
Reducer								
Invert 1	0'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	0.1'	180°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	0.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

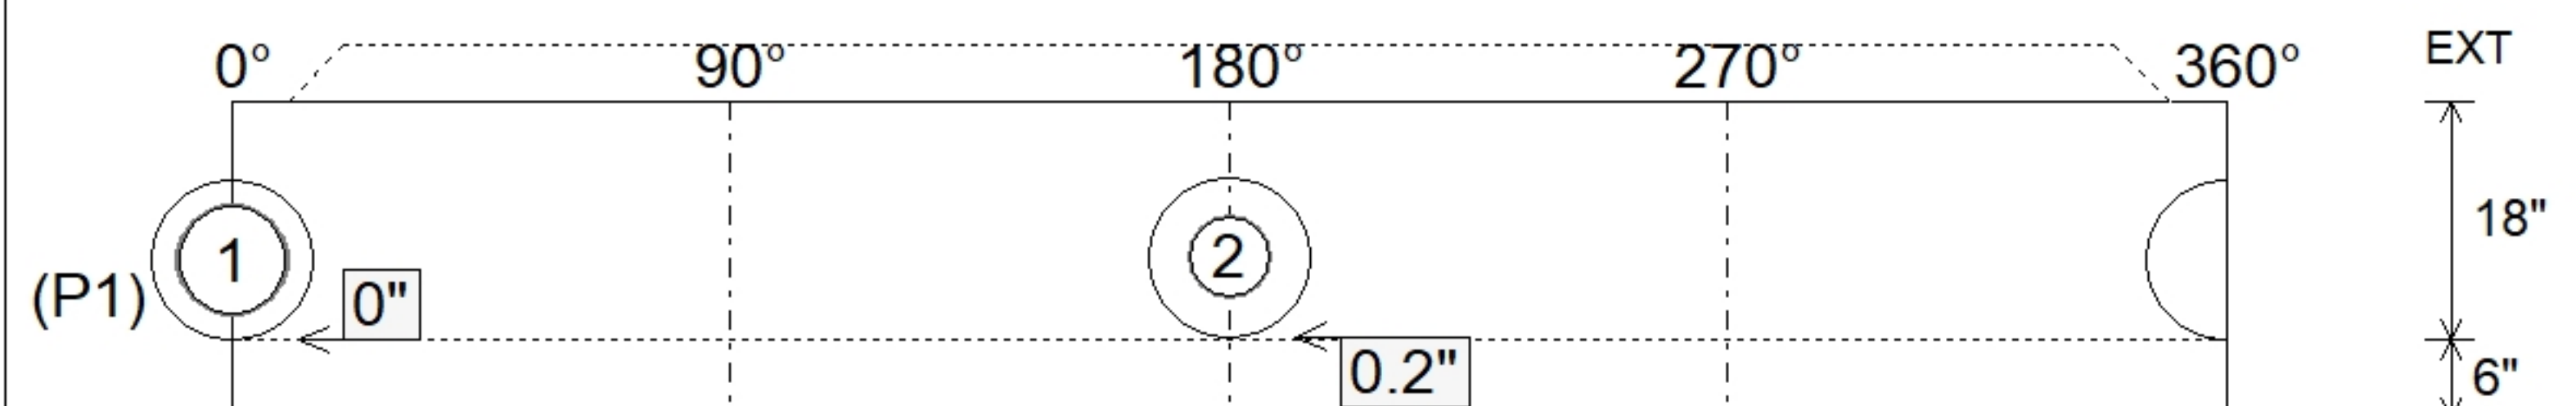

Submittal Drawing
8/19/2026 3:22:05 PM

SUBMITTAL
APPROVED BY:
