



Structure Notes:


1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE 360 L VANE SET).

REINFORCING PER ASTM A615 (GRADE 60).


- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:	
P3) 24" x 30" - CASTING HEIGHT - 4"	0 lb
P2) 24" x 36" - BX FLAT LID 8inW w/24"x30" HOLE F/F - 8"	913 lb
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 23"	3432 lb
1) CASTING - HOE 360 Set (F/G/H)	362 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
2) Hole - 16	0 lb


Structure Total:	4707 lb

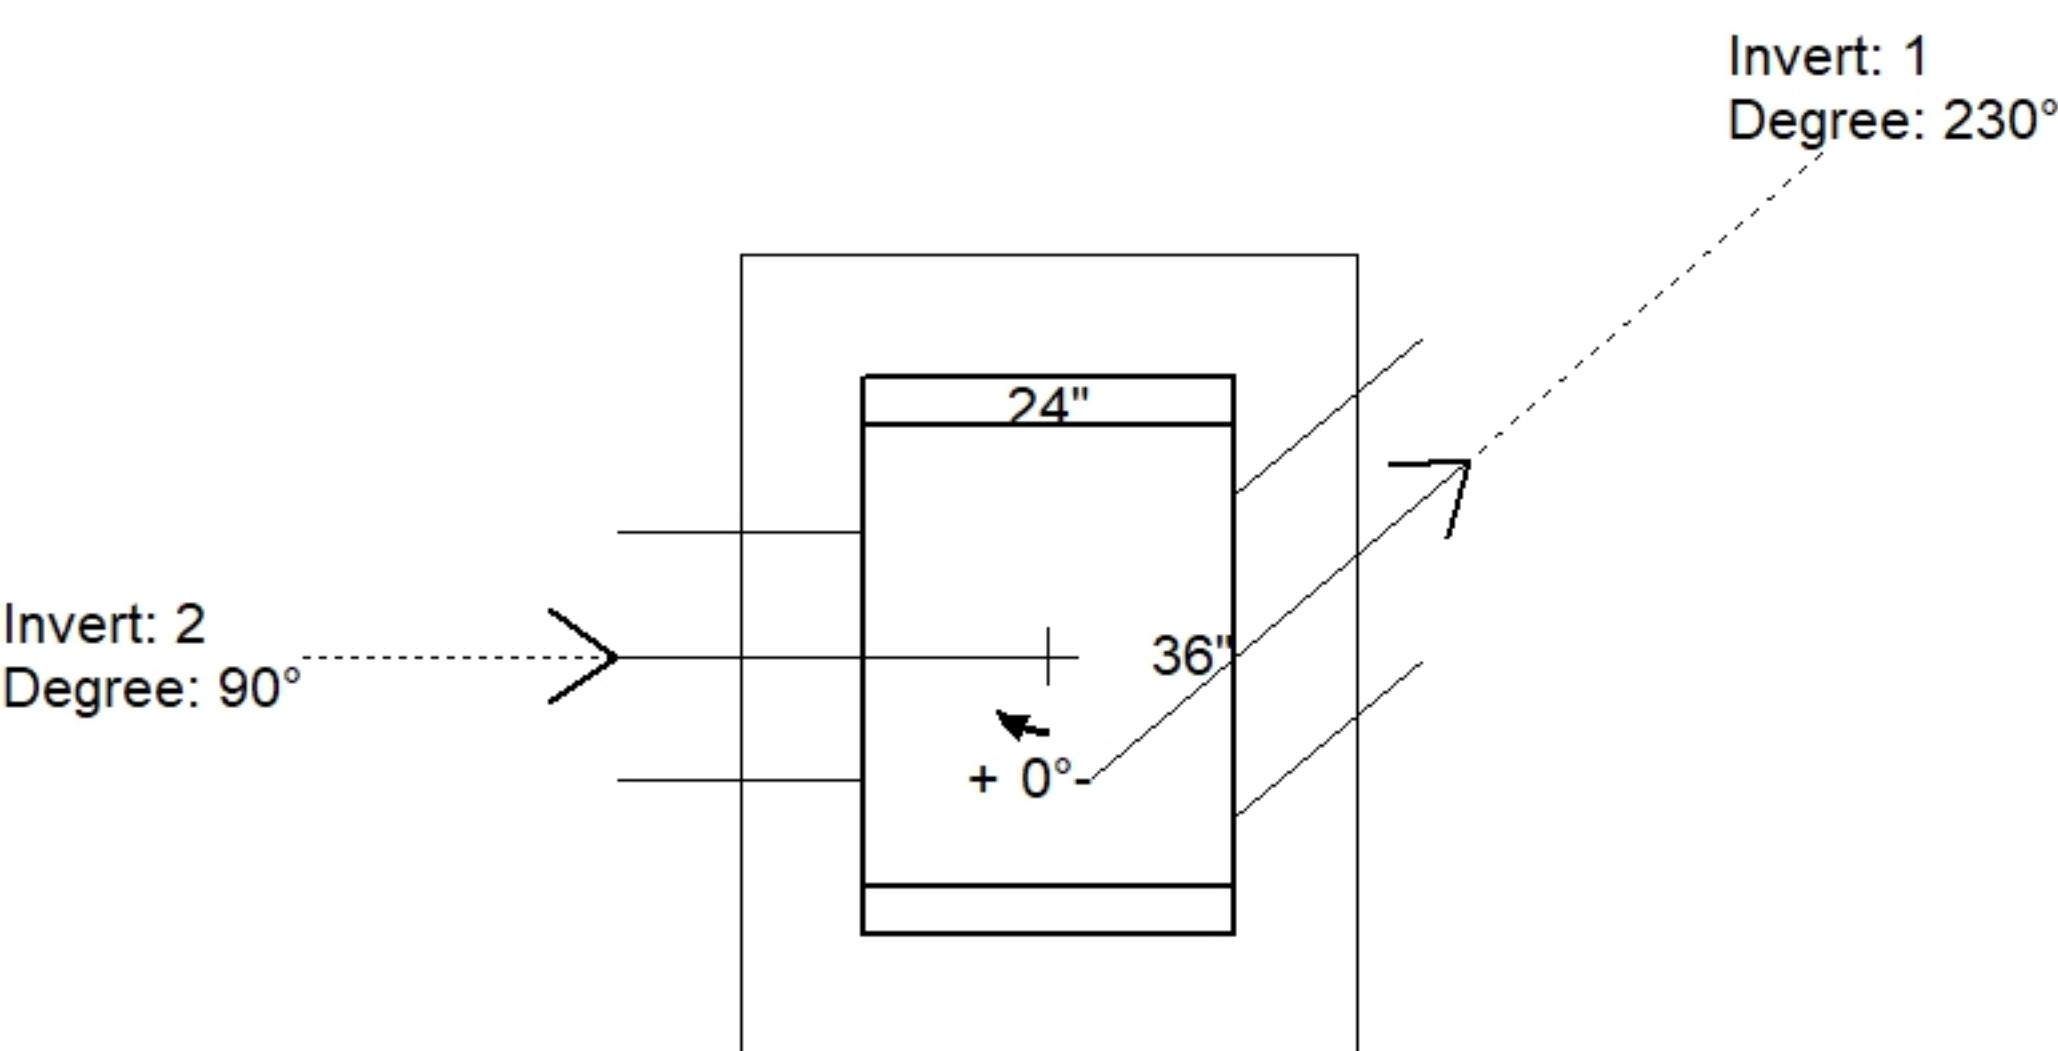

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')_	Ref
Rim	560.37'							
Reducer								
Invert 1	557.4'	230°	12" HDPE	14.5"	16"	Hole 16	0"	P1
Invert 2	557.4'	90°	12" HDPE	14.5"	16"	Hole 16	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

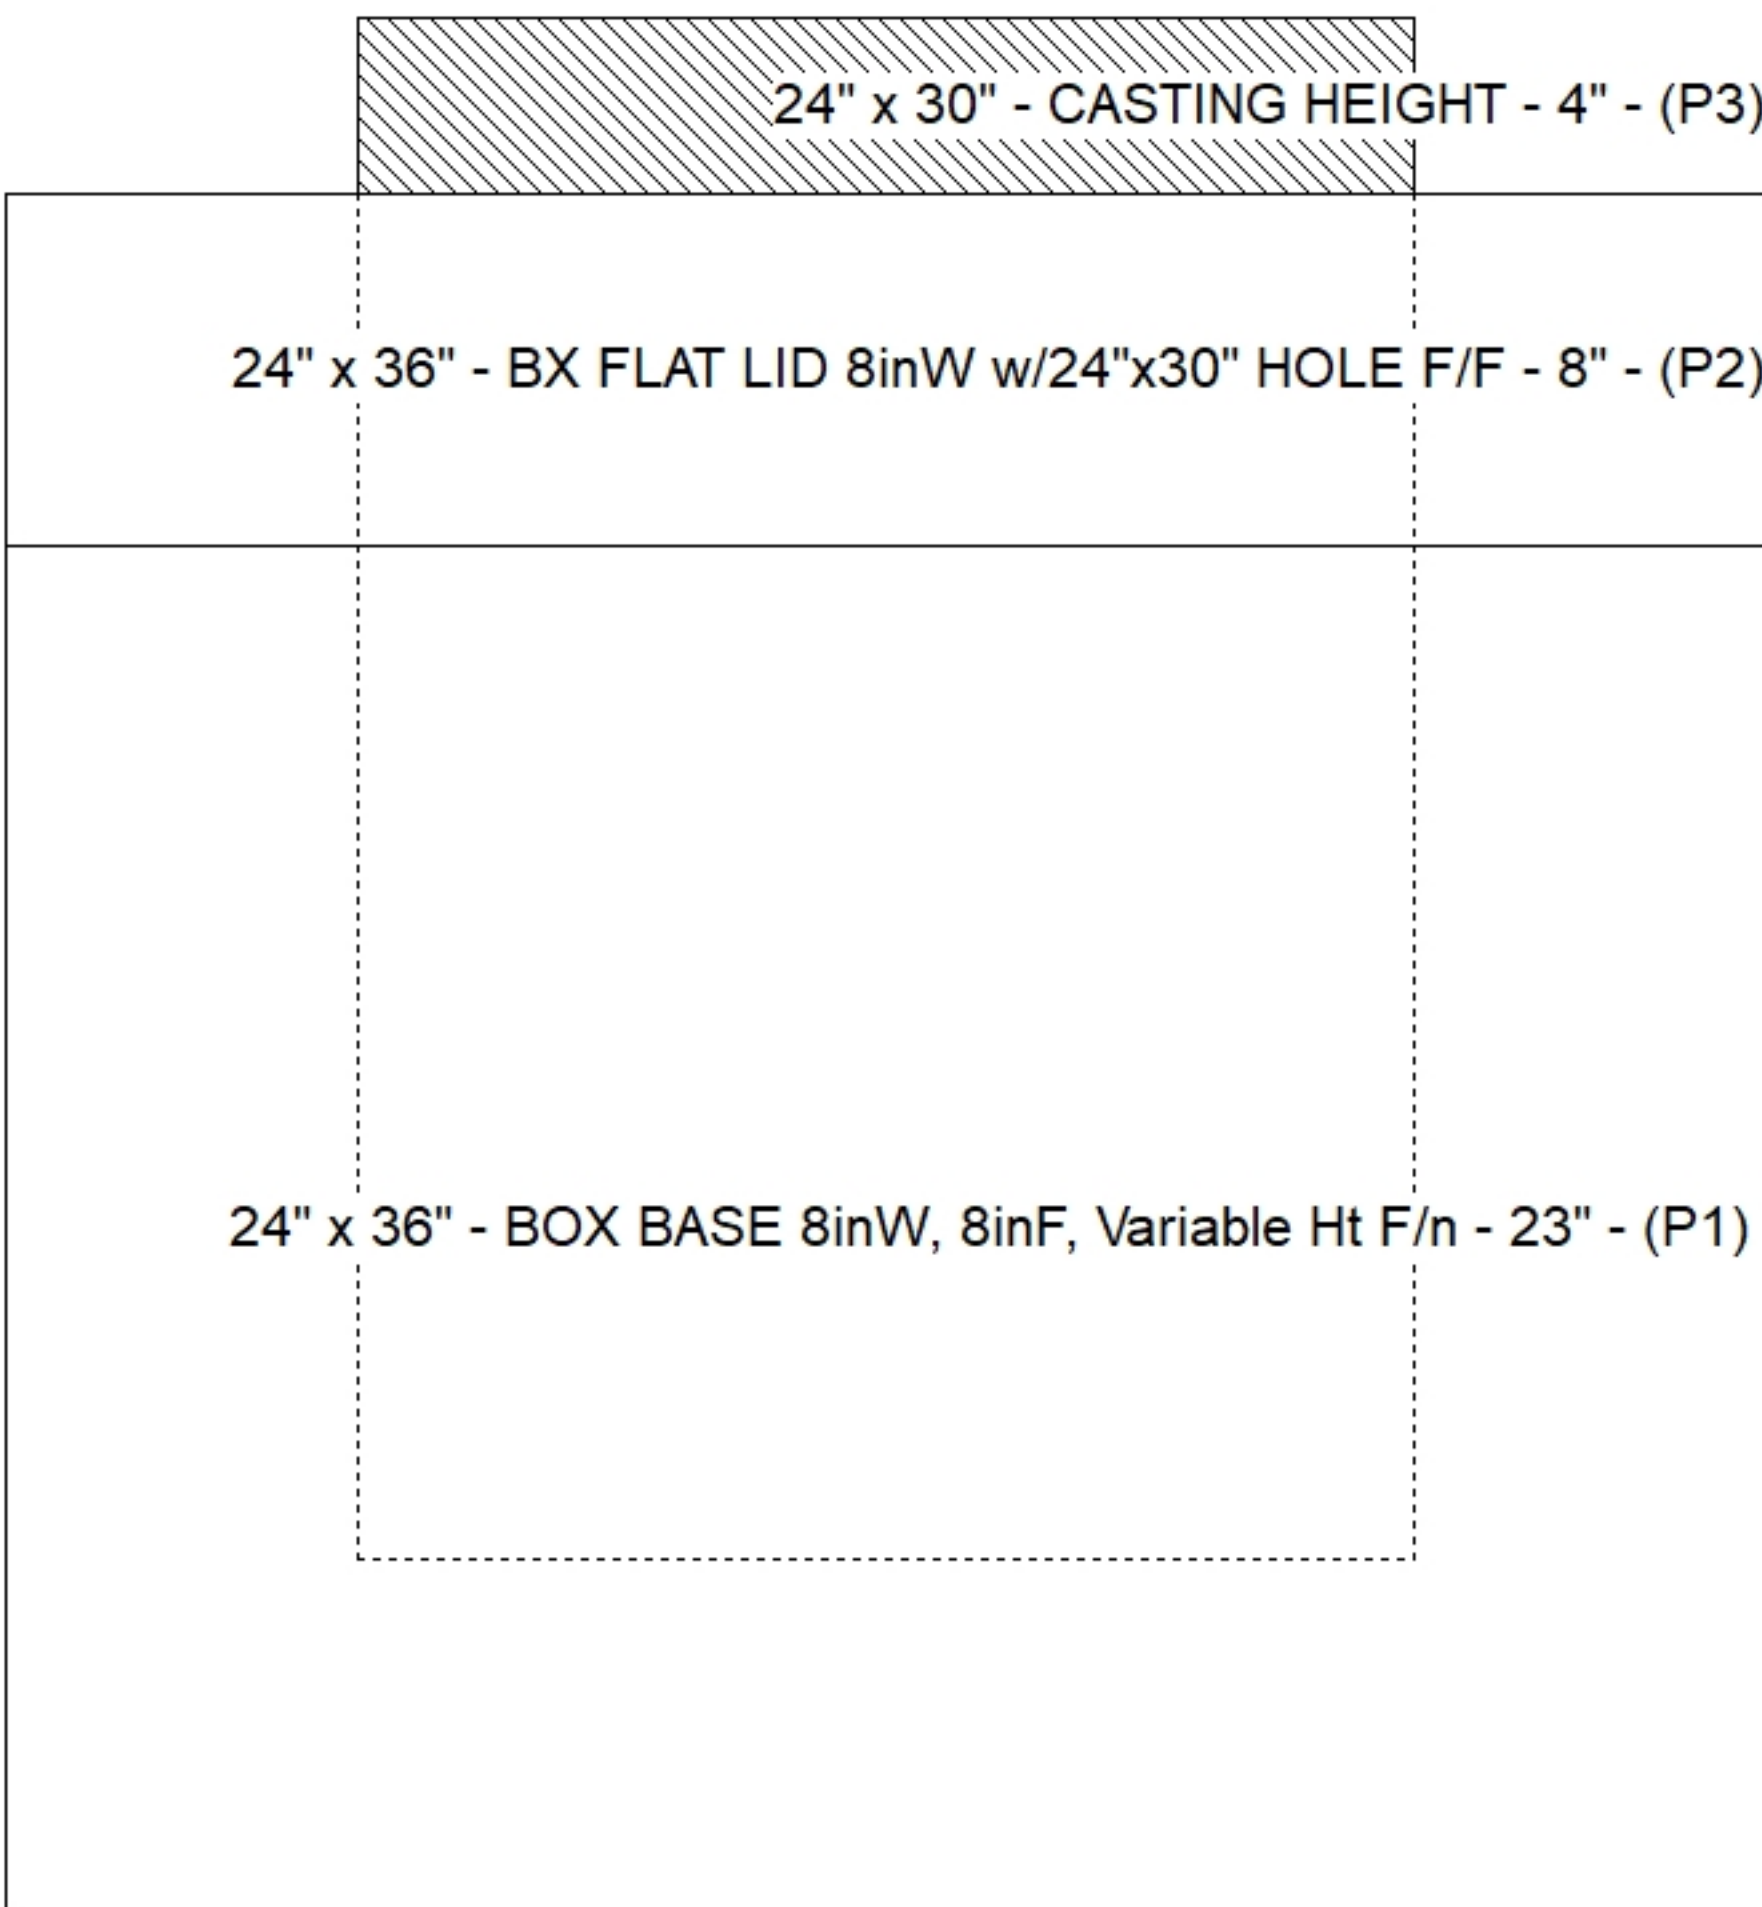

Default - Interior Dimensions

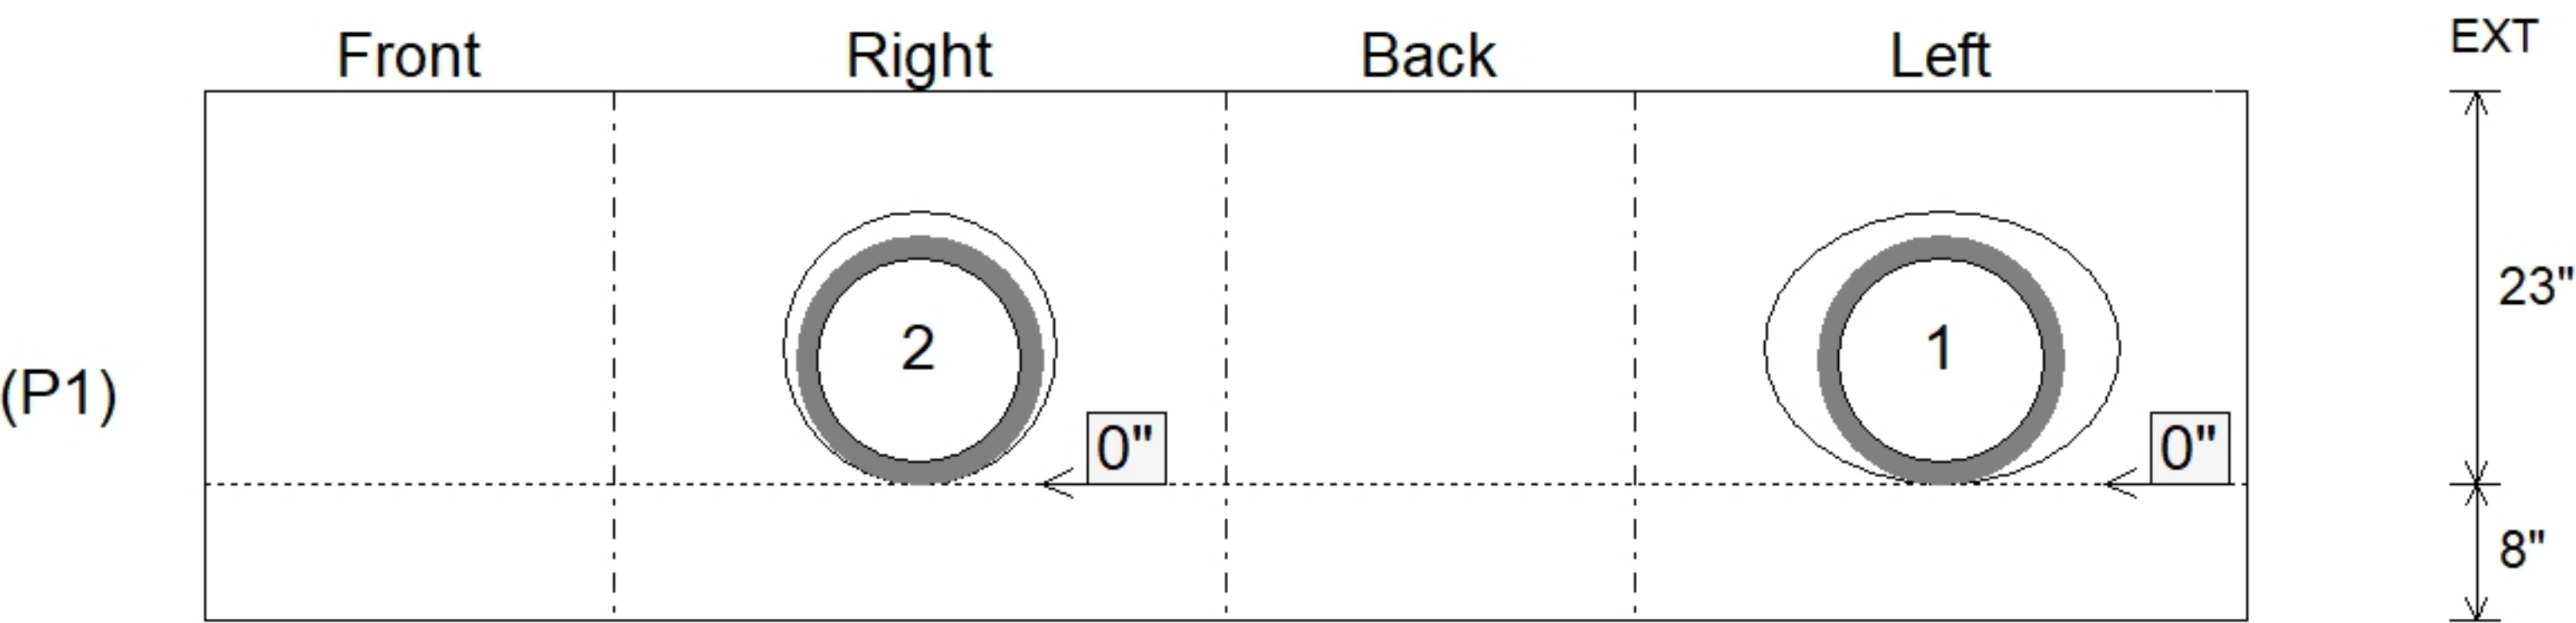

Submittal Drawing
7/27/2026 9:05:40 AM

SUBMITTAL
APPROVED BY:
