

Contractor: Blankenberger Brothers, Inc.

TECH: Jared - F

Plant: 100




Slack: 0.91"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P4) 24" - CASTING HEIGHT - 1.25"
P3) 48" - ECC CONE w/ 24" HOLE - 24"
P2) 48" - MH RISER Custom Ht - 57"
P1) 48" - MH BASE w/FLANGE - 72"
2) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
1) Hole - 20
1) Hole - 26

0 lb
1550 lb
3749 lb
7628 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 12926 lb

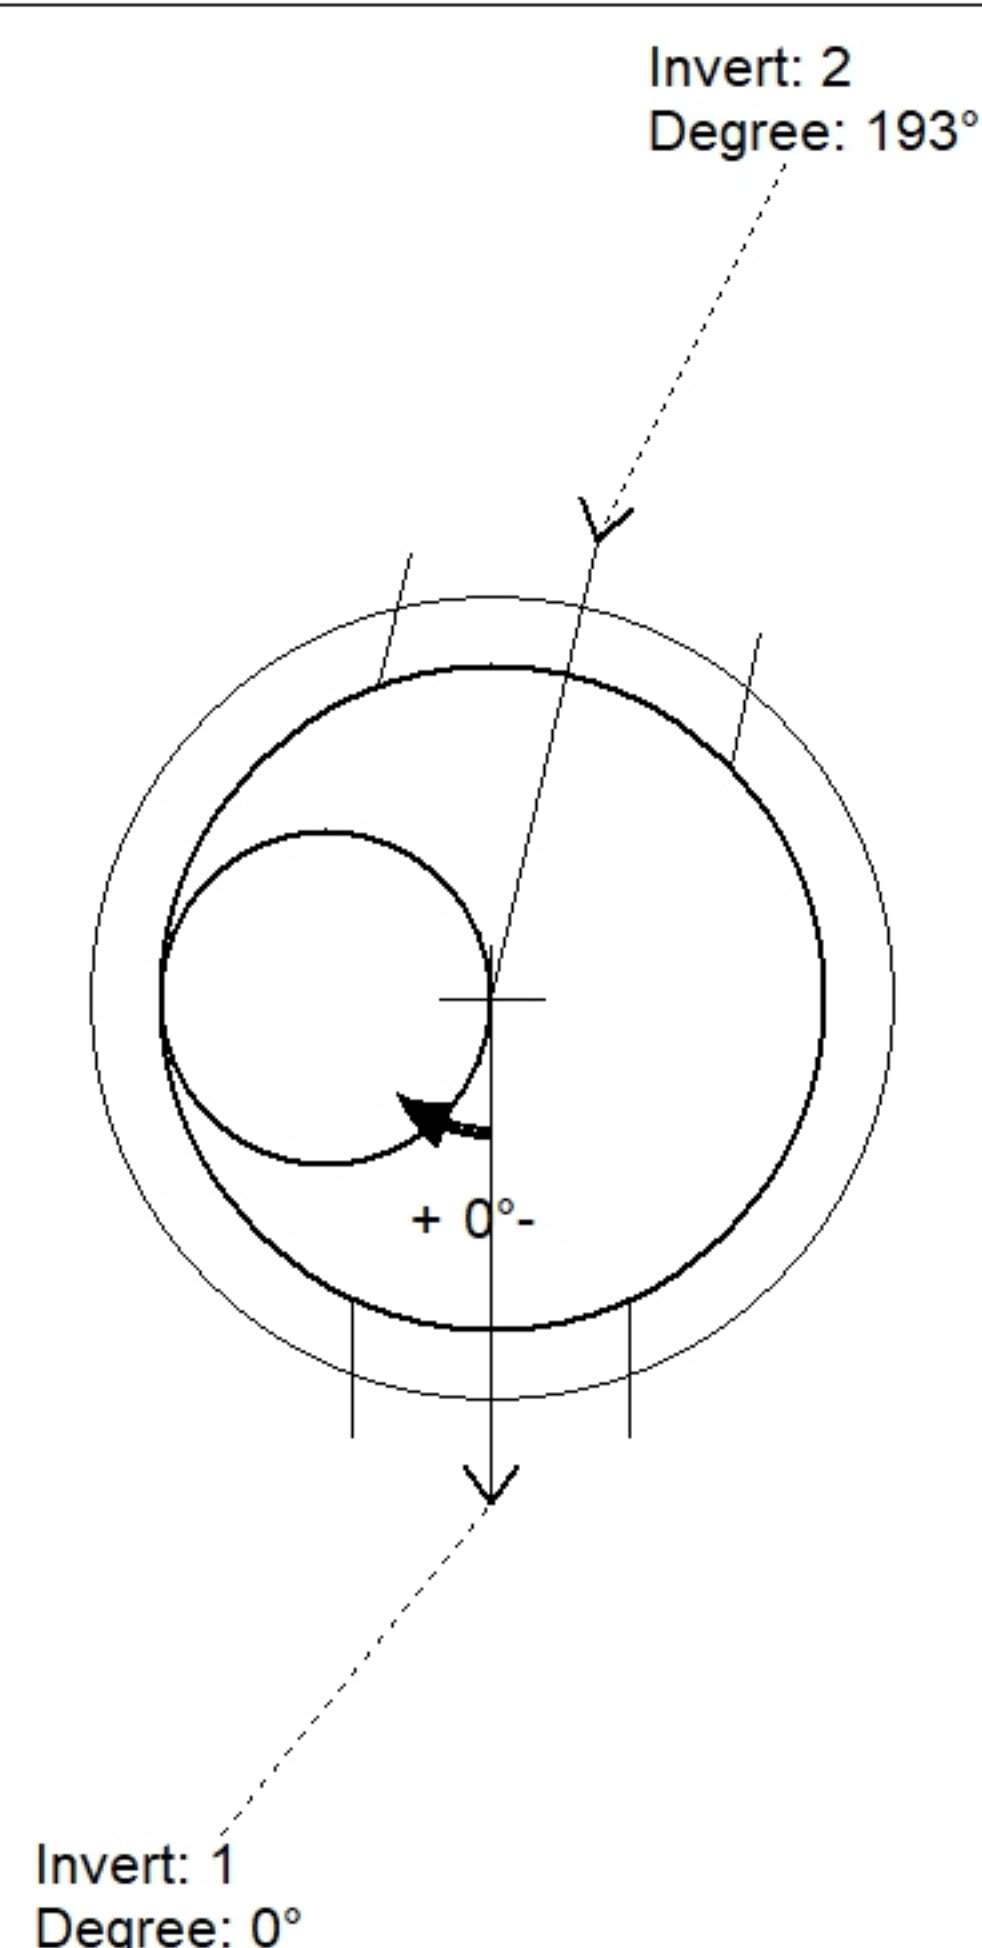

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	385.3'							
Reducer								
Invert 1	372.42'	0°	18" A-2000	19.2"	20"	Hole 20	0"	P1
Invert 2	380.74'	193°	18" RCP B WALL	23"	26"	Hole 26	21.69"	P2
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

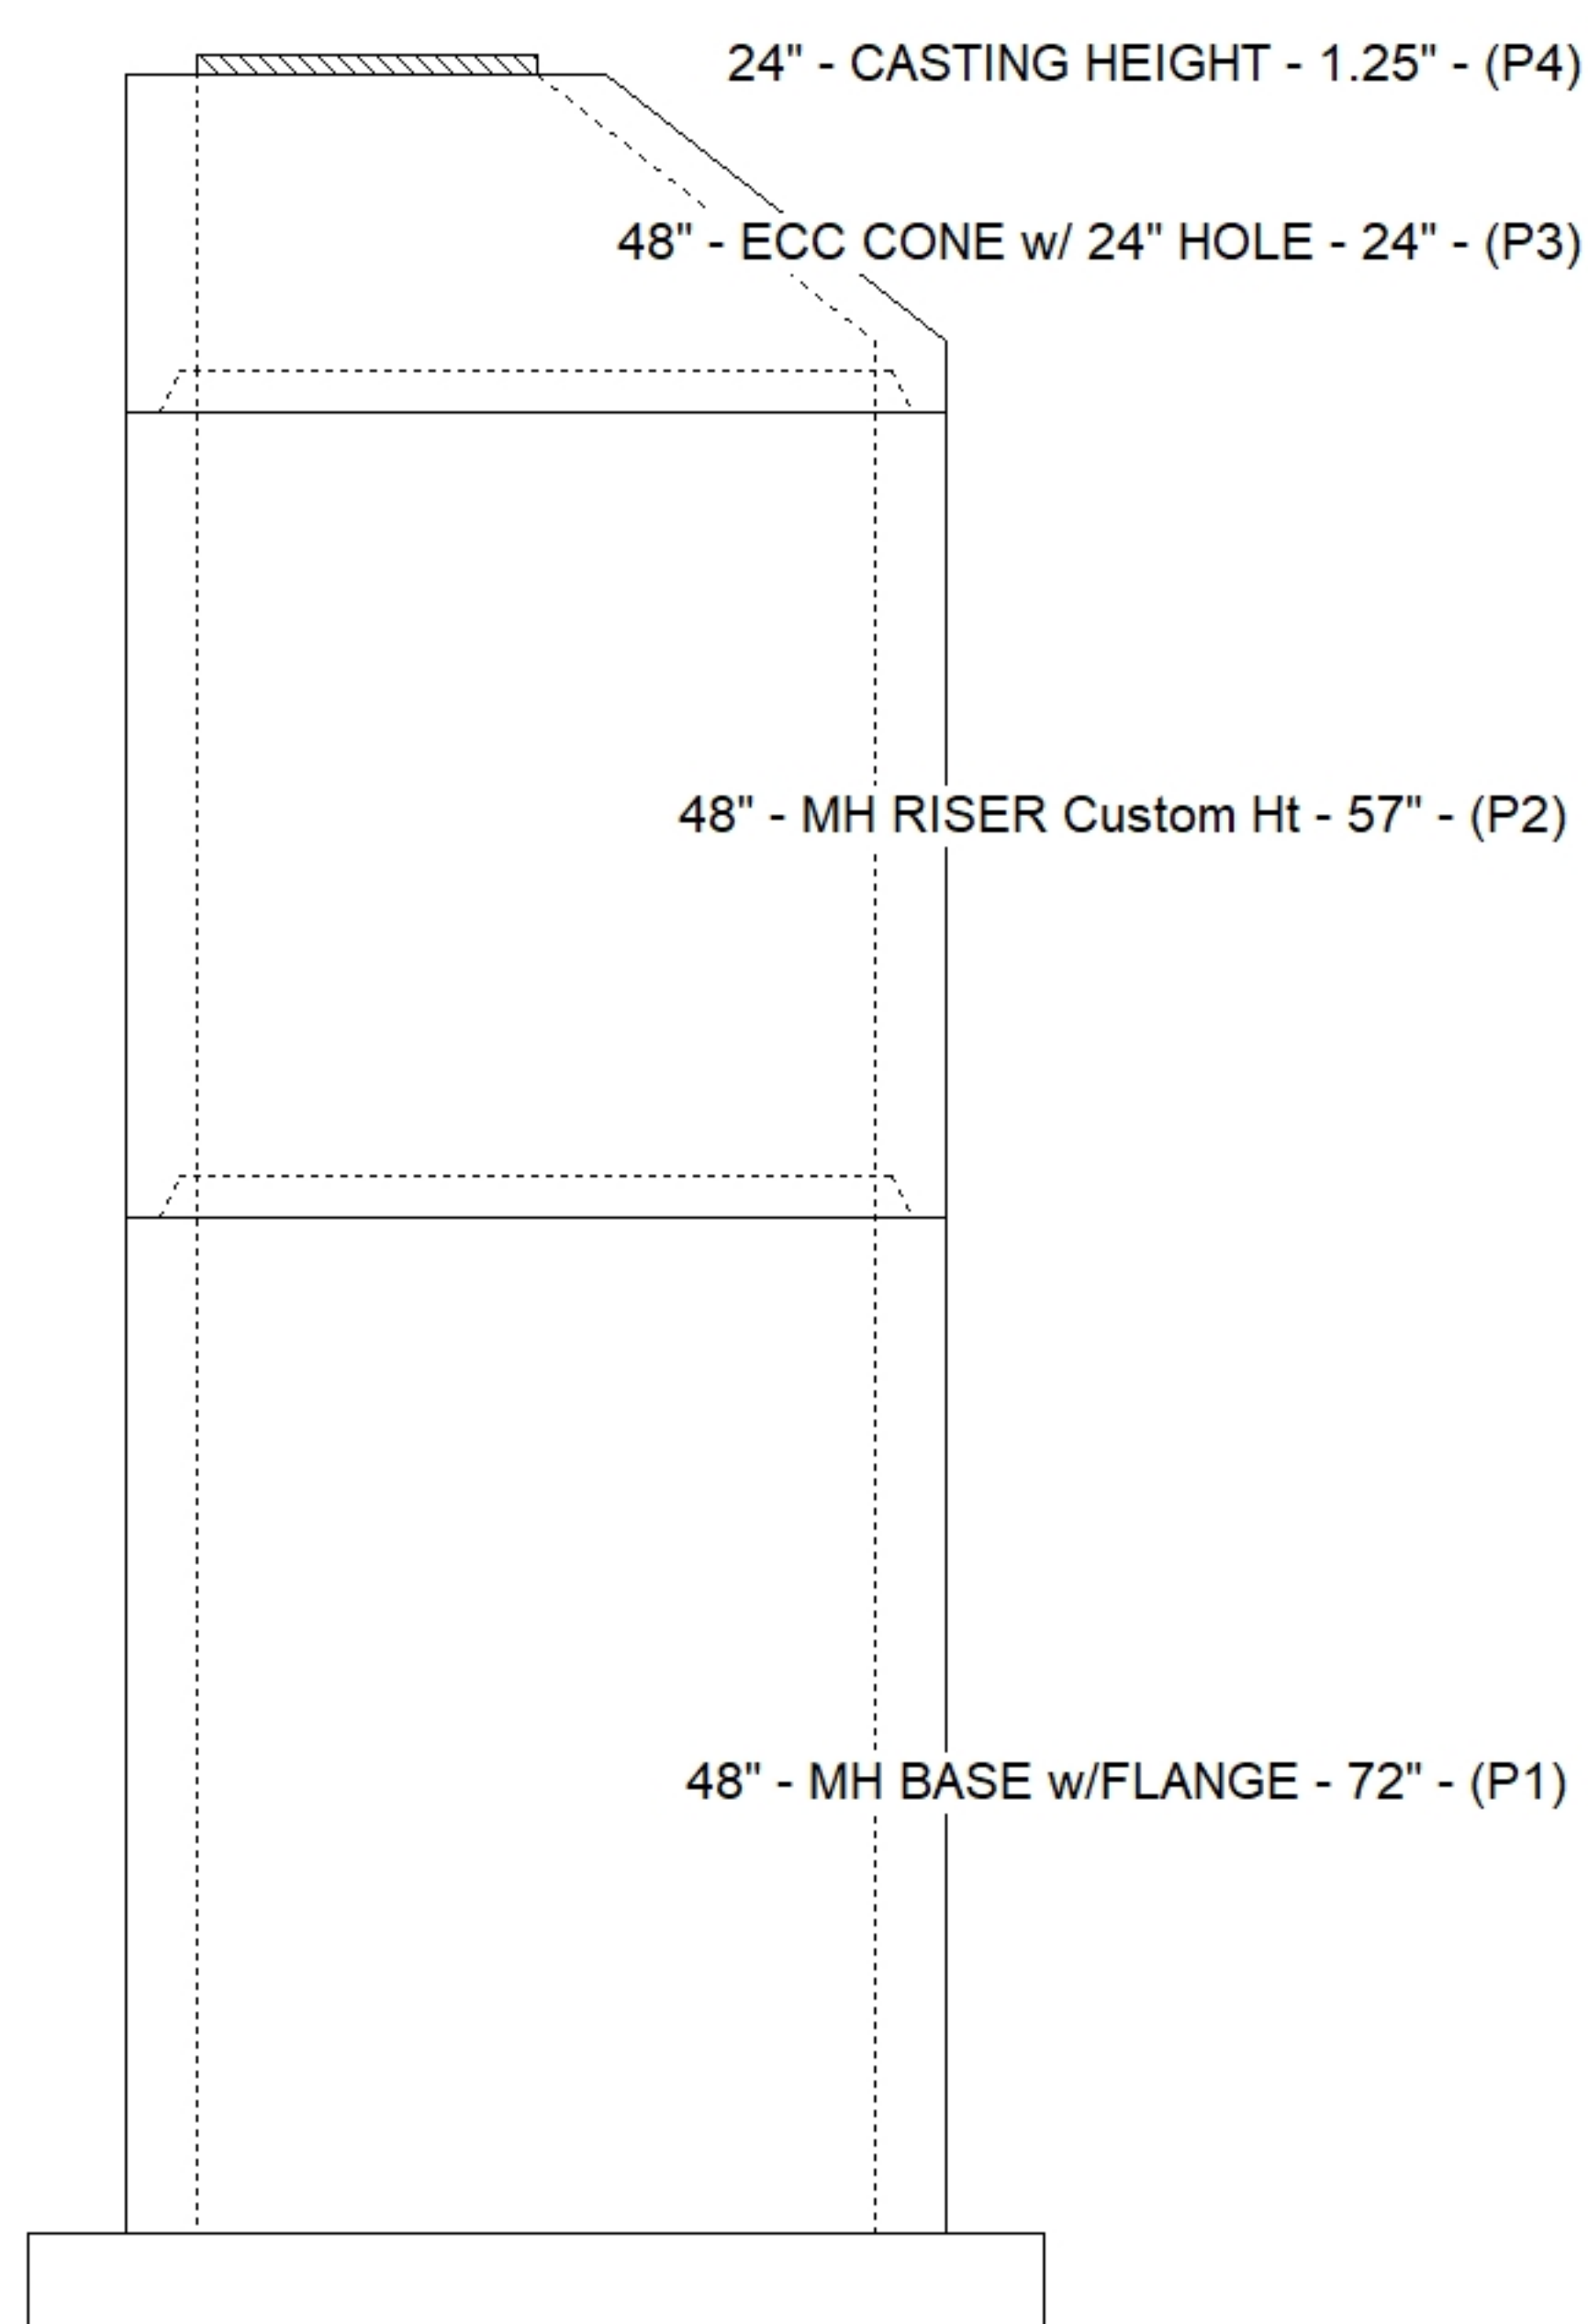

Default - Interior Dimensions

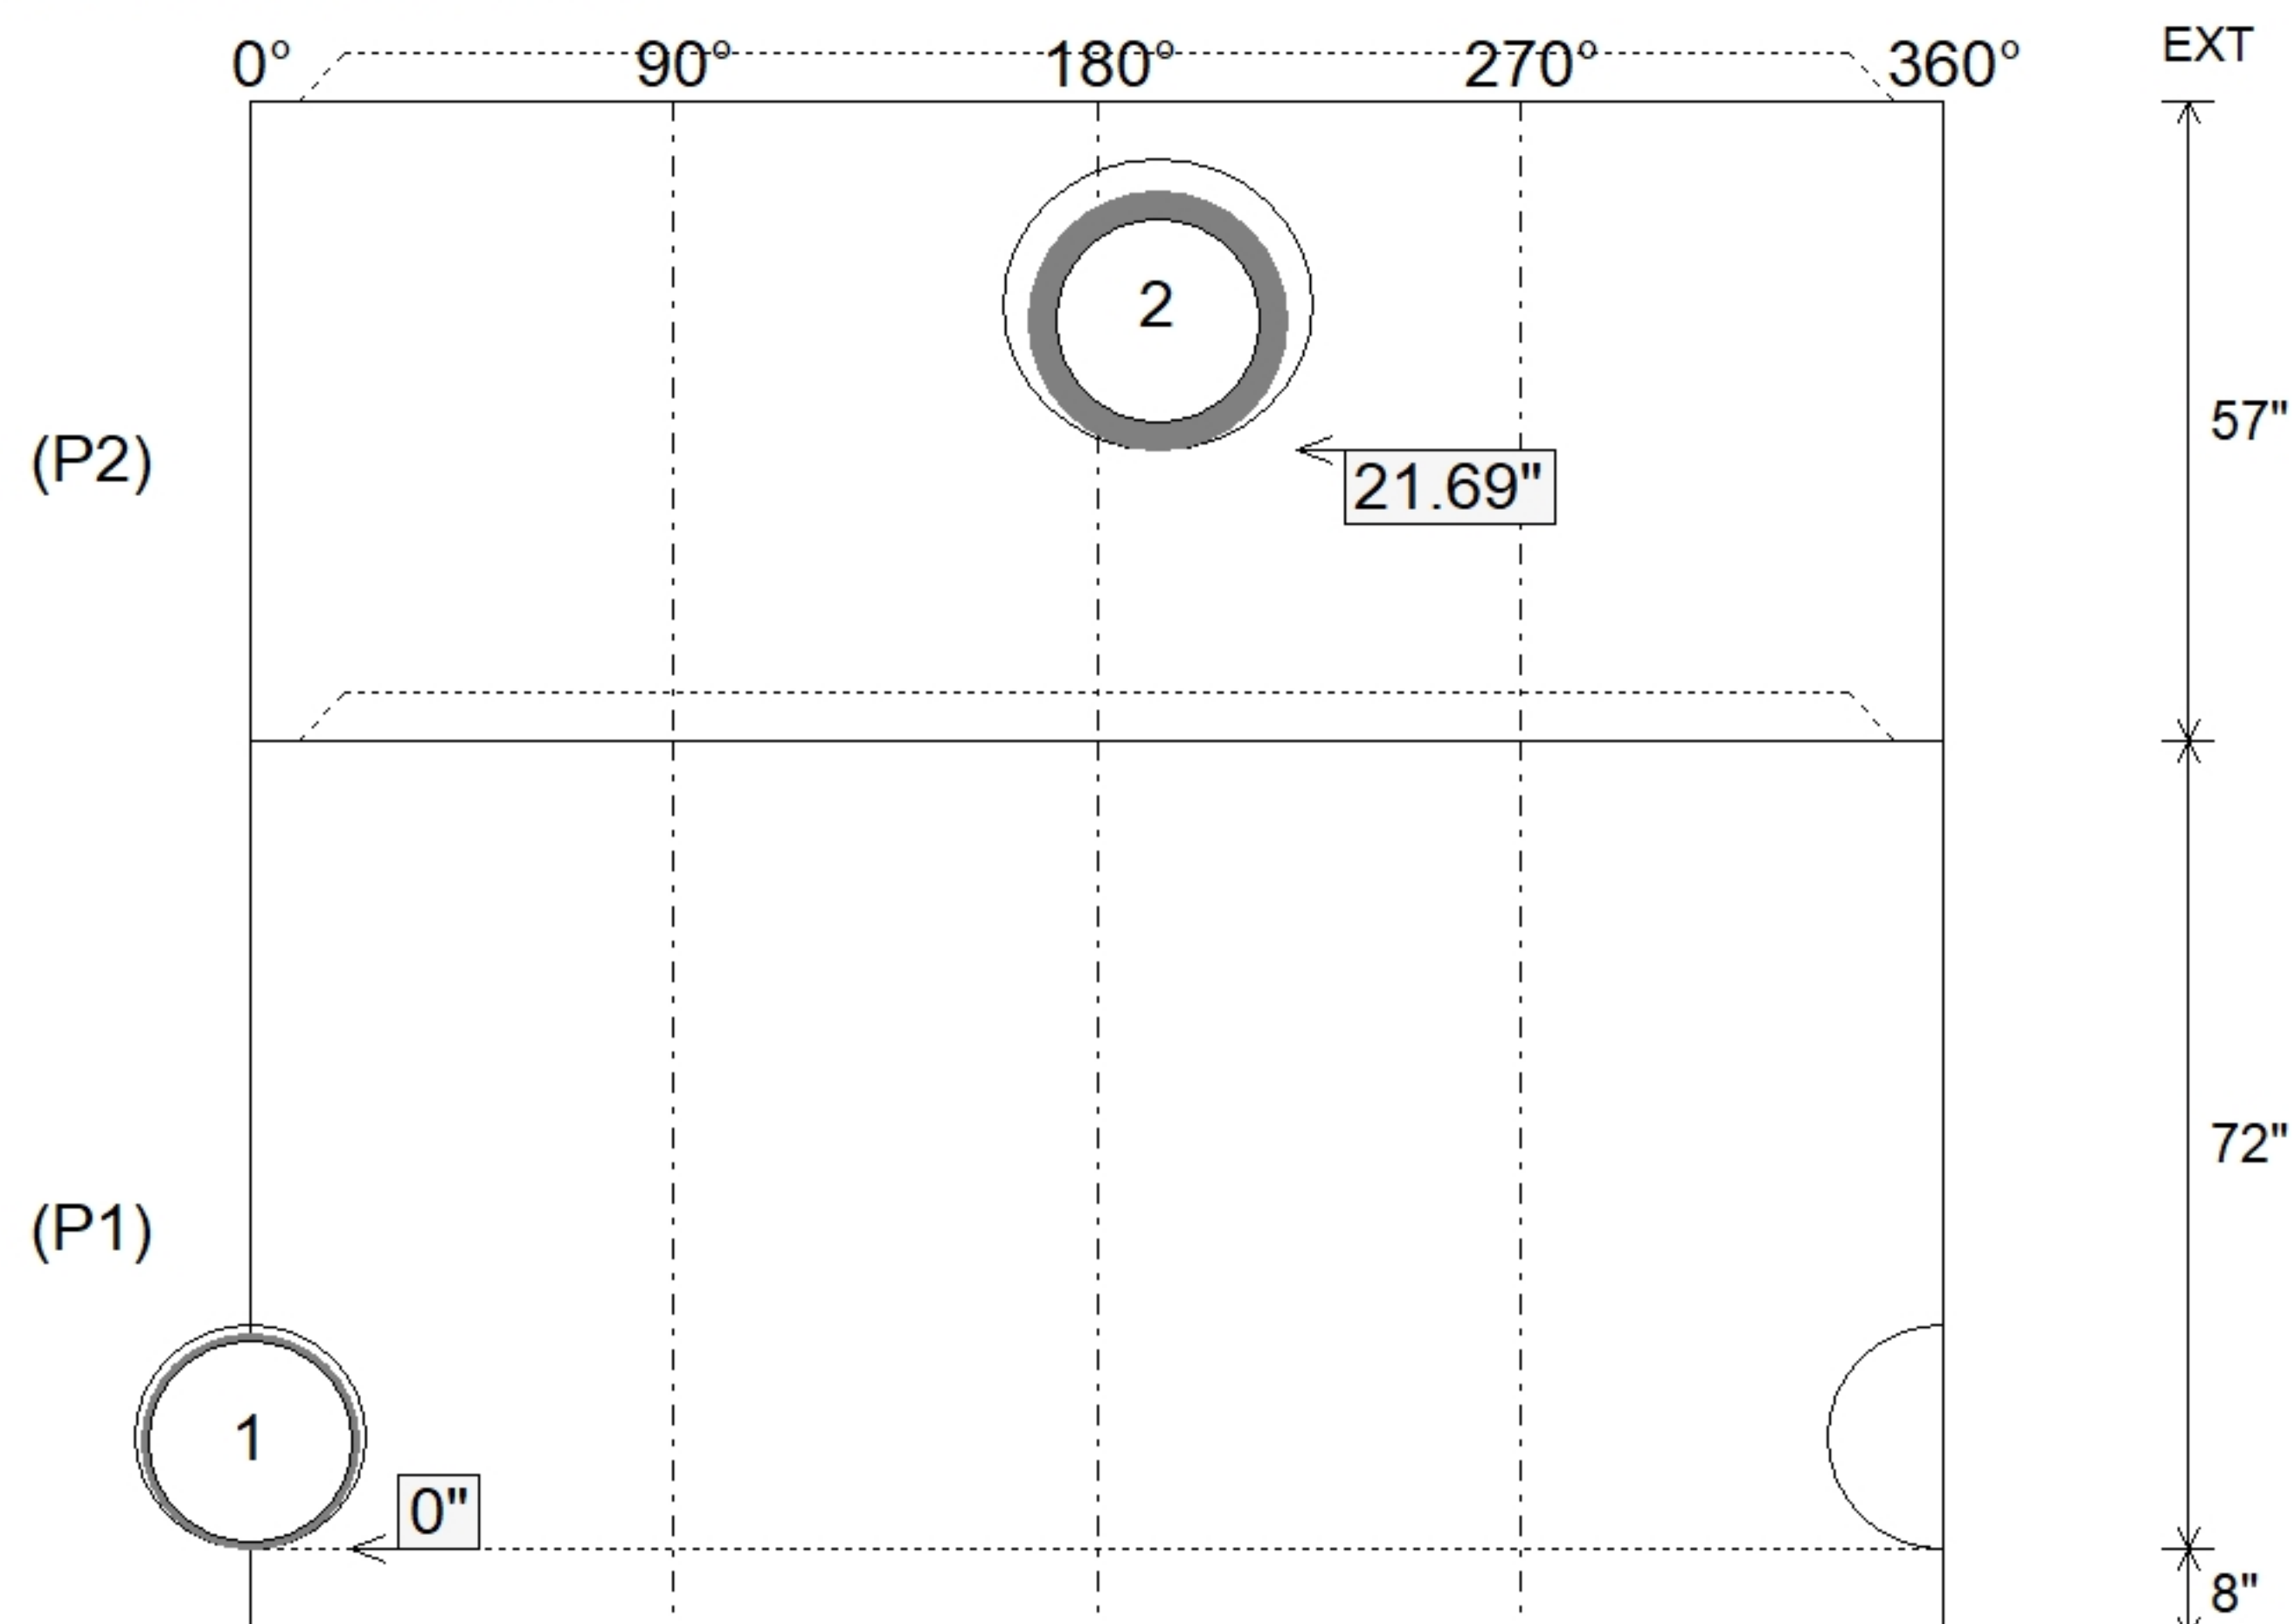

Submittal Drawing
9/3/2026 2:49:28 PM

SUBMITTAL
APPROVED BY:
