





Rim: 447.65'	Sump: 2"	Floor (Bot): 436.983'
Invert: 437.65'	Floor (Top): 437.483'	Overall Height: 10.583'
Rim to Invert: 10'	Floor Height: 6"	Slack: 1"

P4) 24" - CASTING HEIGHT - 7"	0 lb
P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red - 30"	1961 lb
P2) 48" - MH RISER SPECIAL w/ConBlock-CDA Red - 60"	4127 lb
P1) 48" - MH BASE w/ConBlock-CDA Red - 24"	2959 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT	1440 lb
1) CASTING - HOE MC-315 F/C Sanitary	258 lb
2) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) 24" - Conseal CS-102 1.00" (Double)	0 lb
1) PSX - 12-08 NYLO	8 lb
3) PSX - 8QRS-S NYLO	20 lb
10) MH Step ML-10-TDS-NCR - 10"	0 lb

Structure Total:	10773 lb

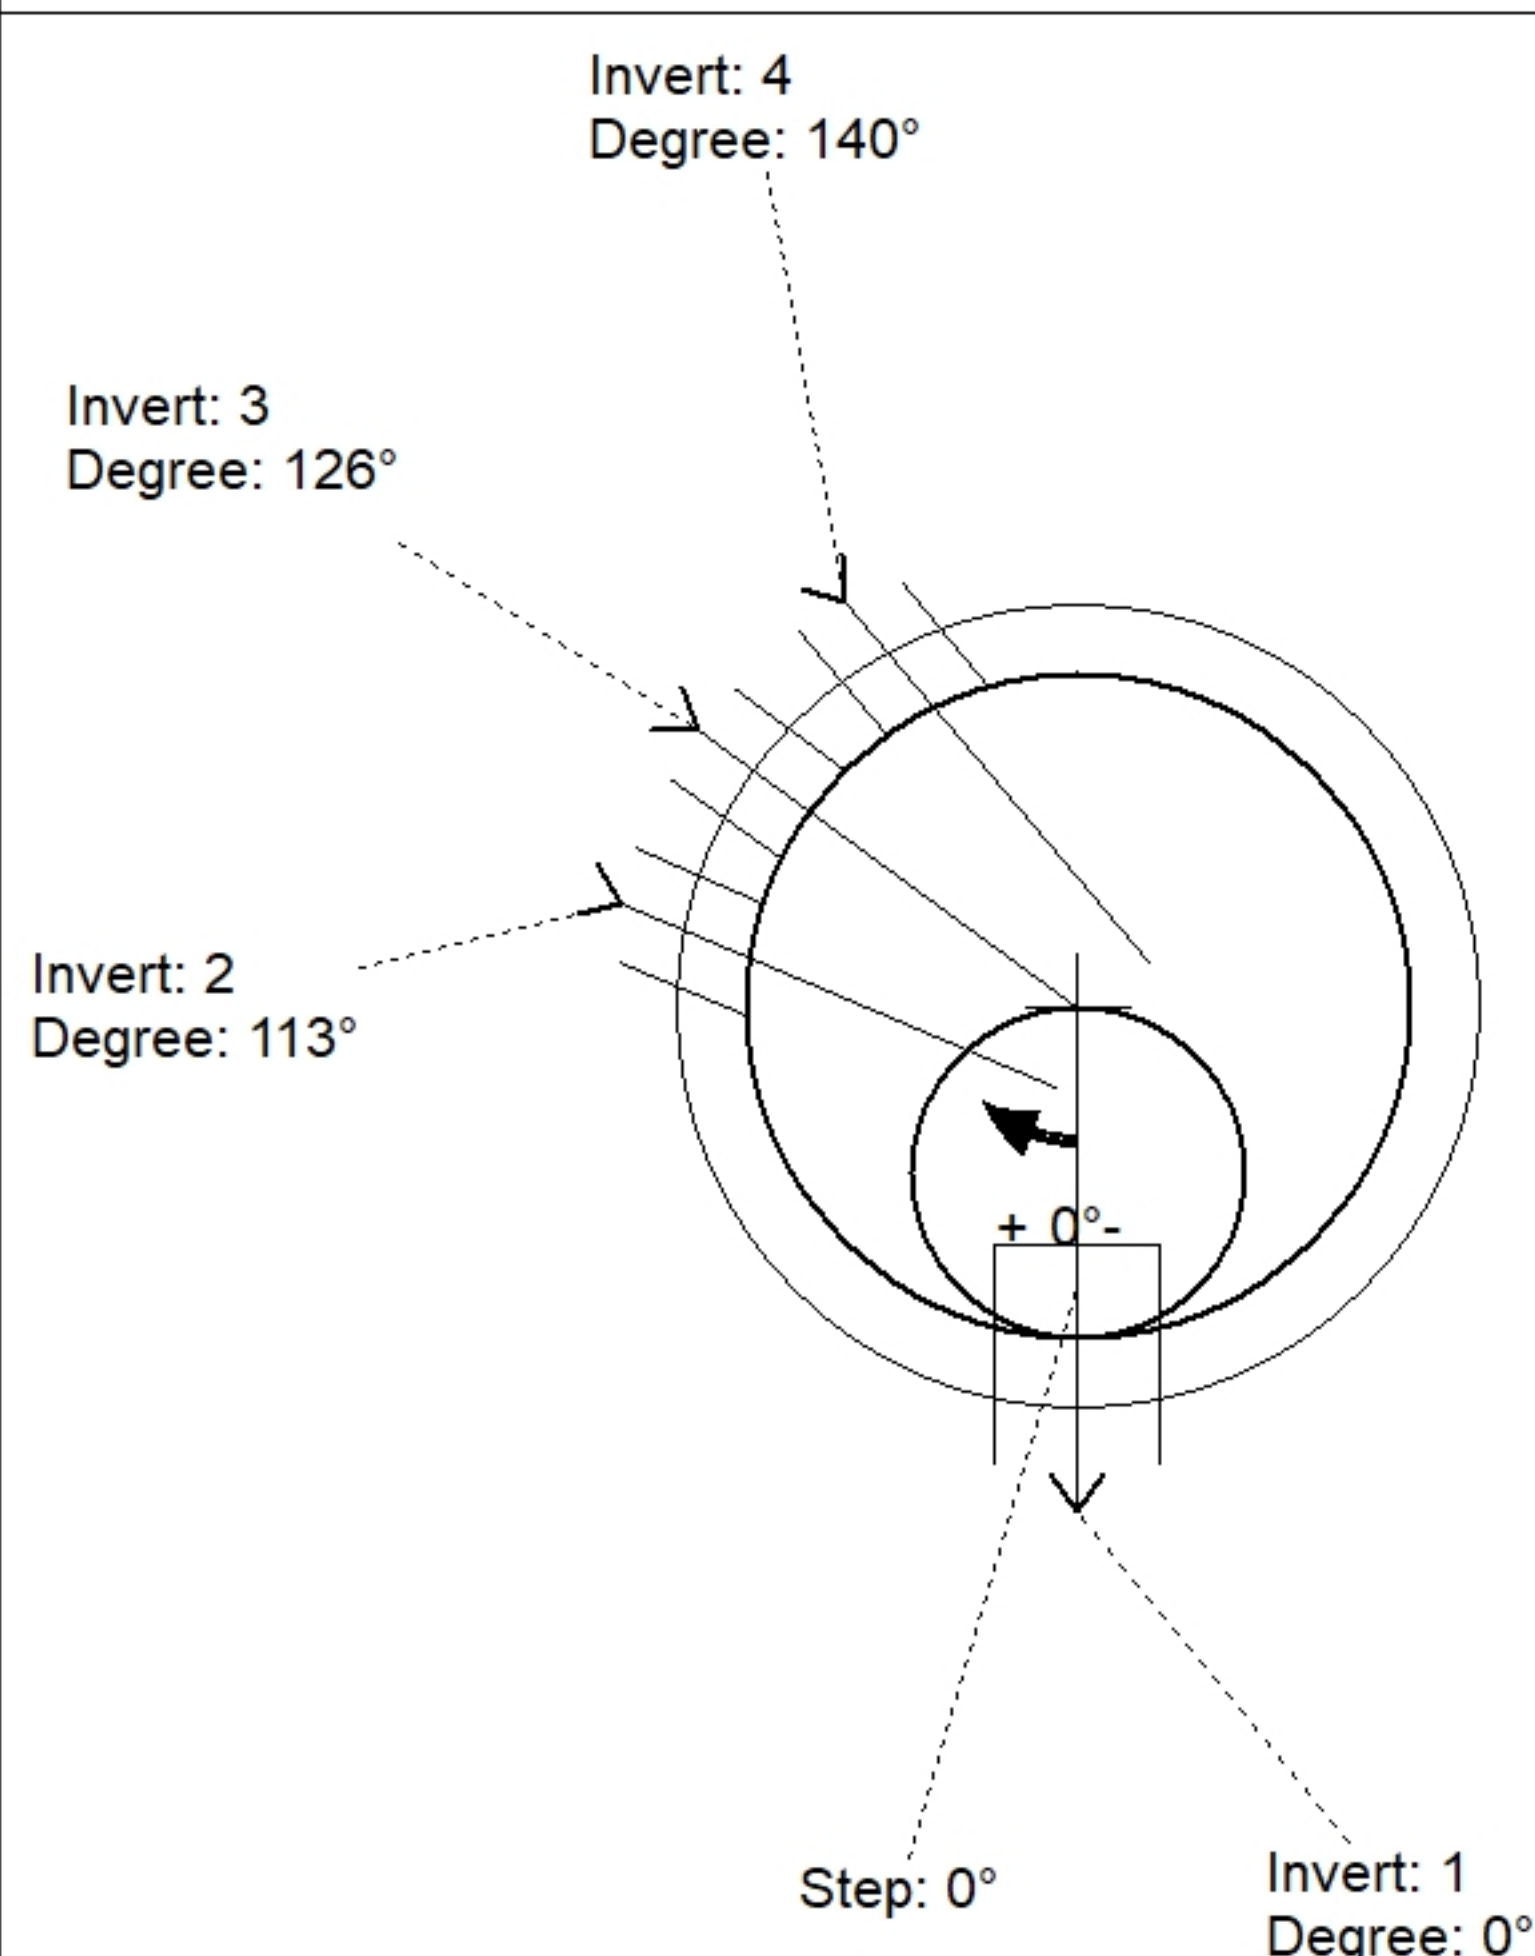

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌋)	Ref
Rim	447.65'							
Reducer								
Invert 1	437.65'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	442.61'	113°	2" PVC SDR21	2.375"	8"	PSX 8QRS-S NYLO	30.27"	P2
Invert 3	442.61'	126°	1.5" PVC SDR21	1.9"	8"	PSX 8QRS-S NYLO	30.13"	P2
Invert 4	442.61'	140°	2" PVC SDR21	2.375"	8"	PSX 8QRS-S NYLO	30.27"	P2
Invert 5								
Invert 6								
Invert 7								
Invert 8								

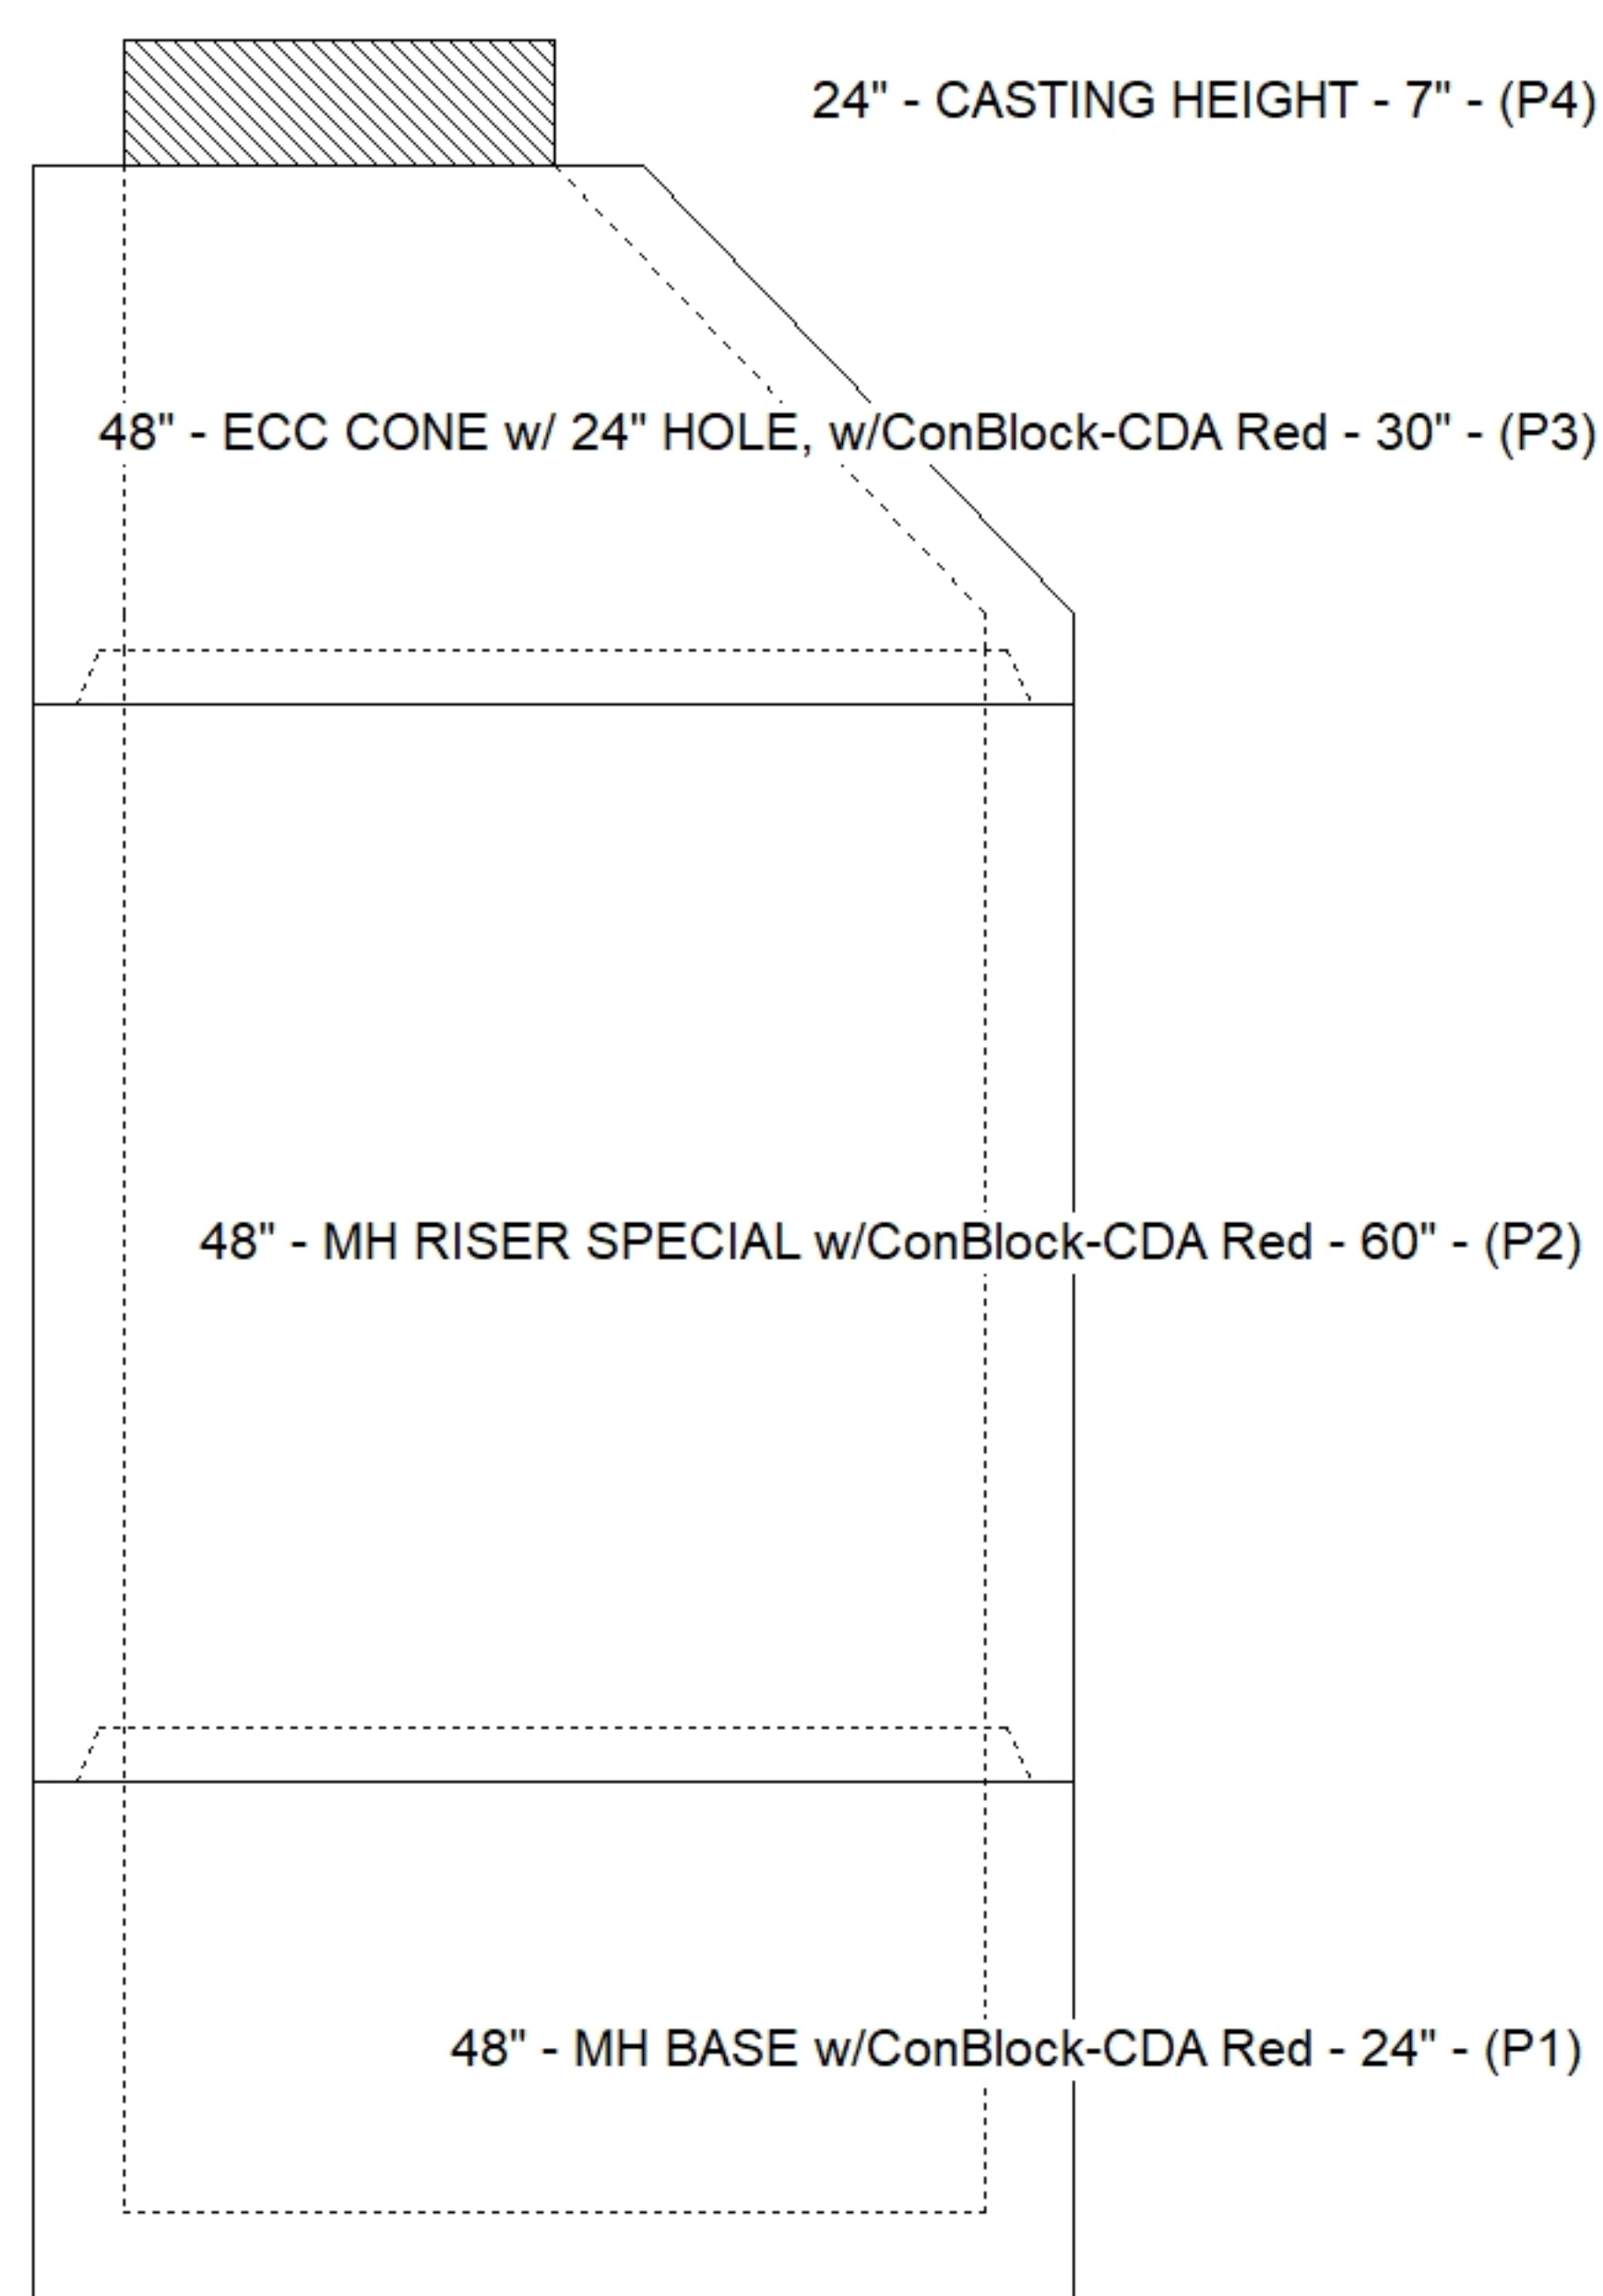

SUBMITTAL
APPROVED BY:
